




# NEXTer<sup>TM</sup> Energy Resources Ashtabula Wind II

## NEXTer<sup>TM</sup> Energy

### Plan of the Day (POD)



**Date:** Saturday, 8/15/2009  
**High:** 80  
**Precipitation Chances:** 55%

**COD:** 10-31-09  
**Low:** 56

**Days to COD:** 78  
**Winds:** SE @ 5 mph  
**Weather Forecast:** Cloudy

## NEXTer<sup>TM</sup> Energy Resources    Otter Tail    Blattner Energy    GE

#### Safety/Environmental:

- Keep hydrated
- Keep your speed to a minimum
- Watch out for blind corners in areas where corn is growing
- SWPPP inspection every two weeks

#### Civil/Erection:

#### Foundations:

- No work due to rain

#### Erection:

- No work due to rain

#### Collection:

#### Electrical:


- Contoller termination at 213-215
- Box pad installation at 165-168
- Tower wiring at 199-200
- Tower wiring pre-walk at 199-200
- IIP at 197
- Mechanical completion at 198-199

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	81	81	0
Grounding XFR	5	5	0
4/0 Cable	441,000	453,555	-12,555
500 KCM	36,000	37,036	-1,036
Copperclad	84,000	84,579	-579
1000 KCM	333,000	334,956	-1,956
12 Fiber SM FOC	270,000	270,650	-650
1000-2km (Low Voltage)	30,500	31,330	-830
XFR Box Pads	81	81	0
Controllers	80	80	0
Bases	80	80	0
Mids	80	80	0
Tops	80	80	0
Nacelles	80	80	0
Hubs	80	80	0
Blade Sets	80	80	0

Negative Number Indicates Overage of Cable

### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	71,364	117,188	60.9%
Gravel Roads (6")	68,738	117,188	58.7%
Roads Complete	60,930	117,188	52.0%
Silt Fence Installed	19,695	17,700	111.3%
Foundations Excavated	63	80	78.8%
Foundations Poured	50	80	62.5%
Foundations Backfilled	36	80	45.0%
Crane Pads Completed	33	80	41.3%
Tower Base Sections Erected	16	80	20.0%
Tower Mid Sections Erected	16	80	20.0%
Tower Top Sections Erected	11	80	13.8%
Nacelles Installed	11	80	13.8%
Rotors Installed	11	80	13.8%
Tower Wiring Complete	6	80	7.5%
Mechanically Complete	1	80	1.3%
Final Commissioned	0	80	0.0%
4/0 Cable Trenched	108,938	441,000	24.7%
500 Cable Trenched	19,934	36,000	55.4%
1000 Cable Trenched	115,168	333,000	34.6%
Copperclad	0	84,000	0.0%
1000 Low Voltage Installed	7875	30,500	25.8%
Fiber Optic 12 Fiber SM	71,475	270,000	26.5%
Transformers Set/Terminated	27	80	33.8%
(as of COB yesterday)			

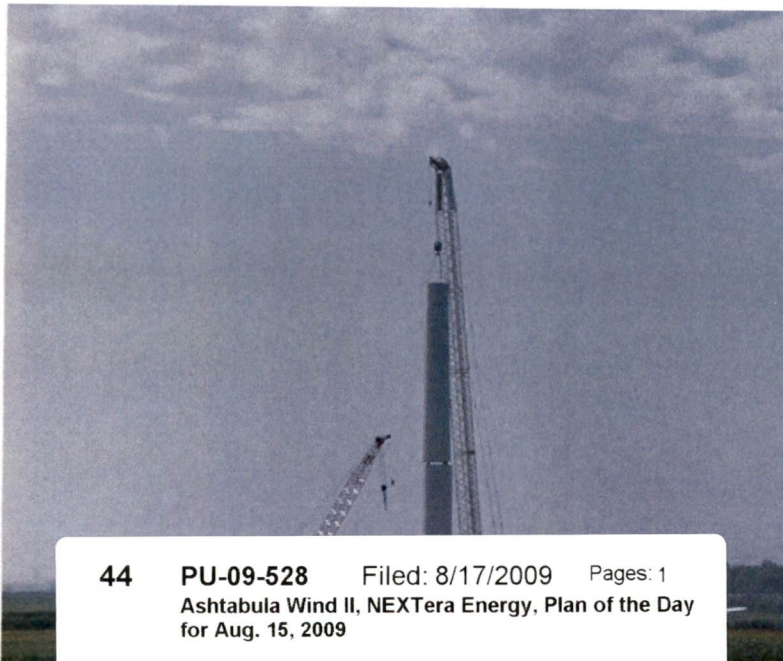

44    PU-09-528    Filed: 8/17/2009    Pages: 1  
 Ashtabula Wind II, NEXTer<sup>TM</sup> Energy, Plan of the Day  
 for Aug. 15, 2009

NextEra Energy Resources, LLC
