




NEXTerTM Energy Resources Ashtabula Wind II

NEXTerTM Energy

Plan of the Day (POD)



Date: Saturday, 8/22/2009
High: 78
Precipitation Chances: 0%

COD: 10-31-09
Low: 52

Days to COD: 71
Winds: S @ 3 mph
Weather Forecast: Partly Sunny

NEXTerTM Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Be aware of changing work conditions
- Keep your speed to a minimum
- SWPPP inspection every two weeks

Civil/Erection:

- Subgrade at 216-220

Foundations:

- Build crane pad at 172, 176, 177 & 240-244

Erection:

- Mobilizing crane to 193

Collection:

- High voltage cable termination at 191-193
- Low voltage cable termination at 213-215
- Boring at 10th St & 119th Ave

Electrical:

- Controllor termination at 167
- Box pad installation at 169-171 & 242
- PMT installation at 165-168
- Mechanical completion pre-walk at 182
- IIP at 183


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	81	81	0
Grounding XFR	5	5	0
4/0 Cable	441,000	453,555	-12,555
500 KCM	36,000	37,036	-1,036
Copperdad	84,000	84,579	-579
1000 KCM	333,000	337,803	-4,803
12 Fiber SM FOC	270,000	270,650	-650
1000-2km (Low Voltage)	30,500	31,330	-830
XFR Box Pads	81	81	0
Controllers	80	80	0
Bases	80	80	0
Mids	80	80	0
Tops	80	80	0
Nacelles	80	80	0
Hubs	80	80	0
Blade Sets	80	80	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	80,186	117,188	68.4%
Gravel Roads (6")	72,651	117,188	62.0%
Roads Complete	71,651	117,188	61.1%
Silt Fence Installed	19,695	17,700	111.3%
Foundations Excavated	72	80	90.0%
Foundations Poured	55	80	68.8%
Foundations Backfilled	49	80	61.3%
Crane Pads Completed	40	80	50.0%
Tower Base Sections Erected	22	80	27.5%
Tower Mid Sections Erected	22	80	27.5%
Tower Top Sections Erected	16	80	20.0%
Nacelles Installed	16	80	20.0%
Rotors Installed	16	80	20.0%
Tower Wiring Complete	14	80	17.5%
Mechanically Complete	6	80	7.5%
Pre-Commissioned	0	80	0.0%
Final Commissioned	0	80	0.0%
4/0 Cable Trenched	141,336	341,700	32.1%
500 Cable Trenched	19,934	36,000	55.4%
1000 Cable Trenched	136,546	333,000	41.0%
Copperdad	0	84,000	0.0%
1000 Low Voltage Installed	7875	30,500	25.8%
Fiber Optic 12 Fiber SM	71,475	270,000	26.5%
Transformers Set/Terminated	34	80	42.5%

(as of COB yesterday)

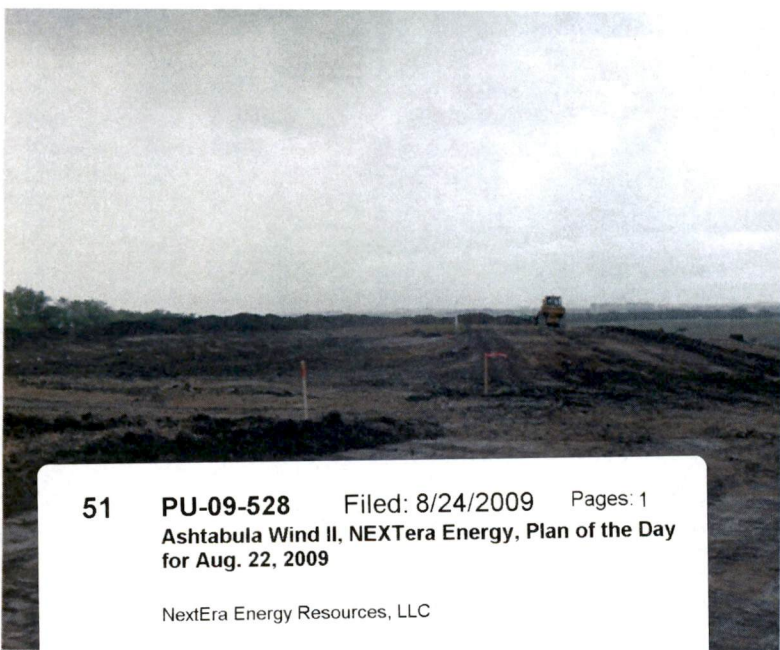

51 PU-09-528 Filed: 8/24/2009 Pages: 1
 Ashtabula Wind II, NEXTerTM Energy, Plan of the Day
 for Aug. 22, 2009

NextEra Energy Resources, LLC
