




# NEXTera™ Energy Resources Ashtabula Wind II

## NEXTera Energy

### Plan of the Day (POD)



**Date: Wednesday, 10/7/09**  
**High: 54**  
**Precipitation Chances: 25%**

**COD: 10-31-09**  
**Low: 30**

**Days to COD: 25**  
**Winds: SSW @ 5 mph**  
**Weather Forecast: Cloudy**

#### NEXTera™ Energy Resources    Otter Tail    Blattner Energy    GE

**Safety/Environmental:**

- Be aware of changing weather
- Have spotters when backing up large equipment
- Keep your speed to a minimum
- SWPPP inspection today

**Civil:**

- Reclaim topsoil

**Foundations:**

**Erection:**

**Collection:**

**Electrical:**

- GE Commissioning continuing

**Substation:**


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	81	81	0
Grounding XFR	5	5	0
4/0 Cable	441,000	453,555	-12,555
500 KCM	36,000	37,036	-1,036
Copperclad	84,000	84,579	-579
1000 KCM	333,000	337,803	-4,803
12 Fiber SM FOC	270,000	270,650	-650
1000-2km (Low Voltage)	30,500	31,330	-830
XFR Box Pads	81	81	0
Controllers	80	80	0
Bases	80	80	0
Mids	80	80	0
Tops	80	80	0
Nacelles	80	80	0
Hubs	80	80	0
Blade Sets	80	80	0

Negative Number Indicates Overage of Cable

#### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	88,996	117,188	100.0%
Gravel Roads (6")	88,996	117,188	100.0%
Roads Complete	88,996	117,188	100.0%
Silt Fence Installed	23,230	17,700	131.2%
Foundations Excavated	80	80	100.0%
Foundations Poured	80	80	100.0%
Foundations Backfilled	80	80	100.0%
Crane Pads Completed	80	80	100.0%
Tower Base Sections Erected	80	80	100.0%
Tower Mid Sections Erected	80	80	100.0%
Tower Top Sections Erected	80	80	100.0%
Nacelles Installed	80	80	100.0%
Rotors Installed	80	80	100.0%
Tower Wiring Complete	80	80	100.0%
Mechanically Complete	80	80	100.0%
Pre-Commissioned	6	80	7.5%
Final Commissioned	57	80	71.3%
4/0 Cable Trenched	381,576	441,000	100.0%
500 Cable Trenched	25,592	36,000	100.0%
1000 Cable Trenched	311,217	333,000	100.0%
Copperclad	92,586	84,000	100.0%
1000 Low Voltage Installed	30,001	30,500	100.0%
Fiber Optic 12 Fiber SM	217,276	270,000	100.0%
Transformers Set/Terminated	80	80	100.0%

(as of COB yesterday)

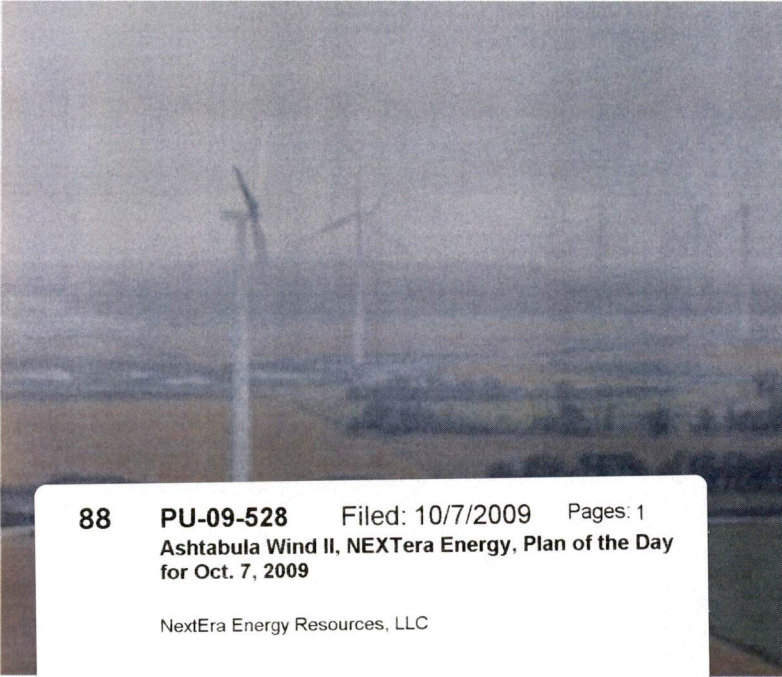

88    PU-09-528    Filed: 10/7/2009    Pages: 1  
 Ashtabula Wind II, NEXTera Energy, Plan of the Day  
 for Oct. 7, 2009  
 NextEra Energy Resources, LLC
