




# NEXtera™ Energy Resources Ashtabula Wind II

## NEXtera Energy

### Plan of the Day (POD)



**Date: Friday, 10/9/09**  
**High: 44**  
**Precipitation Chances: 5%**

**COD: 10-31-09**  
**Low: 20**

**Days to COD: 23**  
**Winds: SW @ 2 mph**  
**Weather Forecast: Partly Sunny**

#### NEXtera™ Energy Resources    Otter Tail    Blattner Energy    GE

**Safety/Environmental:**

- **Be aware of changing weather**
- **Hunting has started; watch out for hunters & animals on the roads**
- **Keep your speed to a minimum**
- **SWPPP inspection every two weeks**

**Civil:**

- **Reclaim topsoil**

**Foundations:**

**Erection:**

**Collection:**

**Electrical:**

- **GE Commissioning continuing**


**Substation:**

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	81	81	0
Grounding XFR	5	5	0
4/0 Cable	441,000	453,555	-12,555
500 KCM	36,000	37,036	-1,036
Copperclad	84,000	84,579	-579
1000 KCM	333,000	337,803	-4,803
12 Fiber SM FOC	270,000	270,650	-650
1000-2km (Low Voltage)	30,500	31,330	-830
XFR Box Pads	81	81	0
Controllers	80	80	0
Bases	80	80	0
Mids	80	80	0
Tops	80	80	0
Nacelles	80	80	0
Hubs	80	80	0
Blade Sets	80	80	0

Negative Number Indicates Overage of Cable

#### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	88,996	117,188	100.0%
Gravel Roads (6")	88,996	117,188	100.0%
Roads Complete	88,996	117,188	100.0%
Silt Fence Installed	23,230	17,700	131.2%
Foundations Excavated	80	80	100.0%
Foundations Poured	80	80	100.0%
Foundations Backfilled	80	80	100.0%
Crane Pads Completed	80	80	100.0%
Tower Base Sections Erected	80	80	100.0%
Tower Mid Sections Erected	80	80	100.0%
Tower Top Sections Erected	80	80	100.0%
Nacelles Installed	80	80	100.0%
Rotors Installed	80	80	100.0%
Tower Wiring Complete	80	80	100.0%
Mechanically Complete	80	80	100.0%
Pre-Commissioned	6	80	100.0%
Final Commissioned	68	80	85.0%
4/0 Cable Trenched	381,576	441,000	100.0%
500 Cable Trenched	25,592	36,000	100.0%
1000 Cable Trenched	311,217	333,000	100.0%
Copperclad	92,586	84,000	100.0%
1000 Low Voltage installed	30,001	30,500	100.0%
Fiber Optic 12 Fiber SM	217,276	270,000	100.0%
Transformers Set/Terminated	80	80	100.0%
(as of COB yesterday)			

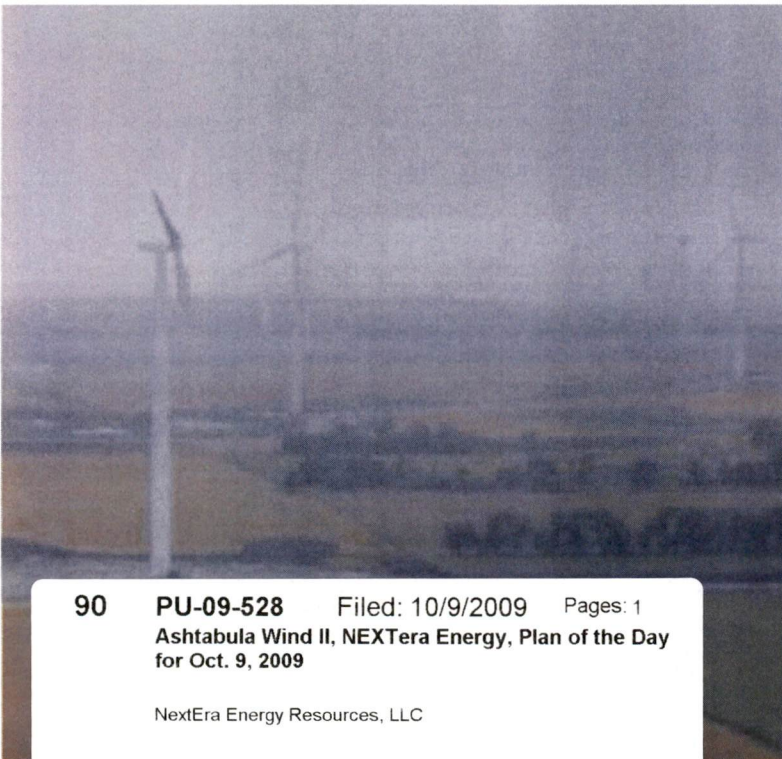

90    PU-09-528    Filed: 10/9/2009    Pages: 1  
 Ashtabula Wind II, NEXtera Energy, Plan of the Day  
 for Oct. 9, 2009

NextEra Energy Resources, LLC
