




# NEXTer<sup>TM</sup> Energy Resources Ashtabula Wind II

## NEXTer<sup>TM</sup> Energy

### Plan of the Day (POD)



**Date:** Saturday, 10/10/09  
**High:** 39  
**Precipitation Chances:** 25%

**COD:** 10-31-09  
**Low:** 18

**Days to COD:** 22  
**Winds:** WSW @ 13 mph  
**Weather Forecast:** Mostly Cloudy

#### NEXTer<sup>TM</sup> Energy Resources    Otter Tail    Blattner Energy    GE

**Safety/Environmental:**

- Be aware of changing weather
- Hunting has started; watch out for hunters & animals on the roads
- Keep your speed to a minimum
- SWPPP inspection every two weeks

**Civil:**

**Foundations:**

**Erection:**

**Collection:**

**Electrical:**

- GE Commissioning continuing

**Substation:**


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	81	81	0
Grounding XFR	5	5	0
4/0 Cable	441,000	453,555	-12,555
500 KCM	36,000	37,036	-1,036
Copperclad	84,000	84,579	-579
1000 KCM	333,000	337,803	-4,803
12 Fiber SM FOC	270,000	270,650	-650
1000-2km (Low Voltage)	30,500	31,330	-830
XFR Box Pads	81	81	0
Controllers	80	80	0
Bases	80	80	0
Mids	80	80	0
Tops	80	80	0
Nacelles	80	80	0
Hubs	80	80	0
Blade Sets	80	80	0

Negative Number Indicates Overage of Cable

#### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	88,996	117,188	100.0%
Gravel Roads (6")	88,996	117,188	100.0%
Roads Complete	88,996	117,188	100.0%
Silt Fence Installed	23,230	17,700	131.2%
Foundations Excavated	80	80	100.0%
Foundations Poured	80	80	100.0%
Foundations Backfilled	80	80	100.0%
Crane Pads Completed	80	80	100.0%
Tower Base Sections Erected	80	80	100.0%
Tower Mid Sections Erected	80	80	100.0%
Tower Top Sections Erected	80	80	100.0%
Nacelles Installed	80	80	100.0%
Rotors Installed	80	80	100.0%
Tower Wiring Complete	80	80	100.0%
Mechanically Complete	80	80	100.0%
Pre-Commissioned	6	80	100.0%
Final Commissioned	74	80	92.5%
4/0 Cable Trenched	381,576	441,000	100.0%
500 Cable Trenched	25,592	36,000	100.0%
1000 Cable Trenched	311,217	333,000	100.0%
Copperclad	92,586	84,000	100.0%
1000 Low Voltage installed	30,001	30,500	100.0%
Fiber Optic 12 Fiber SM	217,276	270,000	100.0%
Transformers Set/Terminated	80	80	100.0%

(as of COB yesterday)

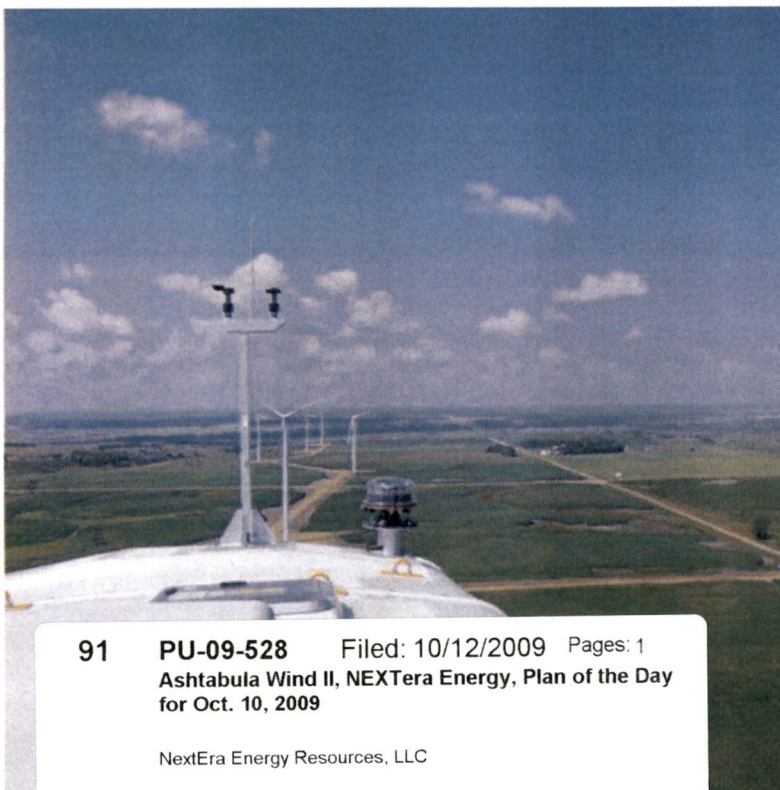

91    PU-09-528    Filed: 10/12/2009    Pages: 1  
 Ashtabula Wind II, NEXTer<sup>TM</sup> Energy, Plan of the Day  
 for Oct. 10, 2009

NextEra Energy Resources, LLC
