

**Plan of the Day (POD)**

**Date:** Friday, 8-6-10

**High:** 86

**Precipitation Chances:** 5%

**COD:** 11-30-10

**Low:** 58

**Weather Forecast:** Mostly Sunny

**Days to COD:** 117

**Winds:** S @ 7 mph

**NextEra™ Energy Resources**

**Blattner Energy**

**Paradigm**

**GE**

**Safety/Environmental:**

- Obey traffic guidelines & speed limits
- Be aware of heat effects
- Use caution working on haul roads
- Fence off wetland near turbines 53
- Installing silt fence

**Civil/Erection:**

- Subgrade string road 60-64
- Gravel yard
- Approach at 60-64 & 57-59

**Foundations:**

**Collection:**

- Staking collection route
- Locating bore locations

**Electrical:**

**Substation:**

- Strip substation
- Tie rebar cages

**Upcoming Events/Outstanding Issues:**


**RECEIVING (As of COB yesterday)**

	Total	Received	Balance
PMT XFR	65	62	3
Grounding XFR	6	0	6
4/0 Cable	519,519	200,907	318612
500 KCM	51,002	39,635	11367
Copperclad	65,280	73,906	-8626
1000 KCM	254,661	105,811	148850
1000 KCM LVC	24,000	40,730	-16730
12 Fiber SM FOC	289,504	336,530	-47026
XFR Box Pads	64	20	44
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

**Negative Number Indicates Overage of Cable**

**General Construction Status**

	Complete	Total	% Complete
Roads Subgraded	3,528	99,651	3.5%
Roads Built	0	99,651	0.0%
Silt Fence Installed	308	11,417	2.7%
Foundations Excavated	0	64	0.0%
Foundations Poured and Backfilled	0	64	0.0%
Crane Pads Completed	0	64	0.0%
Tower Base Sections Erected	0	64	0.0%
Tower Mid Sections Erected	0	64	0.0%
Tower Top Sections Erected	0	64	0.0%
Nacelles Installed	0	64	0.0%
Rotors Installed	0	64	0.0%
Tower Wiring Complete	0	64	0.0%
Final Commissioned	0	64	0.0%
Underground Trenching Installed (ft)	0		0.0%
(as of COB yesterday)			

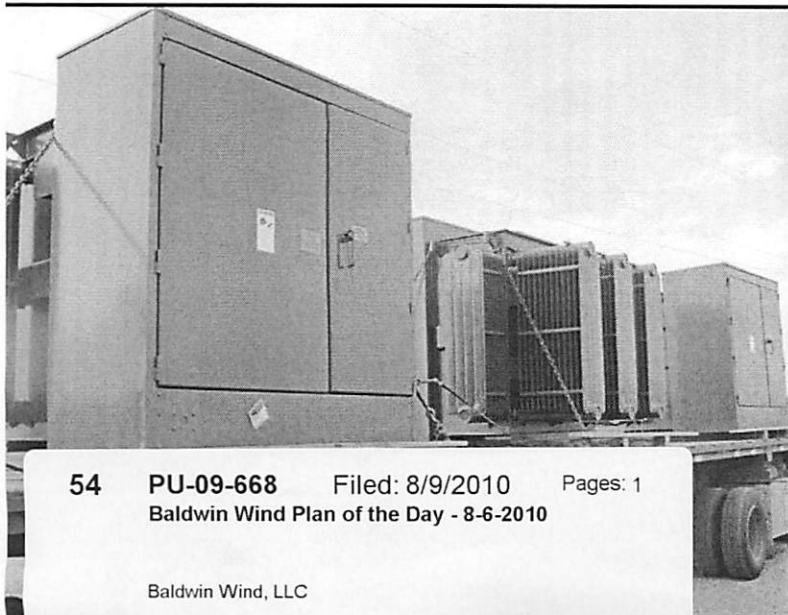

54 PU-09-668 Filed: 8/9/2010 Pages: 1

Baldwin Wind Plan of the Day - 8-6-2010

Baldwin Wind, LLC

DeeDee Olson
