

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Wednesday, 9-8-10
 High: 70
 Precipitation Chances: 10%

COD: 11-30-10
 Low: 50

Days to COD: 84
 Winds: SE @ 18 mph
 Weather Forecast: Partly Sunny

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----


- Safety/Environmental:**
- Inspect rigging before and after picks
 - Stay focused on surroundings and possible hazards
 - Fence off wetland as needed
 - Installing silt fence
- Civil/Erection:**
- Subgrade at 8-14
 - Gravel at 17-20
- Foundations:**
- Foundation excavation at 17 & 21
 - Pour mud mats 17 & 20
 - Install bottom rebar mat at 28 & 30
 - Install anchor bolts at 51-52
 - Install top rebar mat at 50-52
 - Form base at 50-51
 - Pour base at 49-51
 - Form pedestal at 47-48
 - Pour pedestal at 47-48
 - Backfill at 32-33
 - Build crane at 32-33
- Collection:**
- Trench and install 4/0 at JB902-G910 & G708-SP705
 - Underground splicing at SP902 & SP905
 - Setting box pad at 53-56
 - Low voltage wire at 57
 - Terminate controllers at 62-63
 - Ground grid testing at 53-55
- Substation:**
- Install control conduit
 - Steel erection
 - Switch assembly

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	0	6
4/0 Cable	519,519	266,898	252,621
500 KCM	51,002	45,835	5,167
Copperclad	65,280	91,994	-26,714
1000 KCM	254,661	219,795	34,866
1000 KCM LVC	24,000	38,230	-14,230
12 Fiber SM FOC	289,504	329,530	-40,026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	58,264	99,651	58.5%
Roads Built	46,885	99,651	47.0%
Silt Fence Installed	2,274	11,417	19.9%
Foundations Excavated	41	64	64.1%
Foundations Poured	27	64	42.2%
Foundations Backfilled	14	64	21.9%
Crane Pads Completed	14	64	21.9%
Tower Base Sections Erected	0	64	0.0%
Tower Mid Sections Erected	0	64	0.0%
Tower Top Sections Erected	0	64	0.0%
Nacelles Installed	0	64	0.0%
Rotors Installed	0	64	0.0%
Tower Wiring Complete	0	64	0.0%
Mechanically Complete	0	64	0.0%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	29,722	157,430	18.9%
500 Cable Trenched	0	15,455	0.0%
1000 Cable Trenched	54,880	77,170	71.1%
Transformers Set/Terminated	2	64	3.1%
(as of COB yesterday)			

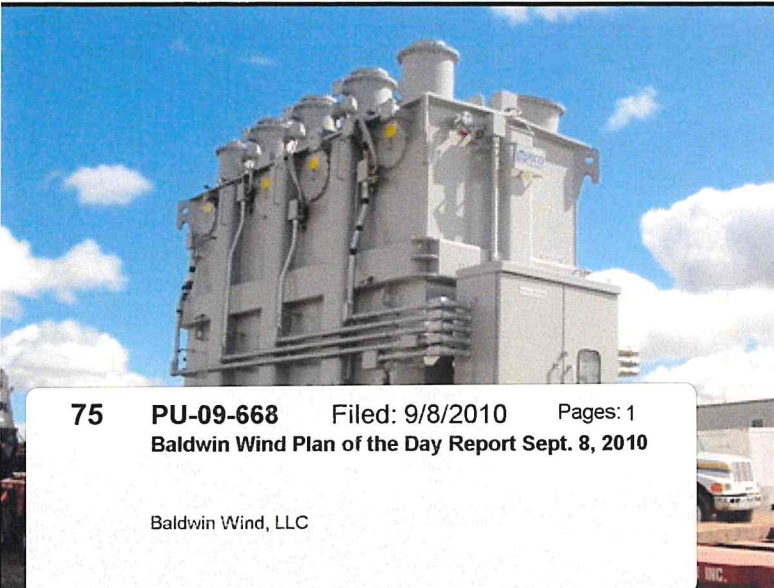

75 PU-09-668 Filed: 9/8/2010 Pages: 1
 Baldwin Wind Plan of the Day Report Sept. 8, 2010

Baldwin Wind, LLC
