

**Baldwin Wind, LLC**

**Plan of the Day (POD)**

Date: Thursday, 9-9-10  
High: 73  
Precipitation Chances: 40%

COD: 11-30-10  
Low: 54

Days to COD: 83  
Winds: SE @ 21 mph  
Weather Forecast: Cloudy

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----

**Safety/Environmental:**

- - 
  - 
  - 
  - Erect base at 61
  - Erect mid at 60-61
- Foundations:**
- Foundation excavation at 21-22
  - Pour mud mats 21-22
  - Install bottom rebar mat at 28 & 31
  - Install anchor bolts at 28 & 30
  - Install top rebar mat at 28 & 30
  - Form base at 28 & 30
  - Pour base at 30 & 52
  - Form pedestal at 49-51
  - Pour pedestal at 49-51
  - Backfill at 33-34
  - Build crane at 33-34


- Collection:**
- Trench and install 4/0 at G909-WTG28 & SP705-JB72
  - Underground splicing at SP902 & SP905
  - Setting transformers at 57-59
  - Low voltage wire at 53, 54 & 56
  - Terminate controllers at 64
  - Ground grid testing at 33 & 38
- Substation:**
- Install control conduit
  - Steel erection
  - Switch assembly
  - Bus Fabrication

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	0	6
4/0 Cable	519,519	288,836	230683
500 KCM	51,002	45,835	5167
Copperclad	65,280	91,994	-26714
1000 KCM	254,661	222,895	31766
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	329,530	-40026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

**General Construction Status**

	Complete	Total	% Complete
Roads Subgraded	59,914	99,651	60.1%
Roads Built	49,356	99,651	49.5%
Silt Fence Installed	2,274	11,417	19.9%
Foundations Excavated	43	64	67.2%
Foundations Poured	29	64	45.3%
Foundations Backfilled	15	64	23.4%
Crane Pads Completed	15	64	23.4%
Tower Base Sections Erected	1	64	1.6%
Tower Mid Sections Erected	0	64	0.0%
Tower Top Sections Erected	0	64	0.0%
Nacelles Installed	0	64	0.0%
Rotors Installed	0	64	0.0%
Tower Wiring Complete	0	64	0.0%
Mechanically Complete	0	64	0.0%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	37,059	157,430	23.5%
500 Cable Trenched	0	15,455	0.0%
1000 Cable Trenched	54,880	77,170	71.1%
Transformers Set/Terminated	4	64	6.3%
(as of COB yesterday)			

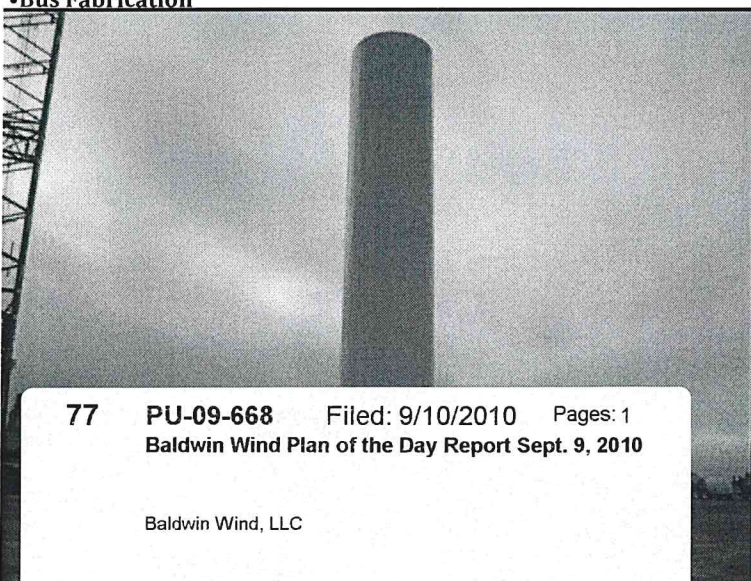

77 PU-09-668 Filed: 9/10/2010 Pages: 1  
Baldwin Wind Plan of the Day Report Sept. 9, 2010

Baldwin Wind, LLC
