

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Thursday, 9-16-10
High: 70
Precipitation Chances: 25%

COD: 11-30-10
Low: 42

Days to COD: 76
Winds: SSW @ 14 mph
Weather Forecast: Partly Sunny

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----

Safety/Environmental:

-
-
-

Civil/Erection:

- Subgrade at 24-26
- Gravel at 10-12 & 8
- Approach at 26
- Rotor assembly at 58-59
- Erect base and mid at 57-59
- Erect top, nacelle & rotor at 64

Foundations:


- Foundation excavation at 5-6 & 24
- Pour mud mats 5-6
- Install bottom rebar mat at 14-15
- Install anchor bolts at 9 & 15
- Install top rebar mat at 9 & 23
- Form base at 9 & 23
- Pour base at 22-23
- Form pedestal at 20-21
- Pour pedestal at 20-21
- Backfill at 43-44 & 4 -48
- Build crane at 43-44 & 4 -48

Collection:

- Trench and install 4/0 at SP602- JB6
- Trench and install 000 at G 08 - JB -2
- Setting transformer box pads at 4 -43
- Ground grid testing at 3 -40
- Terminating LV at 54 and HV at 54-56
- Tower wiring at 6 -62

Substation:

- Install grounding grid
- Torque and level all steel
- Bus Fabrication

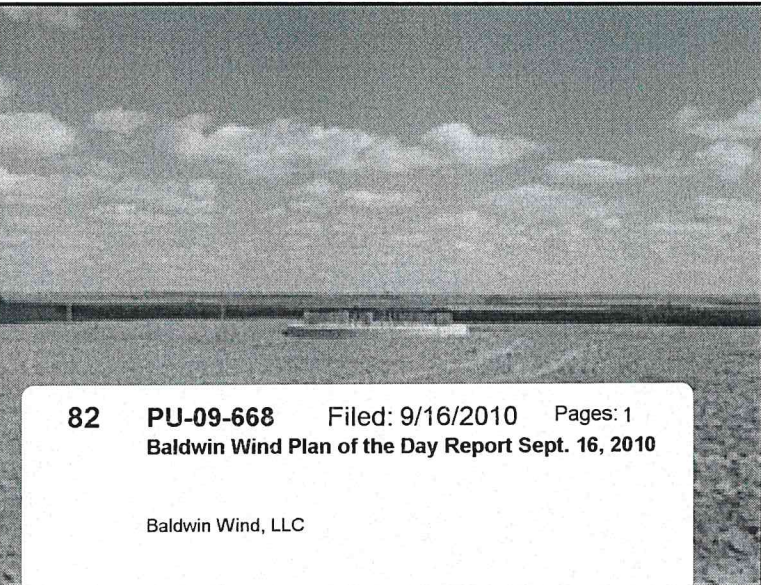

82 PU-09-668 Filed: 9/16/2010 Pages: 1
Baldwin Wind Plan of the Day Report Sept. 16, 2010

Baldwin Wind, LLC

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	0	6
4/0 Cable	519,519	457,289	62,230
500 KCM	51,002	67,700	-16,698
Copperclad	65,280	68,882	-3,602
1000 KCM	254,661	262,581	-7,920
1000 KCM LVC	24,000	38,230	-14,230
12 Fiber SM FOC	289,504	294,530	-5,026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	72,404	99,651	72.7%
Roads Built	57,183	99,651	57.4%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	55	64	85.9%
Foundations Poured	41	64	64.1%
Foundations Backfilled	25	64	39.1%
Crane Pads Completed	25	64	39.1%
Tower Base Sections Erected	5	64	7.8%
Tower Mid Sections Erected	5	64	7.8%
Tower Top Sections Erected	4	64	6.3%
Nacelles Installed	4	64	6.3%
Rotors Installed	4	64	6.3%
Tower Wiring Complete	0	64	0.0%
Mechanically Complete	0	64	0.0%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	68,746	157,430	43.7%
500 Cable Trenched	988	15,455	6.4%
1000 Cable Trenched	67,638	77,170	87.6%
Transformers Set/Terminated	9	64	14.1%

(as of COB yesterday)
