

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Thursday, 9-23-10
High: 52
Precipitation Chances: 100%

COD: 11-30-10
Low: 40

Days to COD: 69
Winds: NNW @ 16 mph
Weather Forecast: Rain

NextEra™ Energy Resources

Blattner Energy

Paradigm

GE

Safety/Environmental:

- Do not go under suspended loads
- Blattner is doing fork lift training

Civil/Erection:

- No work due to rain

Foundations:

Collection:

Electrical:

Substation:

RECEIVING (As of COB yesterday)


	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	0	6
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	108,189	-57187
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	99,651	76.3%
Roads Built	63,285	99,651	63.5%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	63	64	98.4%
Foundations Poured	53	64	82.8%
Foundations Backfilled	41	64	64.1%
Crane Pads Completed	41	64	64.1%
Tower Base Sections Erected	12	64	18.8%
Tower Mid Sections Erected	12	64	18.8%
Tower Top Sections Erected	8	64	12.5%
Nacelles Installed	8	64	12.5%
Rotors Installed	7	64	10.9%
Tower Wiring Complete	6	64	9.4%
Mechanically Complete	2	64	3.1%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	74,338	157,430	47.2%
500 Cable Trenched	7,960	15,455	51.5%
1000 Cable Trenched	77,338	77,170	100.2%
Transformers Set/Terminated	12	64	18.8%

(as of COB yesterday)

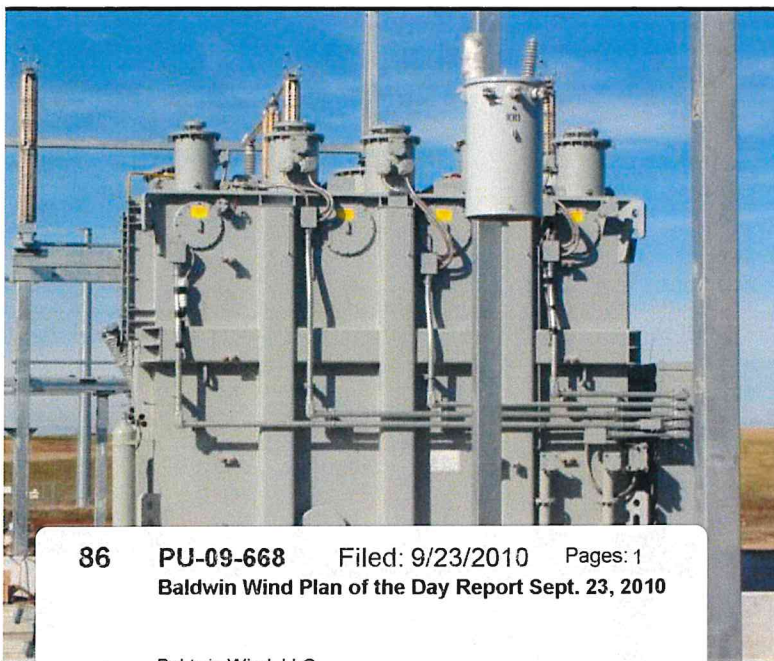

86 PU-09-668 Filed: 9/23/2010 Pages: 1
Baldwin Wind Plan of the Day Report Sept. 23, 2010

Baldwin Wind, LLC
