

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Friday, 9-24-10
High: 68
Precipitation Chances: 25%

COD: 11-30-10
Low: 42

Days to COD: 68
Winds: SW @ 9 mph
Weather Forecast: Partly Cloudy

NextEra™ Energy Resources

Blattner Energy

Paradigm

GE

Safety/Environmental:

- Do not go under suspended loads
- Fence off wetland as needed
- Installing silt fence as needed
- SWPPP inspection today

Civil/Erection:

- Rotor assembly at 54
- Erect base and mid at 32
- Erect rotor at 58

Foundations:

- Foundation excavation at 2
- Pour mud mats 2
- Install bottom rebar mat at 25-26
- Install anchor bolts at 24-25
- Install top rebar mat at 24-25
- Form base at 24-25
- Pour base at 5-6
- Form pedestal at 7-8
- Pour pedestal at 7-8
- Backfill at 19-20
- Build crane at 19-20

Collection:

- Trench and install 4/0 at SP1015-G1020 & 27-30
- Setting JB61
- Ground grid testing at 49-50
- Terminating HV at 37-40 & LV AT 34-36

Electrical:

- Mechanical Completion Pre-walk at 59 & 64
- IIP at 62-64


Substation:

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	0	6
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	108,189	-57187
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	99,651	76.3%
Roads Built	63,285	99,651	63.5%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	63	64	98.4%
Foundations Poured	53	64	82.8%
Foundations Backfilled	41	64	64.1%
Crane Pads Completed	41	64	64.1%
Tower Base Sections Erected	12	64	18.8%
Tower Mid Sections Erected	12	64	18.8%
Tower Top Sections Erected	8	64	12.5%
Nacelles Installed	8	64	12.5%
Rotors Installed	7	64	10.9%
Tower Wiring Complete	6	64	9.4%
Mechanically Complete	2	64	3.1%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	101,729	157,430	64.6%
500 Cable Trenched	9,778	15,455	63.3%
1000 Cable Trenched	75,520	77,170	97.9%
Transformers Set/Terminated	14	64	21.9%
(as of COB yesterday)			

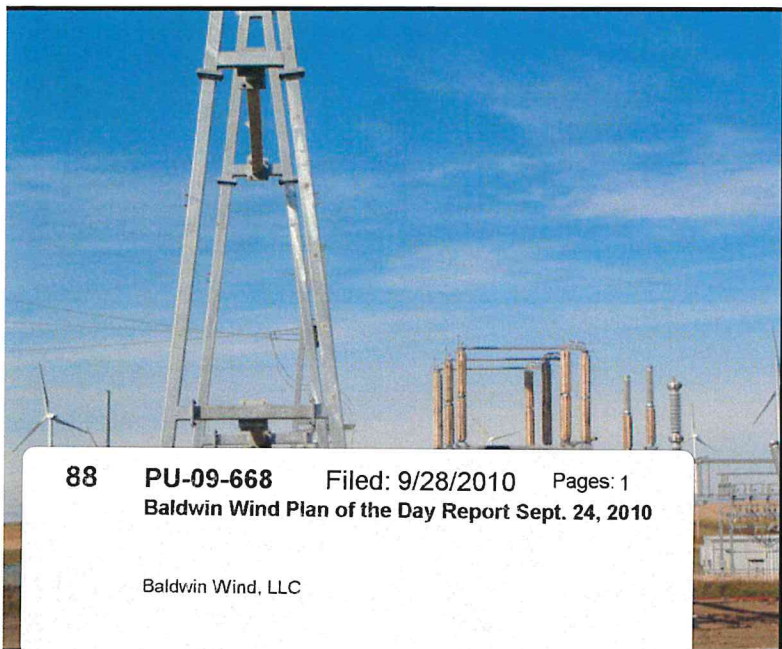

88 PU-09-668 Filed: 9/28/2010 Pages: 1
Baldwin Wind Plan of the Day Report Sept. 24, 2010

Baldwin Wind, LLC
