

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Wednesday, 9-29-10
 High: 71
 Precipitation Chances: 0 %

COD: 11-30-10
 Low: 40

Days to COD: 63
 Winds: NW @ 15 mph
 Weather Forecast: Partly Sunny

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----

Safety/Environmental:

- Do not go under suspended loads
- Fence off wetland as needed
- Installing silt fence as needed

Civil/Erection:

- Gravel at 5-8
- Reclaim at 80th, 257th-66th
- Rotor assembly at 37
- Erect base & mid at 39-40
- Erect top, nacelle, & rotor at 53-54

Foundations:

- Pour pedestal Complete
- Backfill at 13-15
- Build crane pad at 13-15

Collection:

- Trench and install 4/0 at 21-22
- Setting transformer at 16-17 & 27-31
- Terminating HV at 50-52 & LV at 44-45

Electrical:

- Tower wiring at 55-56
- Mechanical Completion Pre-walk at 56
- IIP at 58
- GE pre-commissioning at 60-61

Substation:

- Install above grade conduit
- Bus fabrication
- Spread surface rock


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	0	6
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	66,285	76,066	87.1%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	46	64	71.9%
Crane Pads Completed	46	64	71.9%
Tower Base Sections Erected	19	64	29.7%
Tower Mid Sections Erected	19	64	29.7%
Tower Top Sections Erected	10	64	15.6%
Nacelles Installed	10	64	15.6%
Rotors Installed	10	64	15.6%
Tower Wiring Complete	8	64	12.5%
Mechanically Complete	6	64	9.4%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	118,001	157,430	75.0%
500 Cable Trenched	13,850	15,455	89.6%
1000 Cable Trenched	76,996	77,170	99.8%
Transformers Set/Terminated	24	64	37.5%

(as of COB yesterday)

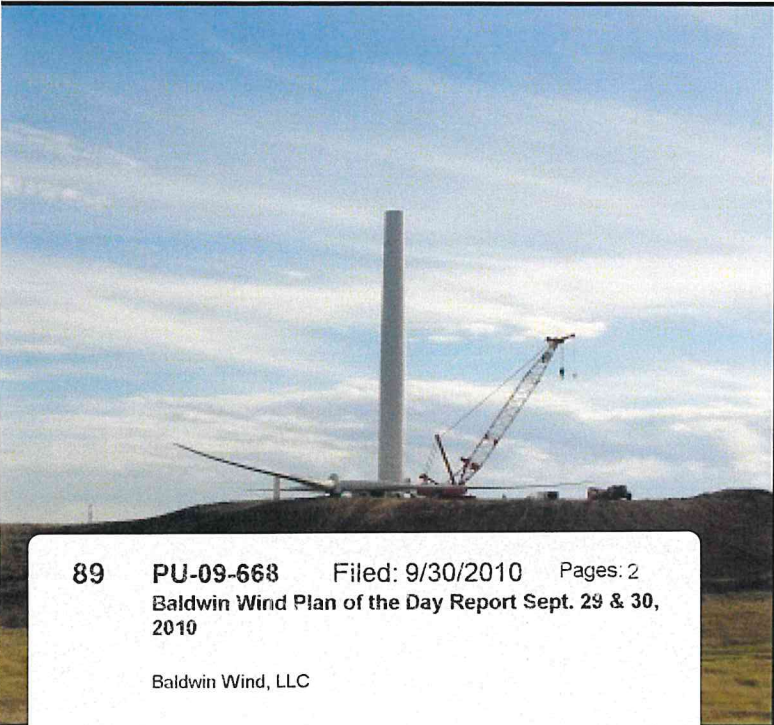

89 PU-09-668 Filed: 9/30/2010 Pages: 2
 Baldwin Wind Plan of the Day Report Sept. 29 & 30, 2010

Baldwin Wind, LLC

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Thursday, 9-30-10
 High: 68
 Precipitation Chances: 0 %

COD: 11-30-10
 Low: 42

Days to COD: 62
 Winds: WNW @ 5 mph
 Weather Forecast: Sunny

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----

Safety/Environmental:

- Do not go under suspended loads
- Fence off wetland as needed
- Installing silt fence as needed

Civil/Erection:

- Gravel at 8
- Reclaim at 80th, 257th-66th
- Rotor assembly at 37
- Erect base & mid at 41-43
- Erect top, nacelle, & rotor at Mob to 32

Foundations:

- Pour pedestal Complete
- Backfill at 10-12
- Build crane pad at 10-12

Collection:

- Trench and install 4/0 at 12-JB10-2
- Underground splicing at SP601
- Setting transformer box pads at 20-23
- Setting JB at JB11-2
- Terminating HV at Substation & LV at 46-48

Electrical:

- Tower wiring at 54-55
- Mechanical Completion Pre-walk at 55
- IIP at 56 & 58
- GE pre-commissioning at 61-62

Substation:

- Install above grade conduit
- Bus fabrication
- Spread surface rock

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	0	6
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	66,285	76,066	87.1%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	49	64	76.6%
Crane Pads Completed	49	64	76.6%
Tower Base Sections Erected	21	64	32.8%
Tower Mid Sections Erected	21	64	32.8%
Tower Top Sections Erected	12	64	18.8%
Nacelles Installed	12	64	18.8%
Rotors Installed	12	64	18.8%
Tower Wiring Complete	9	64	14.1%
Mechanically Complete	6	64	9.4%
Pre-Commissioned	1	64	1.6%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	132,861	157,430	84.4%
500 Cable Trenched	13,965	15,455	90.4%
1000 Cable Trenched	76,996	77,170	99.8%
Transformers Set/Terminated	26	64	40.6%

(as of COB yesterday)

