

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Friday, 10-1-10
 High: 64
 Precipitation Chances: 0 %

COD: 11-30-10
 Low: 34

Days to COD: 61
 Winds: NE @ 12 mph
 Weather Forecast: Mostly Sunny

NextEra™ Energy Resources

Blattner Energy

Paradigm

GE

Safety/Environmental:

- Do not go under suspended loads
- Fence off wetland as needed
- Installing silt fence as needed

Civil/Erection:

- Gravel at 1-8
- Reclaim at 57-59
- Rotor assembly at 40-41
- Erect top, nacelle, & rotor at Mob to 32

Foundations:

- Backfill at 5-8
- Build crane pad at 5-8

Collection:

- Trench and install 4/0 at 5-8
- Setting transformer box pads at 12-15
- Setting JB at JB10-2
- Terminating HV at Substation & LV at 52
- Ground grid testing at 3-4

Electrical:

- Tower wiring at 53
- Mechanical Completion Pre-walk at 54
- IIP at 55 & 57
- GE pre-commissioning at 61-62

Substation:

- Bus fabrication
- Spread surface rock


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	3	3
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	66,285	76,066	87.1%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	53	64	82.8%
Crane Pads Completed	53	64	82.8%
Tower Base Sections Erected	22	64	34.4%
Tower Mid Sections Erected	22	64	34.4%
Tower Top Sections Erected	12	64	18.8%
Nacelles Installed	12	64	18.8%
Rotors Installed	12	64	18.8%
Tower Wiring Complete	11	64	17.2%
Mechanically Complete	8	64	12.5%
Pre-Commissioned	2	64	3.1%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	136,948	157,430	87.0%
500 Cable Trenched	13,965	15,455	90.4%
1000 Cable Trenched	76,996	77,170	99.8%
Transformers Set/Terminated	32	64	50.0%

(as of COB yesterday)

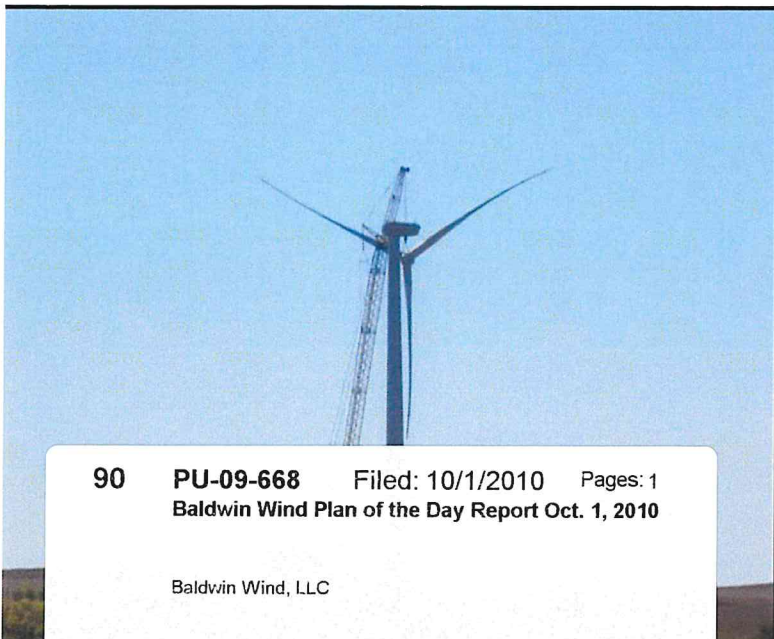

90 PU-09-668 Filed: 10/1/2010 Pages: 1
 Baldwin Wind Plan of the Day Report Oct. 1, 2010

Baldwin Wind, LLC
