

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Thursday, 10-7-10
 High: 79
 Precipitation Chances: 0 %

COD: 11-30-10
 Low: 47

Days to COD: 55
 Winds: S @ 9 mph
 Weather Forecast: Mostly Sunny

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----

Safety/Environmental:

- Be aware of your surroundings
- Fence off wetland as needed
- Installing silt fence as needed

Civil/Erection:

- Reclaim at 32-33
- Erect base & mid at 48 & walk to 49
- Assemble rotor at 46-47
- Erect top, nacelle & rotor at 42-43

Foundations:

- Backfill at Complete
- Build crane pad at Complete

Collection:

- Trench and install 4/0 at 9
- Underground splicing at SP906, SP1006 & SP1106
- Setting transformer box pad at 1, 5 & 6
- Terminating HV at 18-20 & LV at 16 & 27
- DTA to controller terminating at 16-17
- Grounding grid testing at 24-26

Electrical:

- Tower wiring at 37-38
- IIP at 34-35
- GE Pre-commissioning at 53, 55 & 57

Substation:


- Bus fabrication
- Spread surface rock
- Control wire installation
- Conduit run into Wilton II

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	3	3
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	29	64	45.3%
Tower Mid Sections Erected	28	64	43.8%
Tower Top Sections Erected	22	64	34.4%
Nacelles Installed	22	64	34.4%
Rotors Installed	22	64	34.4%
Tower Wiring Complete	18	64	28.1%
Mechanically Complete	13	64	20.3%
Pre-Commissioned	9	64	14.1%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	149,495	157,430	95.0%
500 Cable Trenched	13,965	15,455	90.4%
1000 Cable Trenched	76,996	77,170	99.8%
Transformers Set/Terminated	36	64	56.3%
(as of COB yesterday)			

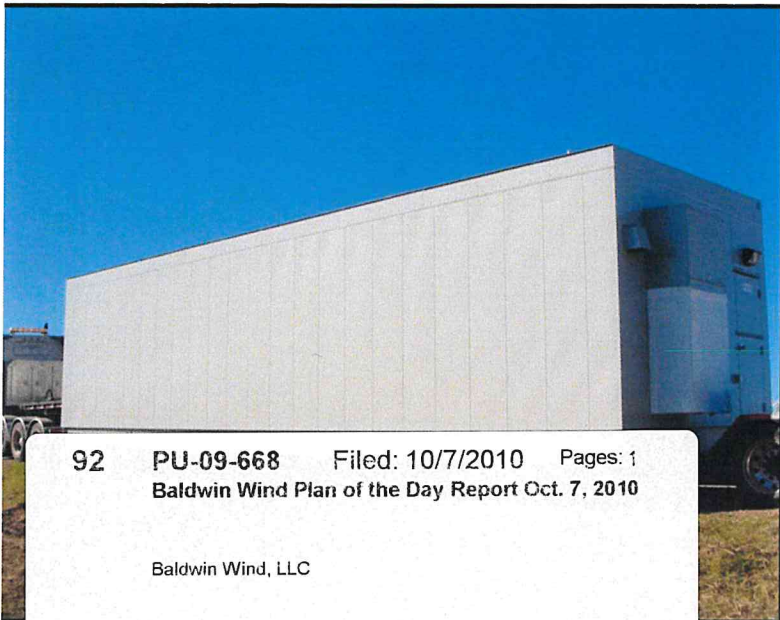

92 PU-09-668 Filed: 10/7/2010 Pages: 1
 Baldwin Wind Plan of the Day Report Oct. 7, 2010

Baldwin Wind, LLC
