

# Baldwin Wind, LLC

## Plan of the Day (POD)

Date: Friday, 10-8-10  
High: 83  
Precipitation Chances: 25 %

COD: 11-30-10  
Low: 51

Days to COD: 54  
Winds: ENE @ 6 mph  
Weather Forecast: Partly Sunny

### NextEra™ Energy Resources

### Blattner Energy

### Paradigm

### GE

**Safety/Environmental:**

- Be aware of your surroundings
- Fence off wetland as needed
- Installing silt fence as needed

**Civil/Erection:**

- Reclaim at 34-37
- Erect base at 51
- Erect mid at 50-51
- Assemble rotor at 47-49
- Erect top, nacelle & rotor at 44-45

**Foundations:**

- Backfill at Complete
- Build crane pad at Complete

**Collection:**

- Trench and install 4/0 at 1
- Underground splicing at SP908, SP1107 & SP1108
- Terminating HV at 21-23 & LV at 17-18
- DTA to controller terminating at 18-20
- Grounding grid testing at 1-10

**Electrical:**

- Tower wiring at 40-41
- IIP at 34 & 37
- GE Pre-commissioning at 33 & 36

**Substation:**


- Bus fabrication
- Spread surface rock
- Control wire installation
- Conduit run into Wilton II

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	3	3
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	31	64	48.4%
Tower Mid Sections Erected	30	64	46.9%
Tower Top Sections Erected	24	64	37.5%
Nacelles Installed	24	64	37.5%
Rotors Installed	24	64	37.5%
Tower Wiring Complete	20	64	31.3%
Mechanically Complete	16	64	25.0%
Pre-Commissioned	13	64	20.3%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	149,619	157,430	95.0%
500 Cable Trenched	13,965	15,455	90.4%
1000 Cable Trenched	76,996	77,170	99.8%
Transformers Set/Terminated	39	64	60.9%
(as of COB yesterday)			

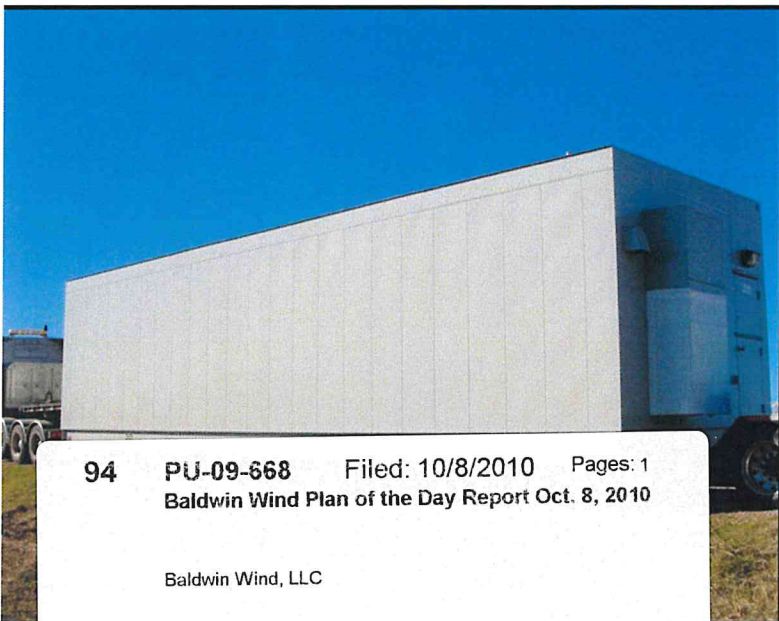

94 PU-09-668 Filed: 10/8/2010 Pages: 1  
Baldwin Wind Plan of the Day Report Oct. 8, 2010

Baldwin Wind, LLC
