

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Thursday, 10-14-10
 High: 68
 Precipitation Chances: 0 %

COD: 11-30-10
 Low: 37

Days to COD: 48
 Winds: NNW @ 7 mph
 Weather Forecast: Mostly Sunny

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----

Safety/Environmental:

- Stay focused on task at hand
- Fence off wetland Complete
- Installing silt fence Complete

Civil/Erection:

- Reclaim 32 & 43-46
- Erect base at 27 & walk to 5
- Erect mid at 27 & walk to 5
- Assemble rotor at 28-29
- Erect top & nacelle at 51-52
- Erect rotor at 50-52

Foundations: Complete

Collection:

- Underground splicing at SP 1018 & Control House
- Setting transformer at Complete
- Terminating HV at 4, 6 & 7, & LV at 1-4
- DTA to controller termination at 10-12
- Turbine fiber splice at 42 & 64

Electrical:

- Tower wiring at 47-48
- Mechanical completion pre-walk at 46-47
- IIP at 44-45
- GE Pre-commissioning at 42-43

Substation:


- Control wire installation
- Conduit run into Wilton II

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	6	0
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	36	64	56.3%
Tower Mid Sections Erected	36	64	56.3%
Tower Top Sections Erected	29	64	45.3%
Nacelles Installed	29	64	45.3%
Rotors Installed	29	64	45.3%
Tower Wiring Complete	27	64	42.2%
Mechanically Complete	24	64	37.5%
Pre-Commissioned	20	64	31.3%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	149,724	149,724	100.0%
500 Cable Trenched	13,965	13,965	100.0%
1000 Cable Trenched	76,996	76,996	100.0%
Transformers Set/Terminated	57	64	89.1%
(as of COB yesterday)			

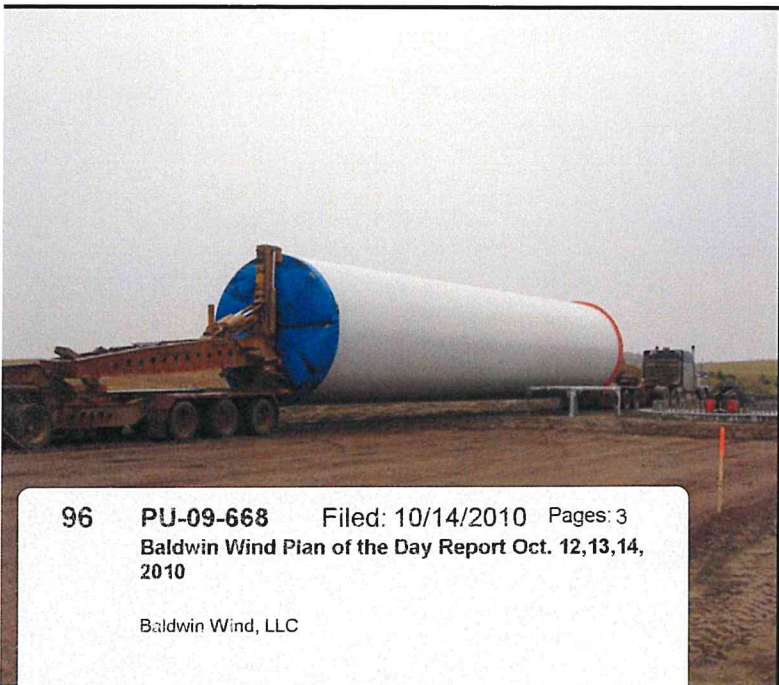

96 PU-09-668 Filed: 10/14/2010 Pages: 3
 Baldwin Wind Plan of the Day Report Oct. 12,13,14, 2010

Baldwin Wind, LLC

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Wednesday, 10-13-10
High: 65
Precipitation Chances: 10 %

COD: 11-30-10
Low: 33

Days to COD: 49
Winds: WNW @ 10 mph
Weather Forecast: Mostly Sunny

NextEra™ Energy Resources

Blattner Energy

Paradigm

GE

Safety/Environmental:

- Stay focused on task at hand
- Fence off wetland Complete
- Installing silt fence Complete

Civil/Erection:

- Reclaim 41-46
- Erect base at walk to 28
- Erect mid at walk to 28
- Assemble rotor at Mob to 31
- Erect top, nacelle & rotor at 49

Foundations:

Collection:

- Underground splicing at SP1012, SP1014, & SP1015
- Setting transformer at Complete
- Terminating HV at 2-4 & LV at 3-5
- DTA to controller termination at 12-15

Electrical:

- Tower wiring at 45-46
- Mechanical completion pre-walk at 44-45
- IIP at 42-43
- GE Pre-commissioning at walk down feeder 7

Substation:

- Control wire installation
- Conduit run into Wilton II



RECEIVING (As of COB yesterday)

	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	3	3
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	36	64	56.3%
Tower Mid Sections Erected	36	64	56.3%
Tower Top Sections Erected	29	64	45.3%
Nacelles Installed	29	64	45.3%
Rotors Installed	29	64	45.3%
Tower Wiring Complete	25	64	39.1%
Mechanically Complete	22	64	34.4%
Pre-Commissioned	18	64	28.1%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	149,724	157,430	95.1%
500 Cable Trenched	13,965	15,455	90.4%
1000 Cable Trenched	76,996	77,170	99.8%
Transformers Set/Terminated	53	64	82.8%

(as of COB yesterday)

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Tuesday, 10-12-10
 High: 63
 Precipitation Chances: 10 %

COD: 11-30-10
 Low: 33

Days to COD: 50
 Winds: WNW @ 15 mph
 Weather Forecast: Partly Sunny

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----

Safety/Environmental:

- Stay focused on task at hand
- Fence off wetland as needed
- Installing silt fence as needed

Civil/Erection:

- Reclaim 40-42
- Erect base at 29
- Erect mid at 29-30
- Assemble rotor at Mob to 31

Foundations:

Collection:

- Underground splicing at SP909, SP1010, SP1011, SP1111, & SP1112
- Setting transformer at 22 & 24-26
- Terminating HV at 12 & LV at 7-10
- DTA to controller termination at 7-10
- Turbine fiber splice at 42-45

Electrical:

- Tower wiring at 43-44
- Mechanical completion pre-walk at 42-43
- IIP at 41-42
- GE Pre-commissioning at 38-39

Substation:

- Control wire installation
- Conduit run into Wilton II

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	3	3
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status			
	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	34	64	53.1%
Tower Mid Sections Erected	33	64	51.6%
Tower Top Sections Erected	29	64	45.3%
Nacelles Installed	29	64	45.3%
Rotors Installed	29	64	45.3%
Tower Wiring Complete	23	64	35.9%
Mechanically Complete	21	64	32.8%
Pre-Commissioned	16	64	25.0%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	149,724	157,430	95.1%
500 Cable Trenched	13,965	15,455	90.4%
1000 Cable Trenched	76,996	77,170	99.8%
Transformers Set/Terminated	48	64	75.0%
(as of COB yesterday)			

