

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Wednesday, 10-20-10
 High: 62
 Precipitation Chances: 0 %

COD: 11-30-10
 Low: 30

Days to COD: 42
 Winds: NW @ 16 mph
 Weather Forecast: Mostly Sunny

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----

Safety/Environmental:

- Stay focused on task at hand
- Substation is energized

Civil/Erection:

- Reclaim at 39-41 & 51-52
- Erect base at 10-12
- Erect mid at 10-12
- Assemble rotor at 8-9
- Erect top, nacelle & rotor at 28-29

Foundations: Complete

Collection:

- Terminating HV Complete
- DTA to controller termination at 2-5
- Turbine fiber splice at 9-14
- Fiber testing at F9B

Electrical:

- Mechanical completion pre-walk at 31
- IIP at 50-51
- GE Commissioning at 63-64

Substation:


- Control wire installation
- Wire Baldwin end of CT circuit

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	6	0
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	43	64	67.2%
Tower Mid Sections Erected	43	64	67.2%
Tower Top Sections Erected	35	64	54.7%
Nacelles Installed	35	64	54.7%
Rotors Installed	34	64	53.1%
Tower Wiring Complete	34	64	53.1%
Mechanically Complete	30	64	46.9%
Pre-Commissioned	24	64	37.5%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	149,724	149,724	100.0%
500 Cable Trenched	13,965	13,965	100.0%
1000 Cable Trenched	76,996	76,996	100.0%
Transformers Set/Terminated	64	64	100.0%
(as of COB yesterday)			

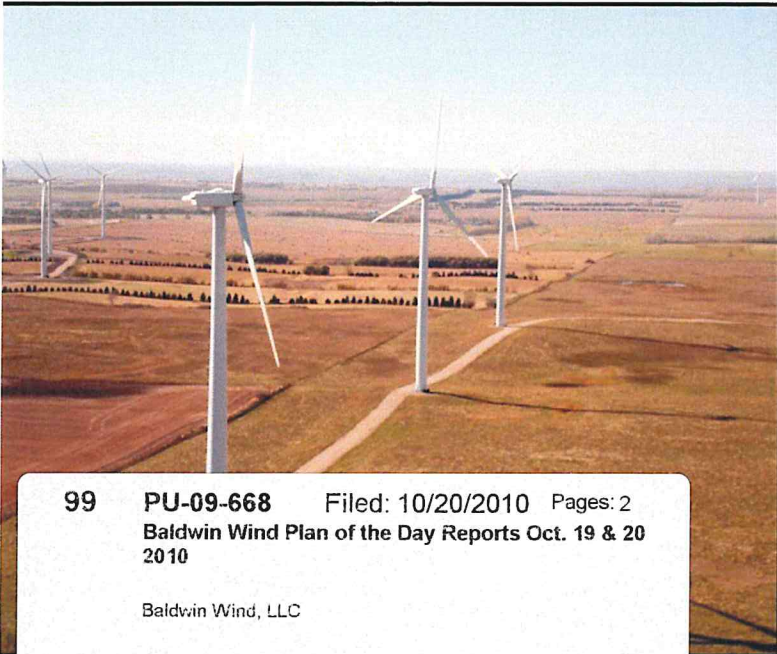

99 PU-09-668 Filed: 10/20/2010 Pages: 2
 Baldwin Wind Plan of the Day Reports Oct. 19 & 20 2010

Baldwin Wind, LLC

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Tuesday, 10-19-10
 High: 65
 Precipitation Chances: 0 %

COD: 11-30-10
 Low: 33

Days to COD: 43
 Winds: WNW @ 13 mph
 Weather Forecast: Partly Sunny

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----

- Safety/Environmental:**
- Stay focused on task at hand
 - Follow proper procedure
 - Continue to train employees
- Civil/Erection:**
- Reclaim at 39-41 & 48-51
 - Erect base at 8-9
 - Erect mid at 8-9
 - Assemble rotor at 6-7
 - Erect top, nacelle & rotor at 30 & walk to 29
- Foundations: Complete**
- Collection:**
- Terminating HV Complete
 - DTA to controller termination at 2-5
 - Turbine fiber splice at 15-16 & 27-29
- Electrical:**
- Tower wiring at 31
 - Mechanical completion pre-walk at 31 & 52
 - IIP at 49-50
 - GE Commissioning at 61-62
- Substation:**
- Control wire installation
 - Pull in CT circuits into Wilton II

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	6	0
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status			
	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	41	64	64.1%
Tower Mid Sections Erected	41	64	64.1%
Tower Top Sections Erected	34	64	53.1%
Nacelles Installed	34	64	53.1%
Rotors Installed	34	64	53.1%
Tower Wiring Complete	33	64	51.6%
Mechanically Complete	28	64	43.8%
Pre-Commissioned	24	64	37.5%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	149,724	149,724	100.0%
500 Cable Trenched	13,965	13,965	100.0%
1000 Cable Trenched	76,996	76,996	100.0%
Transformers Set/Terminated	64	64	100.0%
(as of COB yesterday)			

