

# Baldwin Wind, LLC

## Plan of the Day (POD)

Date: Friday, 10-22-10  
 High: 64  
 Precipitation Chances: 0 %

COD: 11-30-10  
 Low: 33

Days to COD: 40  
 Winds: S @ 76 mph  
 Weather Forecast: Sunny

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----


- Safety/Environmental:**
- SWPPP inspection 10-26-10
  - Always use spotters
- Civil/Erection:**
- Reclaim at 29-30 & 50-52
  - Erect base at 13-14
  - Erect mid at 13-14
  - Assemble rotor at 12-13
  - Erect top at 28
  - Erect nacelle & rotor at 27-28
- Foundations: Complete**
- Collection:**
- Underground fiber splicing at FS901, FS1001 & FS1101
  - Turbine fiber splice at 18-21
- Electrical:**
- Tower wiring at 29
  - IIP at 31 & 52
  - GE Commissioning at 55-57
- Substation:**
- Wire Baldwin end of CT circuit
  - Testing field equipment

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	6	0
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	73,906	-8626
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	46	64	71.9%
Tower Mid Sections Erected	46	64	71.9%
Tower Top Sections Erected	37	64	57.8%
Nacelles Installed	36	64	56.3%
Rotors Installed	36	64	56.3%
Tower Wiring Complete	35	64	54.7%
Mechanically Complete	31	64	48.4%
Pre-Commissioned	24	64	37.5%
Commissioned	7	64	10.9%
4/0 Cable Trenched	149,724	149,724	100.0%
500 Cable Trenched	13,965	13,965	100.0%
1000 Cable Trenched	76,996	76,996	100.0%
Transformers Set/Terminated	64	64	100.0%
(as of COB yesterday)			

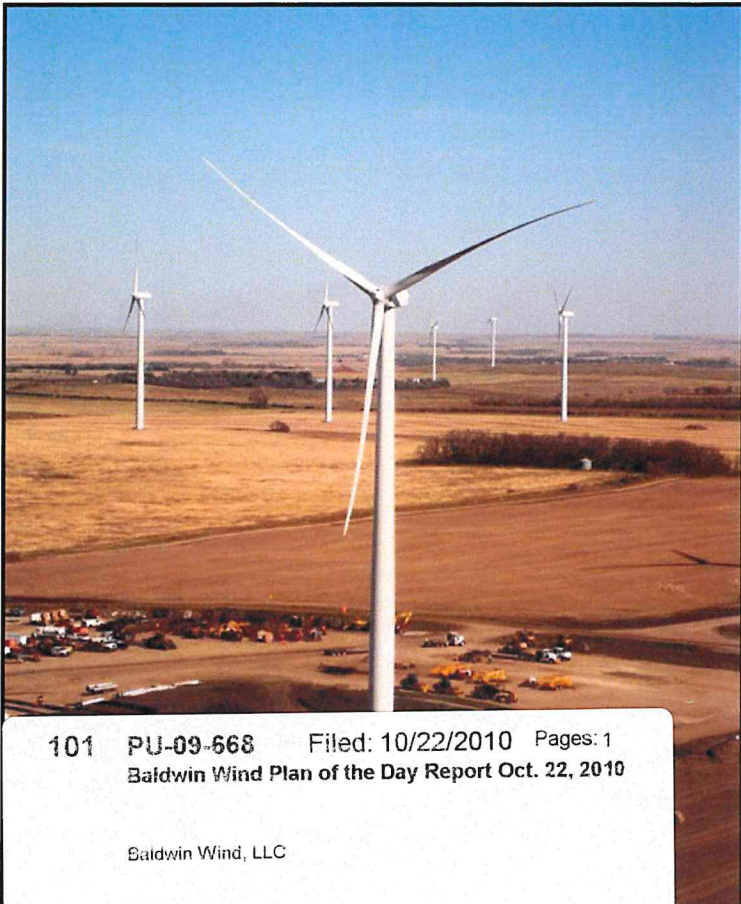

101 PU-09-668 Filed: 10/22/2010 Pages: 1  
 Baldwin Wind Plan of the Day Report Oct. 22, 2010

Baldwin Wind, LLC
