

# Baldwin Wind, LLC

## Plan of the Day (POD)

Date: Tuesday, 10-26-10  
 High: 43  
 Precipitation Chances: 85 %

COD: 11-30-10  
 Low: 22

Days to COD: 37  
 Winds: WNW @ 35 mph  
 Weather Forecast: Cloudy

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----


- Safety/Environmental:
  - SWPPP inspection
  - Be cautious of strong winds
  - Be aware of changing weather conditions
- Civil/Erection:
  - Reclaim at 8-9 & 29-31
- Foundations: Complete
- Collection:
  - Underground fiber splicing at 1007 & 1107
  - Turbine fiber splice at substation
  - Fiber testing circuit 10 & 11
- Electrical:
  - Tower wiring at 8-9
  - Mechanical completion at 7-8
  - IIP at 5 & 27
  - GE Commissioning at 32-33 & 38-39
- Substation:
  - Outage to tie into Wilton
  - Testing field equipment

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	6	0
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	73,906	-8626
1000 KCM	254,661	296,079	-41418
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	49	64	76.6%
Tower Mid Sections Erected	49	64	76.6%
Tower Top Sections Erected	46	64	71.9%
Nacelles Installed	46	64	71.9%
Rotors Installed	46	64	71.9%
Tower Wiring Complete	41	64	64.1%
Mechanically Complete	35	64	54.7%
Pre-Commissioned	24	64	37.5%
Commissioned	13	64	20.3%
4/0 Cable Trenched	149,724	149,724	100.0%
500 Cable Trenched	13,965	13,965	100.0%
1000 Cable Trenched	76,996	76,996	100.0%
Transformers Set/Terminated	64	64	100.0%
(as of COB yesterday)			

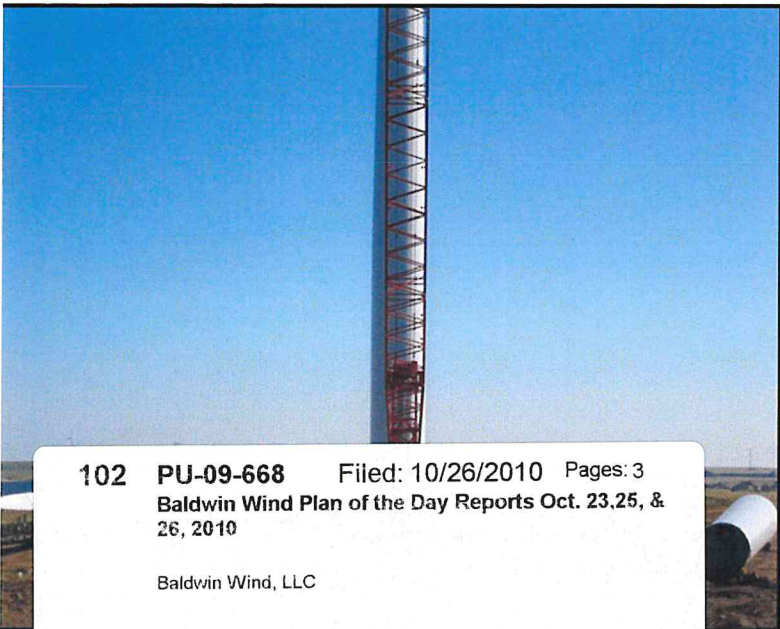

102 PU-09-668 Filed: 10/26/2010 Pages: 3  
 Baldwin Wind Plan of the Day Reports Oct. 23, 25, & 26, 2010

Baldwin Wind, LLC

# Baldwin Wind, LLC

## Plan of the Day (POD)

Date: Monday, 10-25-10  
 High: 56  
 Precipitation Chances: 25 %

COD: 11-30-10  
 Low: 29

Days to COD: 37  
 Winds: WNW @ 19 mph  
 Weather Forecast: Cloudy

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----

- Safety/Environmental:**
- SWPPP inspection 10-26-10
  - Always use spotters
- Civil/Erection:**
- Reclaim at 29-31
  - Erect base & mid at mob to 26
  - Assemble rotor at 14
  - Erect top & nacelle at 12
  - Erect rotor at 11-12
- Foundations: Complete**
- Collection:**
- Underground fiber splicing at 1007 & 1107
  - Fiber testing circuit 10 & 11
- Electrical:**
- Tower wiring at 6-7
  - Mechanical completion at 5-6
  - IIP at 28-29
  - GE Commissioning at 53-54
- Substation:**
- Fabricate jumpers to Wilton II
  - Testing field equipment

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	6	0
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	73,906	-8626
1000 KCM	254,661	296,079	-41418
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	49	64	76.6%
Tower Mid Sections Erected	49	64	76.6%
Tower Top Sections Erected	45	64	70.3%
Nacelles Installed	45	64	70.3%
Rotors Installed	44	64	68.8%
Tower Wiring Complete	37	64	57.8%
Mechanically Complete	34	64	53.1%
Pre-Commissioned	24	64	37.5%
Commissioned	10	64	15.6%
4/0 Cable Trenched	149,724	149,724	100.0%
500 Cable Trenched	13,965	13,965	100.0%
1000 Cable Trenched	76,996	76,996	100.0%
Transformers Set/Terminated	64	64	100.0%
(as of COB yesterday)			



**Plan of the Day (POD)**

Date: Saturday, 10-23-10  
High: 52  
Precipitation Chances: 10 %

COD: 11-30-10  
Low: 34

Days to COD: 39  
Winds: ENE @ 10 mph  
Weather Forecast: Partly Cloudy

**NextEra™ Energy Resources**

**Blattner Energy**

**Paradigm**

**GE**

**Safety/Environmental:**

- SWPPP inspection 10-26-10
- Always use spotters

**Civil/Erection:**

- Reclaim at blade county & string roads
- Erect base at mob to 15
- Erect mid at 14
- Assemble rotor at 14-15
- Erect at 28
- Erect top, nacelle & rotor at Mob to 5

**Foundations: Complete**

**Collection:**

- Underground fiber splicing at 21-26
- Fiber testing circuit 10

**Electrical:**

- Tower wiring at 27-28
- Mechanical completion at 27 & 29
- IIP at 30
- GE Commissioning at 53-54

**Substation:**

- Fabricate jumpers to Wilton II
- Testing field equipment

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	6	0
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	73,906	-8626
1000 KCM	254,661	296,079	-41418
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

**General Construction Status**

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	49	64	76.6%
Tower Mid Sections Erected	48	64	75.0%
Tower Top Sections Erected	38	64	59.4%
Nacelles Installed	38	64	59.4%
Rotors Installed	38	64	59.4%
Tower Wiring Complete	36	64	56.3%
Mechanically Complete	33	64	51.6%
Pre-Commissioned	24	64	37.5%
Commissioned	9	64	14.1%
4/0 Cable Trenched	149,724	149,724	100.0%
500 Cable Trenched	13,965	13,965	100.0%
1000 Cable Trenched	76,996	76,996	100.0%
Transformers Set/Terminated	64	64	100.0%

(as of COB yesterday)

