

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Tuesday, 11-9-10
High: 53
Precipitation Chances: 20 %

COD: 11-30-10
Low: 32

Days to COD: 23
Winds: NNW @ 10 mph
Weather Forecast: Mostly Cloudy

NextEra™ Energy Resources

Blattner Energy

Paradigm

GE

Safety/Environmental:

- Areas of the site are energized
- Stay focused on task at hand

Civil/Erection:

- Reclaim at 2-4 & 16-20

Foundations: Complete

Collection:

Electrical:

- Tower wiring at 3-4
- Mechanical completion at 2-3
- IIP at 1-2
- GE Commissioning at 5-7

Substation:

- Final rock work
- Control house cleanup
- Labeling

RECEIVING (As of COB yesterday)


	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	6	0
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	73,906	-8626
1000 KCM	254,661	296,079	-41418
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	64	64	100.0%
Tower Mid Sections Erected	64	64	100.0%
Tower Top Sections Erected	64	64	100.0%
Nacelles Installed	64	64	100.0%
Rotors Installed	64	64	100.0%
Tower Wiring Complete	62	64	96.9%
Mechanically Complete	59	64	92.2%
Pre-Commissioned	24	64	37.5%
Commissioned	38	64	59.4%
4/0 Cable Trenched	149,724	149,724	100.0%
500 Cable Trenched	13,965	13,965	100.0%
1000 Cable Trenched	76,996	76,996	100.0%
Transformers Set/Terminated	64	64	100.0%

(as of COB yesterday)

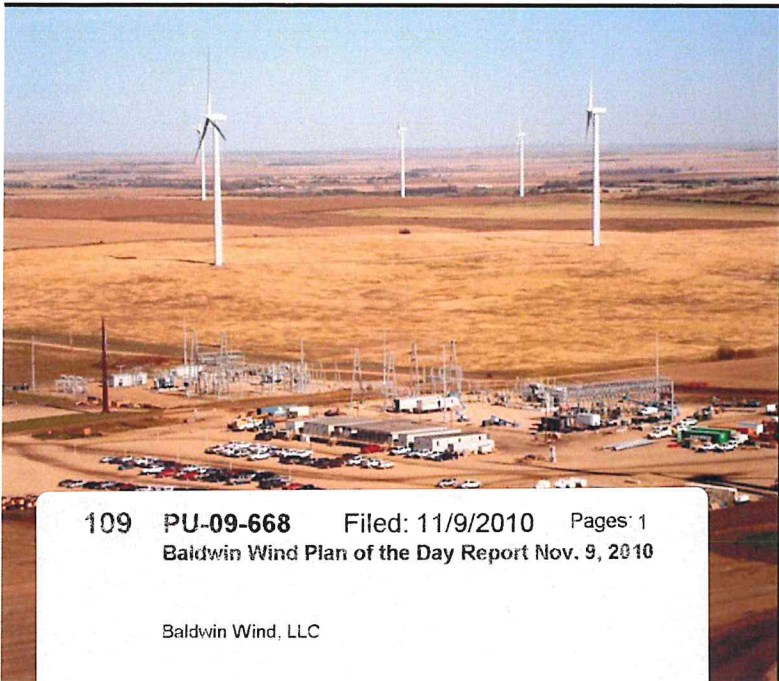

109 PU-09-668 Filed: 11/9/2010 Pages: 1
Baldwin Wind Plan of the Day Report Nov. 9, 2010

Baldwin Wind, LLC
