

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Tuesday, 11-16-10
 High: 38
 Precipitation Chances: 20 %

COD: 11-30-10
 Low: 20

Days to COD: 15
 Winds: ENE @ 8 mph
 Weather Forecast: Cloudy

NextEra™ Energy Resources

Blattner Energy

Paradigm

GE

Safety/Environmental:

- Areas of the site are energized
- Stay focused on task at hand

Civil/Erection:

- Reclaim Complete
- Foundations: Complete


Collection:

Electrical:

- GE Commissioning at 17 & 19-22

Substation:

- All work complete until outage to install metering unit

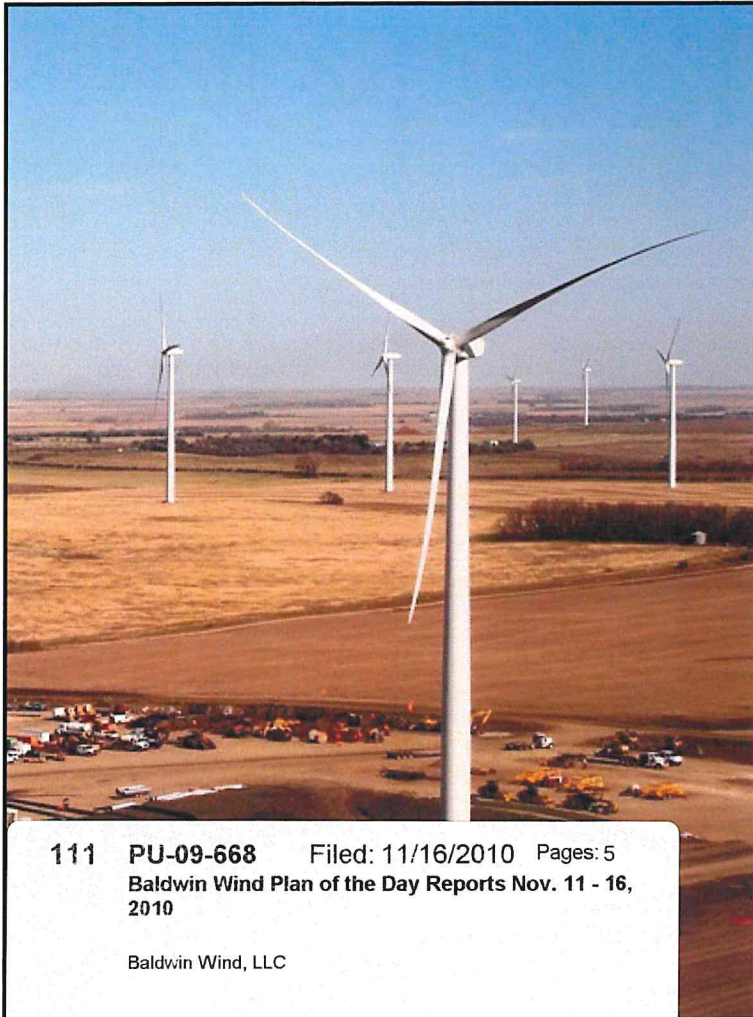

111 PU-09-668 Filed: 11/16/2010 Pages: 5
 Baldwin Wind Plan of the Day Reports Nov. 11 - 16, 2010

Baldwin Wind, LLC

| RECEIVING (As of COB yesterday) | | | |
|---------------------------------|---------|----------|---------|
| | Total | Received | Balance |
| PMT XFR | 65 | 65 | 0 |
| Grounding XFR | 6 | 6 | 0 |
| 4/0 Cable | 519,519 | 500,688 | 18831 |
| 500 KCM | 51,002 | 58,397 | -7395 |
| Copperclad | 65,280 | 73,906 | -8626 |
| 1000 KCM | 254,661 | 296,079 | -41418 |
| 1000 KCM LVC | 24,000 | 38,230 | -14230 |
| 12 Fiber SM FOC | 289,504 | 294,530 | -5026 |
| XFR Box Pads | 64 | 64 | 0 |
| Controllers | 64 | 64 | 0 |
| Bases | 64 | 64 | 0 |
| Mids | 64 | 64 | 0 |
| Tops | 64 | 64 | 0 |
| Nacelles | 64 | 64 | 0 |
| Hubs | 64 | 64 | 0 |
| Blade Sets | 64 | 64 | 0 |

Negative Number Indicates Overage of Cable

General Construction Status

| | Complete | Total | % Complete |
|-----------------------------|----------|---------|------------|
| Roads Subgraded | 76,066 | 76,066 | 100.0% |
| Roads Built | 76,066 | 76,066 | 100.0% |
| Silt Fence Installed | 3,584 | 11,417 | 100.0% |
| Foundations Excavated | 64 | 64 | 100.0% |
| Foundations Poured | 64 | 64 | 100.0% |
| Foundations Backfilled | 64 | 64 | 100.0% |
| Crane Pads Completed | 64 | 64 | 100.0% |
| Tower Base Sections Erected | 64 | 64 | 100.0% |
| Tower Mid Sections Erected | 64 | 64 | 100.0% |
| Tower Top Sections Erected | 64 | 64 | 100.0% |
| Nacelles Installed | 64 | 64 | 100.0% |
| Rotors Installed | 64 | 64 | 100.0% |
| Tower Wiring Complete | 64 | 64 | 100.0% |
| Mechanically Complete | 64 | 64 | 100.0% |
| Pre-Commissioned | 24 | 24 | 100.0% |
| Commissioned | 51 | 64 | 79.7% |
| 4/0 Cable Trenched | 149,724 | 149,724 | 100.0% |
| 500 Cable Trenched | 13,965 | 13,965 | 100.0% |
| 1000 Cable Trenched | 76,996 | 76,996 | 100.0% |
| Transformers Set/Terminated | 64 | 64 | 100.0% |

(as of COB yesterday)

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Monday, 11-15-10
High: 39
Precipitation Chances: 0 %

COD: 11-30-10
Low: 23

Days to COD: 16
Winds: NW @ 7 mph
Weather Forecast: Mostly Cloudy

NextEra™ Energy Resources

Blattner Energy

Paradigm

GE

Safety/Environmental:

- Areas of the site are energized
- Stay focused on task at hand

Civil/Erection:

- Reclaim Complete

Foundations: Complete

Collection:

Electrical:

- IIP Complete

- GE Commissioning on feeder 11

Substation:

- All work complete until outage to install metering unit



| RECEIVING (As of COB yesterday) | | | |
|---------------------------------|---------|----------|---------|
| | Total | Received | Balance |
| PMT XFR | 65 | 65 | 0 |
| Grounding XFR | 6 | 6 | 0 |
| 4/0 Cable | 519,519 | 500,688 | 18831 |
| 500 KCM | 51,002 | 58,397 | -7395 |
| Copperclad | 65,280 | 73,906 | -8626 |
| 1000 KCM | 254,661 | 296,079 | -41418 |
| 1000 KCM LVC | 24,000 | 38,230 | -14230 |
| 12 Fiber SM FOC | 289,504 | 294,530 | -5026 |
| XFR Box Pads | 64 | 64 | 0 |
| Controllers | 64 | 64 | 0 |
| Bases | 64 | 64 | 0 |
| Mids | 64 | 64 | 0 |
| Tops | 64 | 64 | 0 |
| Nacelles | 64 | 64 | 0 |
| Hubs | 64 | 64 | 0 |
| Blade Sets | 64 | 64 | 0 |

Negative Number Indicates Overage of Cable

General Construction Status

| | Complete | Total | % Complete |
|-----------------------------|----------|---------|------------|
| Roads Subgraded | 76,066 | 76,066 | 100.0% |
| Roads Built | 76,066 | 76,066 | 100.0% |
| Silt Fence Installed | 3,584 | 11,417 | 100.0% |
| Foundations Excavated | 64 | 64 | 100.0% |
| Foundations Poured | 64 | 64 | 100.0% |
| Foundations Backfilled | 64 | 64 | 100.0% |
| Crane Pads Completed | 64 | 64 | 100.0% |
| Tower Base Sections Erected | 64 | 64 | 100.0% |
| Tower Mid Sections Erected | 64 | 64 | 100.0% |
| Tower Top Sections Erected | 64 | 64 | 100.0% |
| Nacelles Installed | 64 | 64 | 100.0% |
| Rotors Installed | 64 | 64 | 100.0% |
| Tower Wiring Complete | 64 | 64 | 100.0% |
| Mechanically Complete | 64 | 64 | 100.0% |
| Pre-Commissioned | 24 | 24 | 100.0% |
| Commissioned | 51 | 64 | 79.7% |
| 4/0 Cable Trenched | 149,724 | 149,724 | 100.0% |
| 500 Cable Trenched | 13,965 | 13,965 | 100.0% |
| 1000 Cable Trenched | 76,996 | 76,996 | 100.0% |
| Transformers Set/Terminated | 64 | 64 | 100.0% |

(as of COB yesterday)

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Saturday, 11-13-10
 High: 39
 Precipitation Chances: 0 %

COD: 11-30-10
 Low: 18

Days to COD: 19
 Winds: NNW @ 7 mph
 Weather Forecast: Mostly Cloudy

| NextEra™ Energy Resources | Blattner Energy | Paradigm | GE |
|---------------------------|-----------------|----------|----|
|---------------------------|-----------------|----------|----|

- Safety/Environmental:**
- Areas of the site are energized
 - Stay focused on task at hand
- Civil/Erection:**
- Reclaim Complete
- Foundations: Complete**
- Collection:**
- Electrical:**
- IIP Complete
 - Gen alignments on feeder 10 & 11
 - GE Commissioning at 3 & 11-13
- Substation:**
- All work complete until outage to install metering unit

| RECEIVING (As of COB yesterday) | | | |
|---------------------------------|---------|----------|---------|
| | Total | Received | Balance |
| PMT XFR | 65 | 65 | 0 |
| Grounding XFR | 6 | 6 | 0 |
| 4/0 Cable | 519,519 | 500,688 | 18831 |
| 500 KCM | 51,002 | 58,397 | -7395 |
| Copperclad | 65,280 | 73,906 | -8626 |
| 1000 KCM | 254,661 | 296,079 | -41418 |
| 1000 KCM LVC | 24,000 | 38,230 | -14230 |
| 12 Fiber SM FOC | 289,504 | 294,530 | -5026 |
| XFR Box Pads | 64 | 64 | 0 |
| Controllers | 64 | 64 | 0 |
| Bases | 64 | 64 | 0 |
| Mids | 64 | 64 | 0 |
| Tops | 64 | 64 | 0 |
| Nacelles | 64 | 64 | 0 |
| Hubs | 64 | 64 | 0 |
| Blade Sets | 64 | 64 | 0 |

Negative Number Indicates Overage of Cable

General Construction Status

| | Complete | Total | % Complete |
|-----------------------------|----------|---------|------------|
| Roads Subgraded | 76,066 | 76,066 | 100.0% |
| Roads Built | 76,066 | 76,066 | 100.0% |
| Silt Fence Installed | 3,584 | 11,417 | 31.4% |
| Foundations Excavated | 64 | 64 | 100.0% |
| Foundations Poured | 64 | 64 | 100.0% |
| Foundations Backfilled | 64 | 64 | 100.0% |
| Crane Pads Completed | 64 | 64 | 100.0% |
| Tower Base Sections Erected | 64 | 64 | 100.0% |
| Tower Mid Sections Erected | 64 | 64 | 100.0% |
| Tower Top Sections Erected | 64 | 64 | 100.0% |
| Nacelles Installed | 64 | 64 | 100.0% |
| Rotors Installed | 64 | 64 | 100.0% |
| Tower Wiring Complete | 64 | 64 | 100.0% |
| Mechanically Complete | 64 | 64 | 100.0% |
| Pre-Commissioned | 24 | 64 | 37.5% |
| Commissioned | 42 | 64 | 65.6% |
| 4/0 Cable Trenched | 149,724 | 149,724 | 100.0% |
| 500 Cable Trenched | 13,965 | 13,965 | 100.0% |
| 1000 Cable Trenched | 76,996 | 76,996 | 100.0% |
| Transformers Set/Terminated | 64 | 64 | 100.0% |

(as of COB yesterday)



Baldwin Wind, LLC

Plan of the Day (POD)

Date: Friday, 11-12-10
 High: 45
 Precipitation Chances: 0 %

COD: 11-30-10
 Low: 21

Days to COD: 20
 Winds: SW @ 4 mph
 Weather Forecast: Mostly Sunny

| NextEra™ Energy Resources | Blattner Energy | Paradigm | GE |
|---------------------------|-----------------|----------|----|
|---------------------------|-----------------|----------|----|

- Safety/Environmental:**
- Areas of the site are energized
 - Stay focused on task at hand
- Civil/Erection:**
- Reclaim Complete
- Foundations: Complete**
- Collection:**
- Electrical:**
- IIP Complete
 - GE Commissioning at 8 & 11-14
- Substation:**
- All work complete until outage to install metering unit

| RECEIVING (As of COB yesterday) | | | |
|---------------------------------|---------|----------|---------|
| | Total | Received | Balance |
| PMT XFR | 65 | 65 | 0 |
| Grounding XFR | 6 | 6 | 0 |
| 4/0 Cable | 519,519 | 500,688 | 18831 |
| 500 KCM | 51,002 | 58,397 | -7395 |
| Copperclad | 65,280 | 73,906 | -8626 |
| 1000 KCM | 254,661 | 296,079 | -41418 |
| 1000 KCM LVC | 24,000 | 38,230 | -14230 |
| 12 Fiber SM FOC | 289,504 | 294,530 | -5026 |
| XFR Box Pads | 64 | 64 | 0 |
| Controllers | 64 | 64 | 0 |
| Bases | 64 | 64 | 0 |
| Mids | 64 | 64 | 0 |
| Tops | 64 | 64 | 0 |
| Nacelles | 64 | 64 | 0 |
| Hubs | 64 | 64 | 0 |
| Blade Sets | 64 | 64 | 0 |

Negative Number Indicates Overage of Cable

| General Construction Status | | | |
|-----------------------------|----------|---------|------------|
| | Complete | Total | % Complete |
| Roads Subgraded | 76,066 | 76,066 | 100.0% |
| Roads Built | 76,066 | 76,066 | 100.0% |
| Silt Fence Installed | 3,584 | 11,417 | 31.4% |
| Foundations Excavated | 64 | 64 | 100.0% |
| Foundations Poured | 64 | 64 | 100.0% |
| Foundations Backfilled | 64 | 64 | 100.0% |
| Crane Pads Completed | 64 | 64 | 100.0% |
| Tower Base Sections Erected | 64 | 64 | 100.0% |
| Tower Mid Sections Erected | 64 | 64 | 100.0% |
| Tower Top Sections Erected | 64 | 64 | 100.0% |
| Nacelles Installed | 64 | 64 | 100.0% |
| Rotors Installed | 64 | 64 | 100.0% |
| Tower Wiring Complete | 64 | 64 | 100.0% |
| Mechanically Complete | 64 | 64 | 100.0% |
| Pre-Commissioned | 24 | 64 | 37.5% |
| Commissioned | 39 | 64 | 60.9% |
| 4/0 Cable Trenched | 149,724 | 149,724 | 100.0% |
| 500 Cable Trenched | 13,965 | 13,965 | 100.0% |
| 1000 Cable Trenched | 76,996 | 76,996 | 100.0% |
| Transformers Set/Terminated | 64 | 64 | 100.0% |

(as of COB yesterday)



Plan of the Day (POD)

Date: Thursday, 11-11-10
High: 41
Precipitation Chances: 5 %

COD: 11-30-10
Low: 19

Days to COD: 21
Winds: WNW @ 15 mph
Weather Forecast: Mostly Cloudy

NextEra™ Energy Resources

Blattner Energy

Paradigm

GE

Safety/Environmental:

- Areas of the site are energized
- Stay focused on task at hand

Civil/Erection:

- Reclaim at 3-4

Foundations: Complete

Collection:

Electrical:

- Mechanical completion pre-walk complete

- IIP at 4

- GE Commissioning at 11, 13 & 14

Substation:

- Final rock work

- Wiring to static mast at Wilton II

- Dress up entrance into Wilton II Sub



RECEIVING (As of COB yesterday)

| | Total | Received | Balance |
|-----------------|---------|----------|---------|
| PMT XFR | 65 | 65 | 0 |
| Grounding XFR | 6 | 6 | 0 |
| 4/0 Cable | 519,519 | 500,688 | 18831 |
| 500 KCM | 51,002 | 58,397 | -7395 |
| Copperclad | 65,280 | 73,906 | -8626 |
| 1000 KCM | 254,661 | 296,079 | -41418 |
| 1000 KCM LVC | 24,000 | 38,230 | -14230 |
| 12 Fiber SM FOC | 289,504 | 294,530 | -5026 |
| XFR Box Pads | 64 | 64 | 0 |
| Controllers | 64 | 64 | 0 |
| Bases | 64 | 64 | 0 |
| Mids | 64 | 64 | 0 |
| Tops | 64 | 64 | 0 |
| Nacelles | 64 | 64 | 0 |
| Hubs | 64 | 64 | 0 |
| Blade Sets | 64 | 64 | 0 |

Negative Number Indicates Overage of Cable

General Construction Status

| | Complete | Total | % Complete |
|-----------------------------|----------|---------|------------|
| Roads Subgraded | 76,066 | 76,066 | 100.0% |
| Roads Built | 76,066 | 76,066 | 100.0% |
| Silt Fence Installed | 3,584 | 11,417 | 31.4% |
| Foundations Excavated | 64 | 64 | 100.0% |
| Foundations Poured | 64 | 64 | 100.0% |
| Foundations Backfilled | 64 | 64 | 100.0% |
| Crane Pads Completed | 64 | 64 | 100.0% |
| Tower Base Sections Erected | 64 | 64 | 100.0% |
| Tower Mid Sections Erected | 64 | 64 | 100.0% |
| Tower Top Sections Erected | 64 | 64 | 100.0% |
| Nacelles Installed | 64 | 64 | 100.0% |
| Rotors Installed | 64 | 64 | 100.0% |
| Tower Wiring Complete | 64 | 64 | 100.0% |
| Mechanically Complete | 63 | 64 | 98.4% |
| Pre-Commissioned | 24 | 64 | 37.5% |
| Commissioned | 39 | 64 | 60.9% |
| 4/0 Cable Trenched | 149,724 | 149,724 | 100.0% |
| 500 Cable Trenched | 13,965 | 13,965 | 100.0% |
| 1000 Cable Trenched | 76,996 | 76,996 | 100.0% |
| Transformers Set/Terminated | 64 | 64 | 100.0% |

(as of COB yesterday)
