

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Friday, 11-19-10
High: 23
Precipitation Chances: 20 %

COD: 11-30-10
Low: 6

Days to COD: 12
Winds: NW @ 16 mph
Weather Forecast: Partly Cloudy

NextEra™ Energy Resources	Blattner Energy	Paradigm	GE
---------------------------	-----------------	----------	----

- Safety/Environmental:**
- Areas of the site are energized
 - Stay focused on task at hand
- Civil/Erection:**
- Foundations: Complete
- Collection:**
- Electrical:**
- GE Commissioning Complete
- Substation:**

This is the final POD
Baldwin Wind was completed 11-18-10


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	6	0
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	73,906	-8626
1000 KCM	254,661	296,079	-41418
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	100.0%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	64	64	100.0%
Tower Mid Sections Erected	64	64	100.0%
Tower Top Sections Erected	64	64	100.0%
Nacelles Installed	64	64	100.0%
Rotors Installed	64	64	100.0%
Tower Wiring Complete	64	64	100.0%
Mechanically Complete	64	64	100.0%
Pre-Commissioned	24	24	100.0%
Commissioned	64	64	100.0%
4/0 Cable Trenched	149,724	149,724	100.0%
500 Cable Trenched	13,965	13,965	100.0%
1000 Cable Trenched	76,996	76,996	100.0%
Transformers Set/Terminated	64	64	100.0%

(as of COB yesterday)

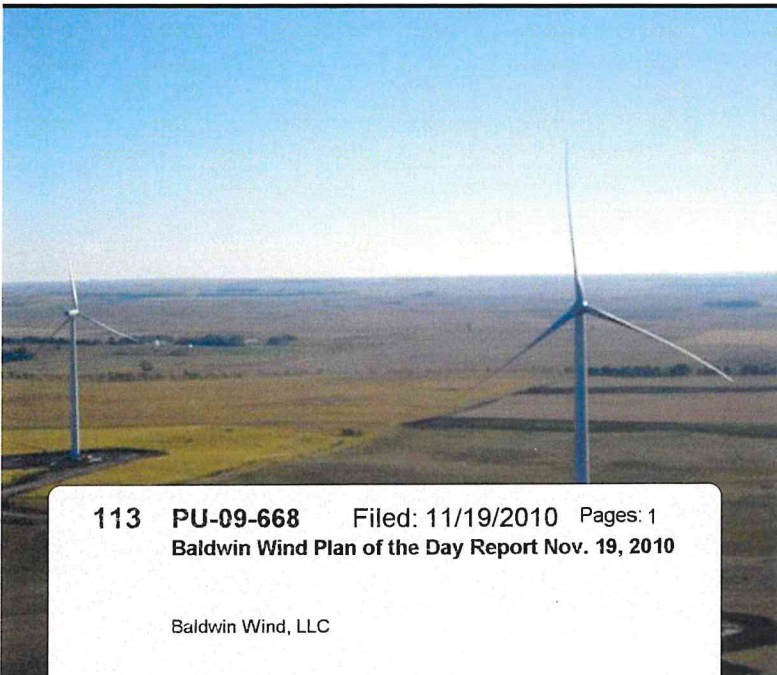

113 PU-09-668 Filed: 11/19/2010 Pages: 1
Baldwin Wind Plan of the Day Report Nov. 19, 2010

Baldwin Wind, LLC
