




NEXtera™ Energy Resources Ashtabula Wind III



NEXtera Energy Plan of the Day (POD)

Date: **Friday, 9-10-10**
 High: **68**
 Precipitation Chances: **60%**

COD: **12-15-10**
 Low: **47**

Days to COD: **97**
 Winds: **S @ 17 mph**
 Weather Forecast: **Cloudy**

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- SWPPP today
- Be cautious of your speeds, obey traffic signs
- Give large trucks the right of way

Civil/Erection:

- No work due to rain

Foundations:

Collection:

Electrical:


Substation:

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	0	3
4/0 Cable	251,642	115,617	136,025
500 KCM	42,438	0	42,438
1000 KCM	265,584	67,633	197,951
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	20	20
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	21,356	68,421	31.2%
Roads Complete	0	68,421	0.0%
Silt Fence Installed	19,706	55,716	35.4%
Foundations Excavated	9	39	23.1%
Foundations Poured	0	39	0.0%
Foundations Backfilled	0	39	0.0%
Crane Pads Completed	0	39	0.0%
Tower Base Sections Erected	0	39	0.0%
Tower Mid Sections Erected	0	39	0.0%
Tower Top Sections Erected	0	39	0.0%
Nacelles Installed	0	39	0.0%
Rotors Installed	0	39	0.0%
Tower Wiring Complete	0	39	0.0%
Mechanically Complete	0	80	0.0%
Mechanically Complete	0	39	0.0%
Pre-Commissioned	0	39	0.0%
Final Commissioned	0	39	0.0%
4/0 Cable Trenched	0	251,642	0.0%
500 Cable Trenched	0	42,438	0.0%
1000 Cable Trenched	12,113	265,584	4.6%
1250 Cable Trenched	0	85,568	0.0%
Fiber Optic 12 Fiber SM	0	211,602	0.0%
Transformers Set/Terminated	0	39	0.0%
(as of COB yesterday)			

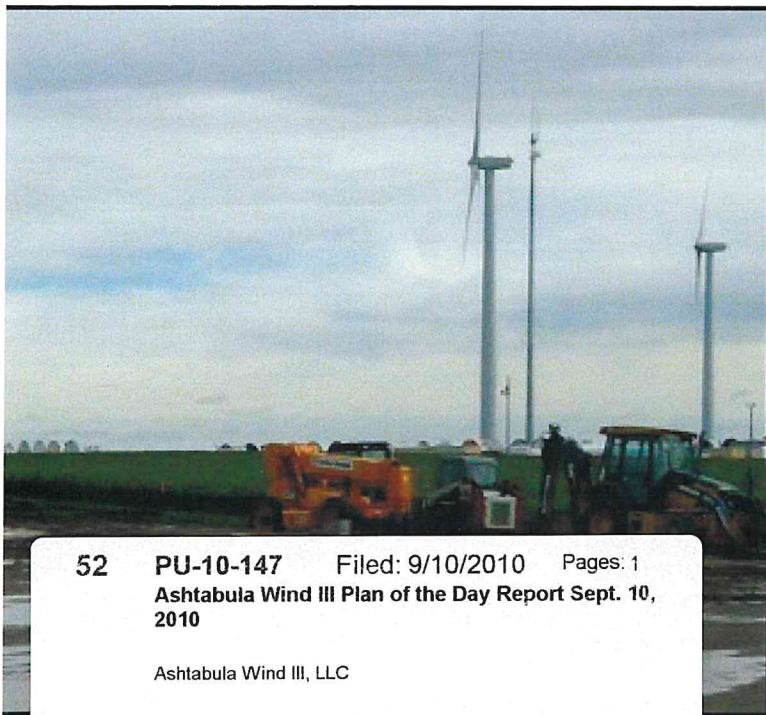

52 PU-10-147 Filed: 9/10/2010 Pages: 1
 Ashtabula Wind III Plan of the Day Report Sept. 10, 2010

Ashtabula Wind III, LLC
