

**NEXTer Energy**  
**Plan of the Day (POD)**

Date: Friday, 10-1-10  
 High: 62  
 Precipitation Chances: 0 %

COD: 12-15-10  
 Low: 34

Days to COD: 76  
 Winds: NNW @ 12 mph  
 Weather Forecast: Mostly Sunny

**NEXTer<sup>TM</sup> Energy Resources    Otter Tail    Blattner Energy    GE**

**Safety/Environmental:**

- Keep yard picked up
- Prevent slips, trips & falls

**Civil/Erection:**

- Gravel at 272-279

**Foundations:**

- Foundation excavation at 272-273
- Pour mud mat at 272-273
- Install bottom rebar mat at 275-276
- Install anchor bolts at 276-277
- Install top rebar mat at 278-279
- Form base at 278-279
- Pour base at 280-281
- Form pedestal at 282-283
- Pour pedestal at 255 & 264
- Backfill at 259 & 267
- Build crane pads at 248-250

**Collection:**

- Trench and install 1000 at 267-268 & north to Hwy 26
- Cable splicing at SP1105, SP1106, SP1205 & SP1206

**Electrical:**

- Pedestal conduit at 282-283
- Smurf tube at 278-279
- Grounding grid at 256, 268 & 276-277
- Install PMT at 251-253 & 266

**Substation:**


- Installing conduit from Sibley Sub to white house
- Installing trench cable

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	0	3
4/0 Cable	251,642	122,687	128,955
500 KCM	42,438	31,163	11,275
1000 KCM	265,584	221,710	43,874
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	20	20
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

**General Construction Status**

	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	25,128	44,274	56.8%
Silt Fence Installed	19,706	55,716	35.4%
Foundations Excavated	34	39	87.2%
Foundations Poured	22	39	56.4%
Foundations Backfilled	15	39	38.5%
Crane Pads Completed	0	39	0.0%
Tower Base Sections Erected	0	39	0.0%
Tower Mid Sections Erected	0	39	0.0%
Tower Top Sections Erected	0	39	0.0%
Nacelles Installed	0	39	0.0%
Rotors Installed	0	39	0.0%
Tower Wiring Complete	0	39	0.0%
Mechanically Complete	0	80	0.0%
Mechanically Complete	0	39	0.0%
Pre-Commissioned	0	39	0.0%
Final Commissioned	0	39	0.0%
4/0 Cable Trenched	89,721	251,642	35.7%
500 Cable Trenched	0	42,438	0.0%
1000 Cable Trenched	200,208	265,584	75.4%
1250 Cable Trenched	0	85,568	0.0%
Fiber Optic 12 Fiber SM	0	211,602	0.0%
Transformers Set/Terminated	0	39	0.0%
(as of COB yesterday)			

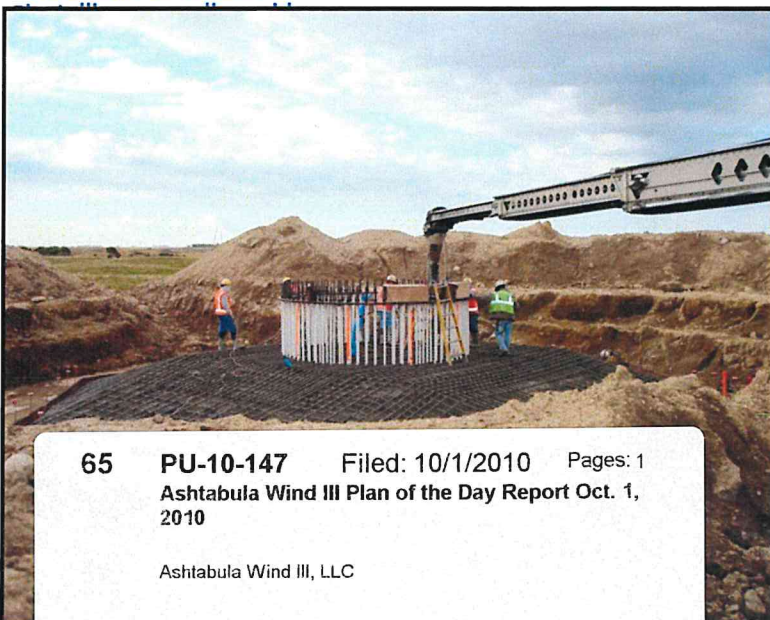

65    PU-10-147    Filed: 10/1/2010    Pages: 1  
 Ashtabula Wind III Plan of the Day Report Oct. 1, 2010

Ashtabula Wind III, LLC
