




# NEXTer<sup>TM</sup> Energy Resources Ashtabula Wind III

## NEXTer<sup>TM</sup> Energy Plan of the Day (POD)



Date: Thursday, 10-7-10  
High: 79  
Precipitation Chances: 0 %

COD: 12-15-10  
Low: 47

Days to COD: 70  
Winds: S @ 9 mph  
Weather Forecast: Mostly Sunny

### NEXTer<sup>TM</sup> Energy Resources    Otter Tail    Blattner Energy    GE

**Safety/Environmental:**

- One way traffic for heavy hauling on 21<sup>st</sup> ST

- Beware of pinch points

**Civil/Erection:**

- Gravel at 269-270

**Foundations:**

- Foundation excavation at 270
- Install bottom rebar mat at 269
- Install anchor bolts at 269
- Install top rebar mat at 269 & 271
- Form base at 269 271
- Pour base at 272-273
- Form pedestal at 274-275
- Pour pedestal at 276-277
- Backfill at 257-258

**Collection:**

- Trench and install 1000 at South to 20<sup>th</sup> St & West to F11 & F12
- Trench and install 4/0 at 264 East
- Cable splicing at SP1110 & SP1210
- Boring 17-18

**Electrical:**

- Pedestal conduit at 274-275
- Smurf tube at 269, 278 & 279
- Grounding grid at 273-274 & 282-283
- Install box pads at 254-256
- Install PMT at 253 & 259

**Substation:**


- Install high side breaker
- Install underground conduit
- Install grounding grid
- Surface rock

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	0	3
4/0 Cable	251,642	151,951	99,691
500 KCM	42,438	37,397	5,041
1000 KCM	265,584	231,901	33,683
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	37,261	44,274	84.2%
Silt Fence Installed	19,706	55,716	35.4%
Foundations Excavated	38	39	97.4%
Foundations Poured	30	39	76.9%
Foundations Backfilled	22	39	56.4%
Crane Pads Completed	14	39	35.9%
Tower Base Sections Erected	0	39	0.0%
Tower Mid Sections Erected	0	39	0.0%
Tower Top Sections Erected	0	39	0.0%
Nacelles Installed	0	39	0.0%
Rotors Installed	0	39	0.0%
Tower Wiring Complete	0	39	0.0%
Mechanically Complete	0	80	0.0%
Mechanically Complete	0	39	0.0%
Pre-Commissioned	0	39	0.0%
Final Commissioned	0	39	0.0%
4/0 Cable Trenched	105,243	251,642	41.8%
500 Cable Trenched	0	42,438	0.0%
1000 Cable Trenched	218,760	265,584	82.4%
1250 Cable Trenched	0	85,568	0.0%
Fiber Optic 12 Fiber SM	0	211,602	0.0%
Transformers Set	8	39	20.5%
(as of COB yesterday)			

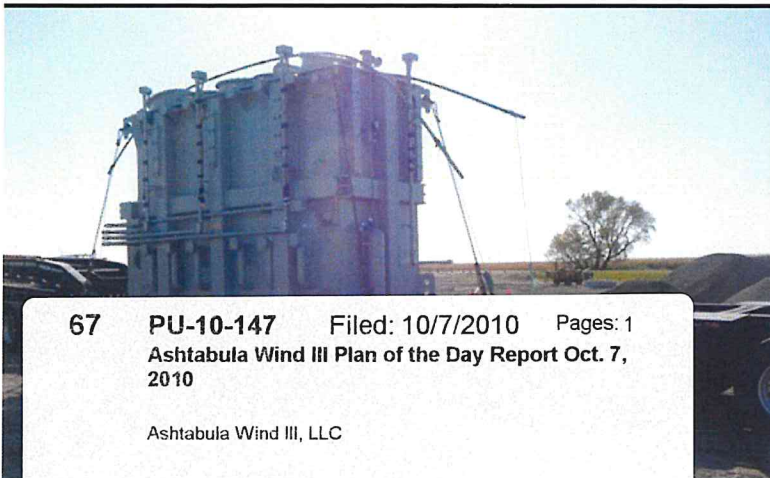

67 PU-10-147 Filed: 10/7/2010 Pages: 1  
Ashtabula Wind III Plan of the Day Report Oct. 7, 2010

Ashtabula Wind III, LLC
