




NEXTerTM Energy Resources Ashtabula Wind III



NEXTer Energy Plan of the Day (POD)

Date: Friday, 10-8-10
High: 83
Precipitation Chances: 25 %

COD: 12-15-10
Low: 40

Days to COD: 69
Winds: ESE @ 6 mph
Weather Forecast: Partly Sunny

NEXTerTM Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- One way traffic for heavy hauling on 21st ST
- Be careful around cranes

Civil/Erection:

- Gravel at 269-270

Foundations:

- Foundation excavation at 270
- Install bottom rebar mat at 270
- Pour base at 269 & 271
- Form pedestal at 272-273
- Pour pedestal at 274-275
- Build crane pads at 254, 256, 267 & 268

Collection:

- Trench and install 1000 at South to 20th St & West to F11 & F12
- Trench and install 4/0 at 264 East
- Cable splicing at SP1110, SP1111, SP1112 & SP1211
- Boring 18-19
- Low voltage cable termination at 249

Electrical:

- Pedestal conduit at 272-273
- Grounding grid at 277-278
- Install box pads at 254-256, 262 & 264
- Install PMT at 260-261

Substation:

- Install high side breaker
- Install underground conduit
- Install grounding grid
- Surface rock


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	0	3
4/0 Cable	251,642	173,852	77,790
500 KCM	42,438	37,397	5,041
1000 KCM	265,584	234,933	30,651
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	37,261	44,274	84.2%
Silt Fence Installed	19,706	55,716	35.4%
Foundations Excavated	38	39	97.4%
Foundations Poured	32	39	82.1%
Foundations Backfilled	24	39	61.5%
Crane Pads Completed	14	39	35.9%
Tower Base Sections Erected	0	39	0.0%
Tower Mid Sections Erected	0	39	0.0%
Tower Top Sections Erected	0	39	0.0%
Nacelles Installed	0	39	0.0%
Rotors Installed	0	39	0.0%
Tower Wiring Complete	0	39	0.0%
Mechanically Complete	0	80	0.0%
Mechanically Complete	0	39	0.0%
Pre-Commissioned	0	39	0.0%
Final Commissioned	0	39	0.0%
4/0 Cable Trenched	117,783	251,642	46.8%
500 Cable Trenched	0	42,438	0.0%
1000 Cable Trenched	228,936	265,584	86.2%
1250 Cable Trenched	0	85,568	0.0%
Fiber Optic 12 Fiber SM	0	211,602	0.0%
Transformers Set	10	39	25.6%

(as of COB yesterday)

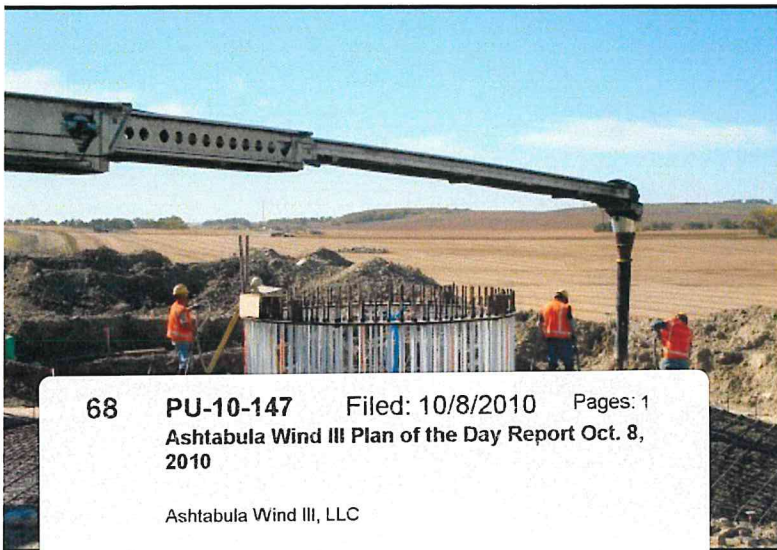

68 PU-10-147 Filed: 10/8/2010 Pages: 1
Ashtabula Wind III Plan of the Day Report Oct. 8, 2010

Ashtabula Wind III, LLC
