




NEXTerTM Energy Resources Ashtabula Wind III



NEXTerTM Energy Plan of the Day (POD)

Date: Friday, 10-22-10
High: 65
Precipitation Chances: 0 %

COD: 12-15-10
Low: 33

Days to COD: 55
Winds: NNW @ 7 mph
Weather Forecast: Sunny

NEXTerTM Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Make a pre-trip to look for power lines before moving cranes
- SWPPP Inspection

Civil/Erection:

- Erect base at 247
- Erect mid at 247
- Assemble rotor at 247
- Erect top & nacelle at 245
- Erect rotor at 245 & 248

Foundations:

- Backfill at 269
- Build crane pad at 274-275


Collection:

- Trench and install 4/0 at JB 102 to bore 36 & 279
- Trench and install 500 at 275 East, JB 102 to Bore 36
- Cable splicing at SP1202
- Cable termination LV at 249, 253 & HV at 246, 248-249
- Boring at 28-29
- Fiber termination at 258-262

Electrical:

Substation:

- Installing substation steel

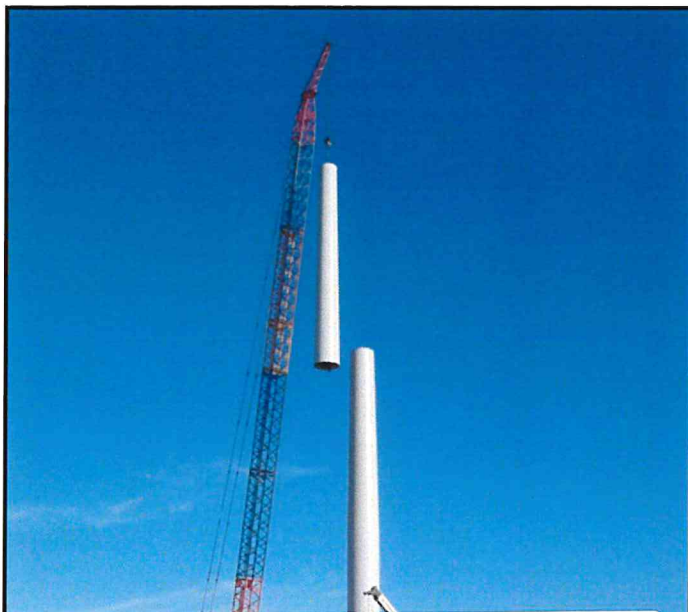

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	3	0
4/0 Cable	251,642	268,753	-17,111
500 KCM	42,438	46,661	-4,223
1000 KCM	265,584	234,933	30,651
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status			
	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	44,274	44,274	100.0%
Silt Fence Installed	19,851	55,716	35.6%
Foundations Excavated	39	39	100.0%
Foundations Poured	39	39	100.0%
Foundations Backfilled	38	39	97.4%
Crane Pads Completed	31	39	79.5%
Tower Base Sections Erected	5	39	12.8%
Tower Mid Sections Erected	5	39	12.8%
Tower Top Sections Erected	2	39	5.1%
Nacelles Installed	2	39	5.1%
Rotors Installed	2	39	5.1%
Tower Wiring Complete	0	39	0.0%
Mechanically Complete	0	80	0.0%
Mechanically Complete	0	39	0.0%
Pre-Commissioned	0	39	0.0%
Final Commissioned	0	39	0.0%
4/0 Cable Trenched	163,533	251,642	65.0%
500 Cable Trenched	14,346	42,438	33.8%
1000 Cable Trenched	236,514	265,584	89.1%
1250 Cable Trenched	38,382	85,568	44.9%
Fiber Optic 12 Fiber SM	126,644	211,602	59.9%
Transformers Set	24	39	61.5%

(as of COB yesterday)
