



NEXTerTM Energy Resources Ashtabula Wind III



NEXTer Energy Plan of the Day (POD)

Date: Thursday, 10-28-10
High: 36
Precipitation Chances: 0 %

COD: 12-15-10
Low: 21

Days to COD: 50
Winds: WNW @ 12 mph
Weather Forecast: Partly Sunny

NEXTerTM Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Be aware of changing weather conditions
- Dress appropriately for the weather

Civil/Erection:

- Erect base & mid at 252-253
- Assemble rotor at 251-253
- Erect top, nacelle & rotor at 251

Foundations:

Collection:

- Trench and install 4/0 at 278-279
- Trench and install 1250 at 120th Ave to JB102
- Terminating HV & LV cable at 266-268

Electrical:

- Tower wiring at 248
- Mechanical completion pre-walk at 249
- IIP at 250
- Controller to DTA termination at 266-268
- Box pad installation at 269-271

Substation:


- Installing substation steel
- Welding bus
- Working on above grade conduit
- Installing insulators

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	3	0
4/0 Cable	251,642	276,103	-24,461
500 KCM	42,438	46,661	-4,223
1000 KCM	265,584	256,746	8,838
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	44,274	44,274	100.0%
Silt Fence Installed	19,851	55,716	35.6%
Foundations Excavated	39	39	100.0%
Foundations Poured	39	39	100.0%
Foundations Backfilled	39	39	100.0%
Crane Pads Completed	36	39	92.3%
Tower Base Sections Erected	7	39	17.9%
Tower Mid Sections Erected	7	39	17.9%
Tower Top Sections Erected	6	39	15.4%
Nacelles Installed	6	39	15.4%
Rotors Installed	6	39	15.4%
Tower Wiring Complete	2	39	5.1%
Mechanically Complete	0	80	0.0%
Mechanically Complete	0	39	0.0%
Pre-Commissioned	0	39	0.0%
Final Commissioned	0	39	0.0%
4/0 Cable Trenched	173,625	251,642	69.0%
500 Cable Trenched	29,652	42,438	69.9%
1000 Cable Trenched	236,514	265,584	89.1%
1250 Cable Trenched	47,880	85,568	56.0%
Fiber Optic 12 Fiber SM	126,644	211,602	59.9%
Transformers Set	26	39	66.7%
(as of COB yesterday)			

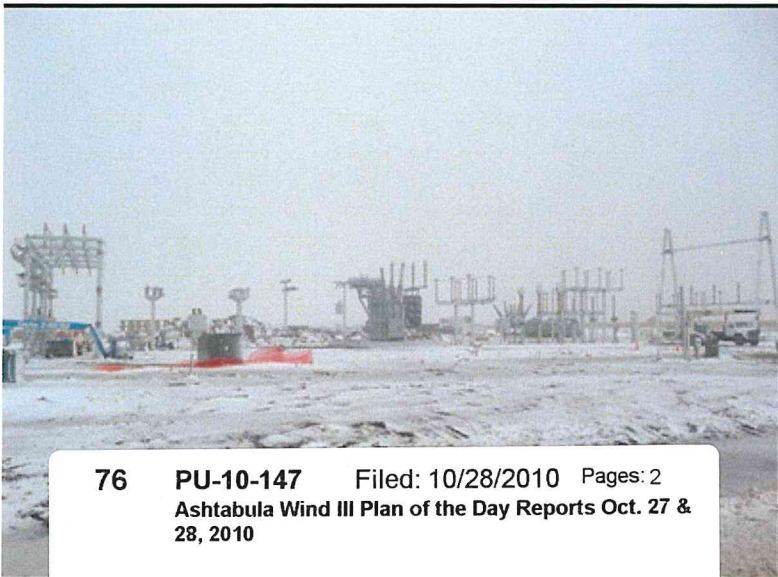

76 PU-10-147 Filed: 10/28/2010 Pages: 2
Ashtabula Wind III Plan of the Day Reports Oct. 27 & 28, 2010

Ashtabula Wind III, LLC



NEXtera™ Energy Resources Ashtabula Wind III



NEXtera Energy

Plan of the Day (POD)

Date: Wednesday, 10-27-10
High: 38
Precipitation Chances: 100 %

COD: 12-15-10
Low: 19

Days to COD: 51
Winds: WNW @ 34 mph
Weather Forecast: Cloudy

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Be aware of changing weather conditions
- Be cautious of strong winds and slippery roads

Civil/Erection:

Foundations:

Collection:

Electrical:

Substation:

- No work due to Winter Storm

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	3	0
4/0 Cable	251,642	276,103	-24,461
500 KCM	42,438	46,661	-4,223
1000 KCM	265,584	256,746	8,838
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	44,274	44,274	100.0%
Silt Fence Installed	19,851	55,716	35.6%
Foundations Excavated	39	39	100.0%
Foundations Poured	39	39	100.0%
Foundations Backfilled	39	39	100.0%
Crane Pads Completed	36	39	92.3%
Tower Base Sections Erected	7	39	17.9%
Tower Mid Sections Erected	7	39	17.9%
Tower Top Sections Erected	6	39	15.4%
Nacelles Installed	6	39	15.4%
Rotors Installed	6	39	15.4%
Tower Wiring Complete	1	39	2.6%
Mechanically Complete	0	80	0.0%
Mechanically Complete	0	39	0.0%
Pre-Commissioned	0	39	0.0%
Final Commissioned	0	39	0.0%
4/0 Cable Trenched	173,625	251,642	69.0%
500 Cable Trenched	29,652	42,438	69.9%
1000 Cable Trenched	236,514	265,584	89.1%
1250 Cable Trenched	47,880	85,568	56.0%
Fiber Optic 12 Fiber SM	126,644	211,602	59.9%
Transformers Set	26	39	66.7%

(as of COB yesterday)

