




# NEXtera™ Energy Resources Ashtabula Wind III



## NEXtera Energy

### Plan of the Day (POD)

Date: Tuesday, 11-9-10  
High: 58  
Precipitation Chances: 5 %

COD: 12-15-10  
Low: 35

Days to COD: 37  
Winds: ESE @ 9 mph  
Weather Forecast: Partly Sunny

#### NEXtera™ Energy Resources    Otter Tail    Blattner Energy    GE

**Safety/Environmental:**

- Secure your load
- Use caution when traveling in congested areas

**Civil/Erection:**

- Erect base & mid at 266 & 282
- Assemble rotor at 265-266 & 282
- Erect top, nacelle & rotor at 283-284

**Foundations:**

**Collection:**

- Trench and install 1250 cable South of substation
- Fiber termination – test F10 & F11 home runs
- Terminating HV cable at 271-272 & 276-277
- Terminating LV cable at 270 & 277-279

**Electrical:**

- Tower wiring at 262
- DTA to Controller termination at 269 & 179
- Mechanical completion pre-walk at 260-261
- IIP at 259
- GE pre-commissioning at 249-250

**Substation:**


- Grounding steel & fence
- Working on high side jumpers and switches
- Working on above grade conduit
- Pulling in control wires
- Start setting up for load bank

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	3	0
4/0 Cable	251,642	276,103	-24,461
500 KCM	42,438	46,661	-4,223
1000 KCM	265,584	256,746	8,838
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	44,274	44,274	100.0%
Silt Fence Installed	19,851	55,716	35.6%
Foundations Excavated	39	39	100.0%
Foundations Poured	39	39	100.0%
Foundations Backfilled	39	39	100.0%
Crane Pads Completed	39	39	100.0%
Tower Base Sections Erected	20	39	51.3%
Tower Mid Sections Erected	20	39	51.3%
Tower Top Sections Erected	16	39	41.0%
Nacelles Installed	16	39	41.0%
Rotors Installed	16	39	41.0%
Tower Wiring Complete	15	39	38.5%
Mechanically Complete	12	39	30.8%
Pre-Commissioned	1	39	2.6%
Commissioned	0	39	0.0%
4/0 Cable Trenched	180,864	251,642	71.9%
500 Cable Trenched	44,508	42,438	104.9%
1000 Cable Trenched	236,514	265,584	89.1%
1250 Cable Trenched	71,592	85,568	83.7%
Fiber Optic 12 Fiber SM	126,644	211,602	59.9%
Transformers Set	39	39	100.0%
(as of COB yesterday)			

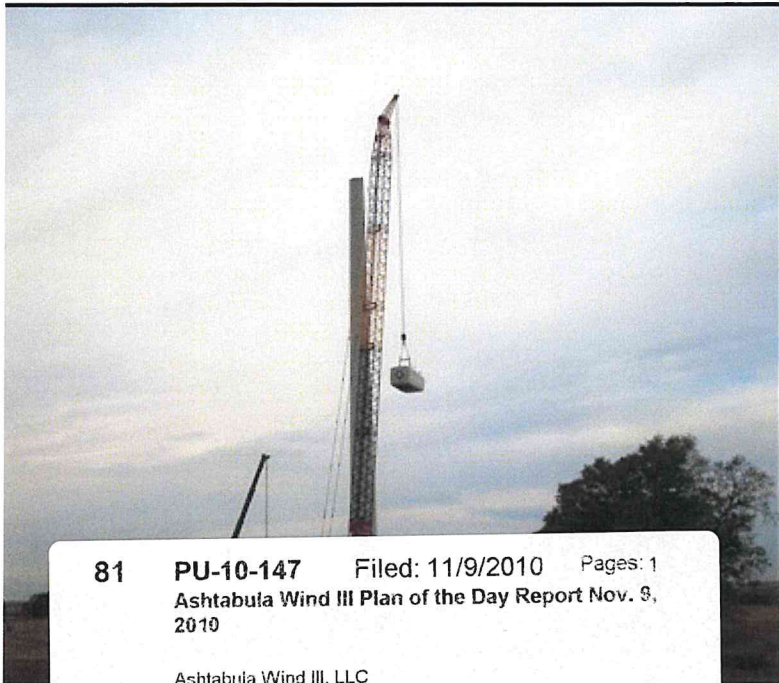

81    PU-10-147    Filed: 11/9/2010    Pages: 1  
Ashtabula Wind III Plan of the Day Report Nov. 9, 2010

Ashtabula Wind III, LLC
