



NEXtera™ Energy Resources Ashtabula Wind III



NEXtera Energy Plan of the Day (POD)

Date: Thursday, 11-18-10
High: 34
Precipitation Chances: 0 %

COD: 12-15-10
Low: 14

Days to COD: 28
Winds: SSE @ 18 mph
Weather Forecast: Mostly Cloudy

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Watch for deer
- Keep headlights on

Civil/Erection:

- Reclaim at 263-266
- Erect mid at 269
- Assemble rotor at 269 & 271
- Erect top, nacelle & rotor at 269 & 272

Foundations:

Collection:

Electrical:

- Tower wiring at 273-274
- Mechanical completion pre-walk at 274-275
- IIP at 257-258 & 277-278
- GE pre-commissioning at 259 & 263
- GE commissioning at 247-248, 250 & 252

Substation:

- Grounding steel, fence & switches
- Terminating control wires
- Working on high side jumpers


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	3	0
4/0 Cable	251,642	276,103	-24,461
500 KCM	42,438	46,661	-4,223
1000 KCM	265,584	256,746	8,838
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	44,274	44,274	100.0%
Silt Fence Installed	19,851	55,716	35.6%
Foundations Excavated	39	39	100.0%
Foundations Poured	39	39	100.0%
Foundations Backfilled	39	39	100.0%
Crane Pads Completed	39	39	100.0%
Tower Base Sections Erected	38	39	97.4%
Tower Mid Sections Erected	37	39	94.9%
Tower Top Sections Erected	35	39	89.7%
Nacelles Installed	35	39	89.7%
Rotors Installed	35	39	89.7%
Tower Wiring Complete	33	39	84.6%
Mechanically Complete	22	39	56.4%
Pre-Commissioned	12	39	30.8%
Commissioned	0	39	0.0%
4/0 Cable Trenched	180,864	251,642	71.9%
500 Cable Trenched	44,508	42,438	104.9%
1000 Cable Trenched	236,514	265,584	89.1%
1250 Cable Trenched	80,826	85,568	94.5%
Fiber Optic 12 Fiber SM	126,644	211,602	59.9%
Transformers Set	39	39	100.0%

(as of COB yesterday)

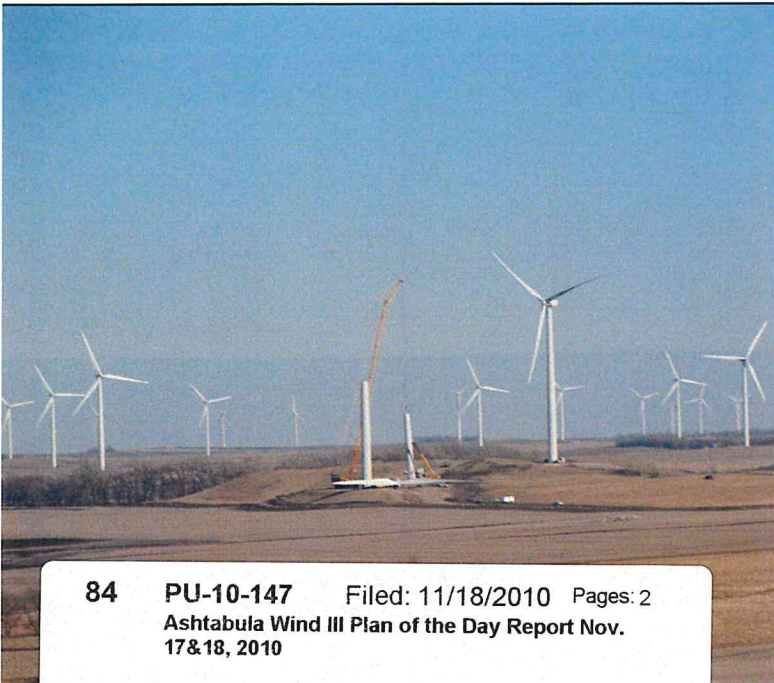

84 PU-10-147 Filed: 11/18/2010 Pages: 2
Ashtabula Wind III Plan of the Day Report Nov.
17 & 18, 2010


Ashtabula Wind III, LLC



NEXtera™ Energy Resources Ashtabula Wind III

NEXtera Energy

Plan of the Day (POD)



Date: Wednesday, 11-17-10
High: 32
Precipitation Chances: 0 %

COD: 12-15-10
Low: 14

Days to COD: 29
Winds: NNW @ 17 mph
Weather Forecast: Mostly Cloudy

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Watch for deer
- Keep headlights on

Civil/Erection:

- Reclaim at 263-266
- Erect base at 271
- Erect mid at 271 & 273
- Assemble rotor at 271 & 273
- Erect top, nacelle & rotor at 273-274

Foundations:

Collection:

Electrical:

- Tower wiring at 275
- Mechanical completion pre-walk at 276-277
- IIP at 278-279 & 281-282
- GE pre-commissioning at 259 & 261-263

Substation:

- Grounding steel, fence & switches
- Terminating control wires
- W

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	3	0
4/0 Cable	251,642	276,103	-24,461
500 KCM	42,438	46,661	-4,223
1000 KCM	265,584	256,746	8,838
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	44,274	44,274	100.0%
Silt Fence Installed	19,851	55,716	35.6%
Foundations Excavated	39	39	100.0%
Foundations Poured	39	39	100.0%
Foundations Backfilled	39	39	100.0%
Crane Pads Completed	39	39	100.0%
Tower Base Sections Erected	36	39	92.3%
Tower Mid Sections Erected	35	39	89.7%
Tower Top Sections Erected	33	39	84.6%
Nacelles Installed	33	39	84.6%
Rotors Installed	33	39	84.6%
Tower Wiring Complete	32	39	82.1%
Mechanically Complete	21	39	53.8%
Pre-Commissioned	11	39	28.2%
Commissioned	0	39	0.0%
4/0 Cable Trenched	180,864	251,642	71.9%
500 Cable Trenched	44,508	42,438	104.9%
1000 Cable Trenched	236,514	265,584	89.1%
1250 Cable Trenched	80,826	85,568	94.5%
Fiber Optic 12 Fiber SM	126,644	211,602	59.9%
Transformers Set	39	39	100.0%

(as of COB yesterday)

