



# NEXTer<sup>TM</sup> Energy Resources Ashtabula Wind III



## NEXTer<sup>TM</sup> Energy Plan of the Day (POD)

Date: **Friday, 11-19-10**  
High: **28**  
Precipitation Chances: **0 %**

COD: **12-15-10**  
Low: **9**

Days to COD: **27**  
Winds: **NW @ 21 mph**  
Weather Forecast: **Mostly Cloudy**

### NEXTer<sup>TM</sup> Energy Resources    Otter Tail    Blattner Energy    GE

**Safety/Environmental:**

- Watch for deer
- Park into the wind
- Keep headlights on

**Civil/Erection:**

- No work today due to high winds

**Foundations:**

**Collection:**

**Electrical:**

- Mechanical completion pre-walk at 273
- GE pre-commissioning at 260, 262, 265 & 266
- GE commissioning at 248, 250 & 255

**Substation:**

- Grounding steel, fence & switches
- Terminating control wires
- Working on high side jumpers


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	3	0
4/0 Cable	251,642	276,103	-24,461
500 KCM	42,438	46,661	-4,223
1000 KCM	265,584	256,746	8,838
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	44,274	44,274	100.0%
Silt Fence Installed	19,851	55,716	35.6%
Foundations Excavated	39	39	100.0%
Foundations Poured	39	39	100.0%
Foundations Backfilled	39	39	100.0%
Crane Pads Completed	39	39	100.0%
Tower Base Sections Erected	38	39	97.4%
Tower Mid Sections Erected	38	39	97.4%
Tower Top Sections Erected	35	39	89.7%
Nacelles Installed	35	39	89.7%
Rotors Installed	35	39	89.7%
Tower Wiring Complete	35	39	89.7%
Mechanically Complete	23	39	59.0%
Pre-Commissioned	15	39	38.5%
Commissioned	8	39	20.5%
4/0 Cable Trenched	180,864	251,642	71.9%
500 Cable Trenched	44,508	42,438	104.9%
1000 Cable Trenched	236,514	265,584	89.1%
1250 Cable Trenched	80,826	85,568	94.5%
Fiber Optic 12 Fiber SM	126,644	211,602	59.9%
Transformers Set	39	39	100.0%

(as of COB yesterday)

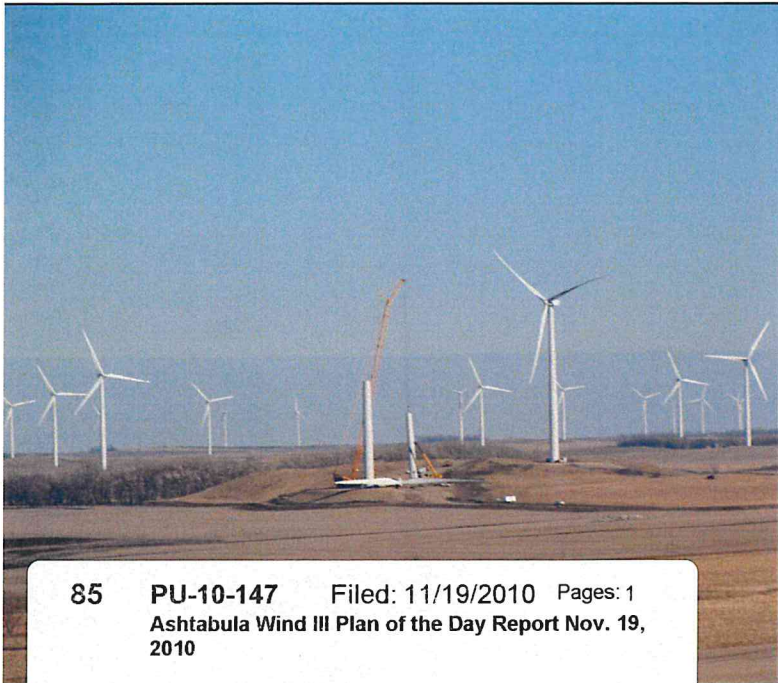

85    PU-10-147    Filed: 11/19/2010    Pages: 1  
Ashtabula Wind III Plan of the Day Report Nov. 19, 2010

Ashtabula Wind III, LLC
