




NEXtera™ Energy Resources Ashtabula Wind III



NEXtera Energy Plan of the Day (POD)

Date: Monday, 11-29-10
High: 32
Precipitation Chances: 0 %

COD: 12-15-10
Low: 15

Days to COD: 17
Winds: S @ 7 mph
Weather Forecast: Partly Sunny

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Keep focused on task at hand
- Watch for slippery surfaces

Civil/Erection:

- Snow removal

Foundations:

Collection:

Electrical:

- GE commissioning at 274 & 276

Substation:


- Working on high side jumpers
- Supporting testers
- Load banking F-10

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	3	0
4/0 Cable	251,642	276,103	-24,461
500 KCM	42,438	46,661	-4,223
1000 KCM	265,584	256,746	8,838
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	44,274	44,274	100.0%
Silt Fence Installed	19,851	55,716	100.0%
Foundations Excavated	39	39	100.0%
Foundations Poured	39	39	100.0%
Foundations Backfilled	39	39	100.0%
Crane Pads Completed	39	39	100.0%
Tower Base Sections Erected	39	39	100.0%
Tower Mid Sections Erected	39	39	100.0%
Tower Top Sections Erected	39	39	100.0%
Nacelles Installed	39	39	100.0%
Rotors Installed	39	39	100.0%
Tower Wiring Complete	39	39	100.0%
Mechanically Complete	39	39	100.0%
Pre-Commissioned	17	39	100.0%
Commissioned	24	39	61.5%
4/0 Cable Trenched	180,864	251,642	100.0%
500 Cable Trenched	44,508	42,438	100.0%
1000 Cable Trenched	236,514	265,584	100.0%
1250 Cable Trenched	80,826	85,568	100.0%
Fiber Optic 12 Fiber SM	126,644	211,602	100.0%
Transformers Set	39	39	100.0%
(as of COB yesterday)			

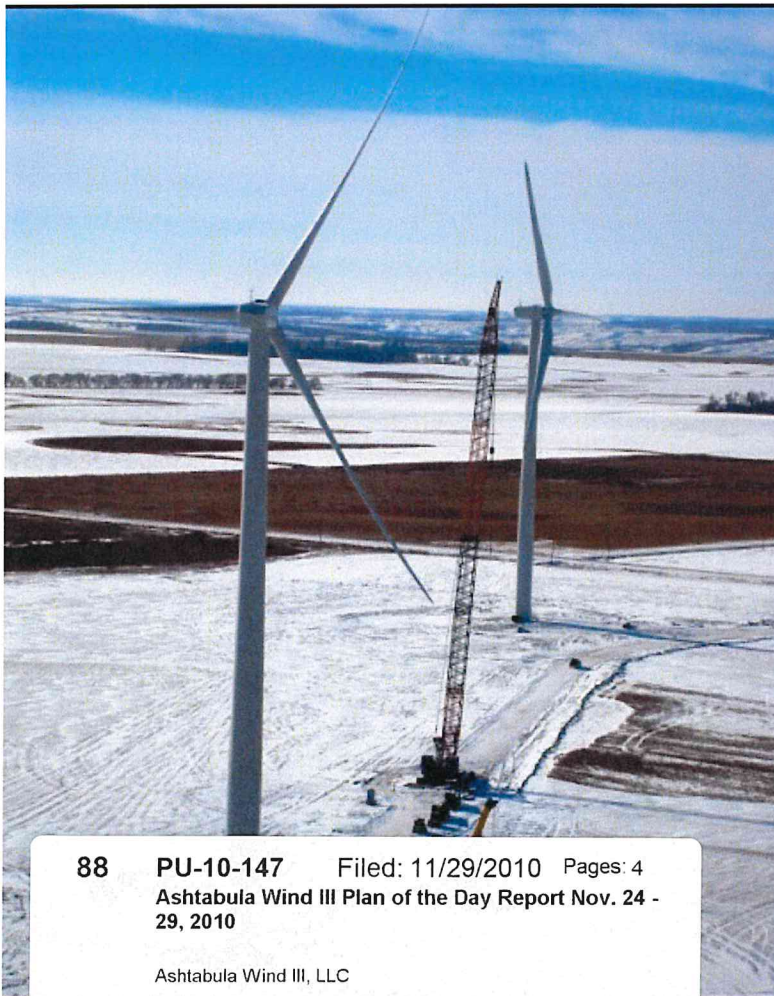


88 PU-10-147 Filed: 11/29/2010 Pages: 4
Ashtabula Wind III Plan of the Day Report Nov. 24 - 29, 2010

Ashtabula Wind III, LLC



NEXtera™ Energy Resources Ashtabula Wind III



NEXtera Energy

Plan of the Day (POD)

Date: **Saturday, 11-27-10**
 High: **32**
 Precipitation Chances: **0 %**

COD: **12-15-10**
 Low: **15**

Days to COD: **19**
 Winds: **S @ 7 mph**
 Weather Forecast: **Partly Sunny**

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Keep focused on task at hand
- Watch for slippery surfaces

Civil/Erection:

- Snow removal

Foundations:

Collection:

Electrical:

- GE gen alignment at 279, 281 & 283
- GE commissioning at 269 & 280-282

Substation:

- Working on high side jumpers
- Supporting testers
- Load banking F-10

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	3	0
4/0 Cable	251,642	276,103	-24,461
500 KCM	42,438	46,661	-4,223
1000 KCM	265,584	256,746	8,838
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status


	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	44,274	44,274	100.0%
Silt Fence Installed	19,851	55,716	100.0%
Foundations Excavated	39	39	100.0%
Foundations Poured	39	39	100.0%
Foundations Backfilled	39	39	100.0%
Crane Pads Completed	39	39	100.0%
Tower Base Sections Erected	39	39	100.0%
Tower Mid Sections Erected	39	39	100.0%
Tower Top Sections Erected	39	39	100.0%
Nacelles Installed	39	39	100.0%
Rotors Installed	39	39	100.0%
Tower Wiring Complete	39	39	100.0%
Mechanically Complete	39	39	100.0%
Pre-Commissioned	17	39	43.6%
Commissioned	20	39	51.3%
4/0 Cable Trenched	180,864	251,642	100.0%
500 Cable Trenched	44,508	42,438	100.0%
1000 Cable Trenched	236,514	265,584	100.0%
1250 Cable Trenched	80,826	85,568	100.0%
Fiber Optic 12 Fiber SM	126,644	211,602	100.0%
Transformers Set	39	39	100.0%

(as of COB yesterday)





NEXtera™ Energy Resources Ashtabula Wind III



NEXtera Energy

Plan of the Day (POD)

Date: Friday, 11-26-10
High: 26
Precipitation Chances: 100 %

COD: 12-15-10
Low: 7

Days to COD: 20
Winds: WNW @ 11 mph
Weather Forecast: Partly cloudy

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Keep focused on task at hand
- Watch for slippery surfaces

Civil/Erection:

- Snow removal

Foundations:

Collection:

Electrical:

- GE gen alignment at 280, 281 & 283
- GE commissioning at 280 & 282

Substation:

- Working on high side jumpers
- Supporting testers
- Load banking F-10

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	3	0
4/0 Cable	251,642	276,103	-24,461
500 KCM	42,438	46,661	-4,223
1000 KCM	265,584	256,746	8,838
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status


	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	44,274	44,274	100.0%
Silt Fence Installed	19,851	55,716	100.0%
Foundations Excavated	39	39	100.0%
Foundations Poured	39	39	100.0%
Foundations Backfilled	39	39	100.0%
Crane Pads Completed	39	39	100.0%
Tower Base Sections Erected	39	39	100.0%
Tower Mid Sections Erected	39	39	100.0%
Tower Top Sections Erected	39	39	100.0%
Nacelles Installed	39	39	100.0%
Rotors Installed	39	39	100.0%
Tower Wiring Complete	39	39	100.0%
Mechanically Complete	39	39	100.0%
Pre-Commissioned	17	39	43.6%
Commissioned	20	39	51.3%
4/0 Cable Trenched	180,864	251,642	100.0%
500 Cable Trenched	44,508	42,438	100.0%
1000 Cable Trenched	236,514	265,584	100.0%
1250 Cable Trenched	80,826	85,568	100.0%
Fiber Optic 12 Fiber SM	126,644	211,602	100.0%
Transformers Set	39	39	100.0%

(as of COB yesterday)





NEXtera™ Energy Resources Ashtabula Wind III



NEXtera Energy

Plan of the Day (POD)

Date: **Wednesday, 11-24-10**
 High: **21**
 Precipitation Chances: **100 %**

COD: **12-15-10**
 Low: **-2**

Days to COD: **22**
 Winds: **SW @ 15 mph**
 Weather Forecast: **Cloudy / Snow**

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Keep focused on task at hand
- Watch for slippery surfaces
- Keep headlights on

Civil/Erection:

Foundations:

Collection:

Electrical:

- IIP at Complete
- FCAT at 266-268
- GE commissioning at 257 & 266-268

Substation:

- Working on high side jumpers
- Supporting testers
- Load banking F-12

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	3	0
4/O Cable	251,642	276,103	-24,461
500 KCM	42,438	46,661	-4,223
1000 KCM	265,584	256,746	8,838
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	44,274	44,274	100.0%
Silt Fence Installed	19,851	55,716	35.6%
Foundations Excavated	39	39	100.0%
Foundations Poured	39	39	100.0%
Foundations Backfilled	39	39	100.0%
Crane Pads Completed	39	39	100.0%
Tower Base Sections Erected	39	39	100.0%
Tower Mid Sections Erected	39	39	100.0%
Tower Top Sections Erected	39	39	100.0%
Nacelles Installed	39	39	100.0%
Rotors Installed	39	39	100.0%
Tower Wiring Complete	39	39	100.0%
Mechanically Complete	39	39	100.0%
Pre-Commissioned	17	39	43.6%
Commissioned	15	39	38.5%
4/O Cable Trenched	180,864	251,642	100.0%
500 Cable Trenched	44,508	42,438	100.0%
1000 Cable Trenched	236,514	265,584	100.0%
1250 Cable Trenched	80,826	85,568	100.0%
Fiber Optic 12 Fiber SM	126,644	211,602	100.0%
Transformers Set	39	39	100.0%

(as of COB yesterday)

