




NEXtera™ Energy Resources Ashtabula Wind III



NEXtera Energy

Plan of the Day (POD)

Date: Tuesday, 11-30-10
High: 18
Precipitation Chances: 40 %

COD: 12-15-10
Low: -2

Days to COD: 16
Winds: NW @ 28 mph
Weather Forecast: Mostly Cloudy

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Keep focused on task at hand
- Watch for slippery surfaces

Civil/Erection:

- Snow removal

Foundations:

Collection:

Electrical:

- GE working on miscellaneous punch list items
- No commissioning due to high winds

Substation:

- Supporting testers
- Load banking F-10


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	3	0
4/O Cable	251,642	276,103	-24,461
500 KCM	42,438	46,661	-4,223
1000 KCM	265,584	256,746	8,838
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	44,274	44,274	100.0%
Silt Fence Installed	19,851	55,716	100.0%
Foundations Excavated	39	39	100.0%
Foundations Poured	39	39	100.0%
Foundations Backfilled	39	39	100.0%
Crane Pads Completed	39	39	100.0%
Tower Base Sections Erected	39	39	100.0%
Tower Mid Sections Erected	39	39	100.0%
Tower Top Sections Erected	39	39	100.0%
Nacelles Installed	39	39	100.0%
Rotors Installed	39	39	100.0%
Tower Wiring Complete	39	39	100.0%
Mechanically Complete	39	39	100.0%
Pre-Commissioned	17	39	100.0%
Commissioned	26	39	66.7%
4/O Cable Trenched	180,864	251,642	100.0%
500 Cable Trenched	44,508	42,438	100.0%
1000 Cable Trenched	236,514	265,584	100.0%
1250 Cable Trenched	80,826	85,568	100.0%
Fiber Optic 12 Fiber SM	126,644	211,602	100.0%
Transformers Set	39	39	100.0%

(as of COB yesterday)

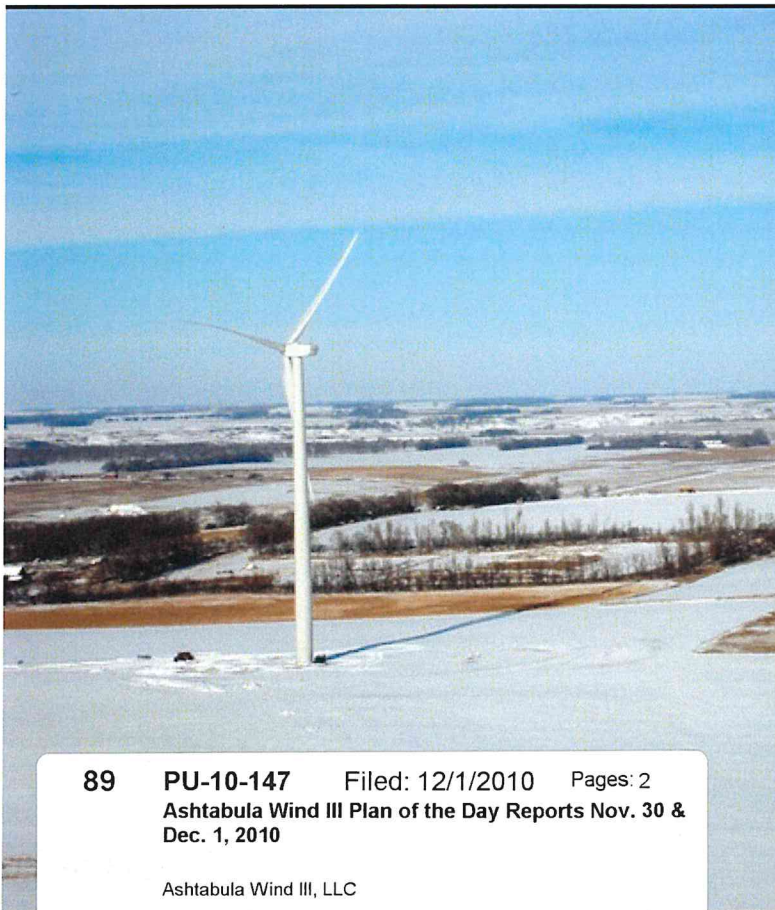


89 PU-10-147 Filed: 12/1/2010 Pages: 2
Ashtabula Wind III Plan of the Day Reports Nov. 30 &
Dec. 1, 2010

Ashtabula Wind III, LLC



NEXtera™ Energy Resources Ashtabula Wind III



NEXtera Energy Plan of the Day (POD)

Date: Wednesday, 12-01-10
High: 16
Precipitation Chances: 50 %

COD: 12-15-10
Low: 0

Days to COD: 15
Winds: W @ 16 mph
Weather Forecast: Mostly Cloudy

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Keep focused on task at hand
- Watch for slippery surfaces

Civil/Erection:

- Snow removal

Foundations:

Collection:

Electrical:

- GE Gen Alignments at 271-273
- GE Commissioning at 275, 278 & 279

Substation:

- Supporting testers
- Load banking F-10

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	3	0
4/0 Cable	251,642	276,103	-24,461
500 KCM	42,438	46,661	-4,223
1000 KCM	265,584	256,746	8,838
1250 KCMIL	85,586	90,696	-5,110
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	40	0
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	44,274	44,274	100.0%
Roads Complete	44,274	44,274	100.0%
Silt Fence Installed	19,851	55,716	100.0%
Foundations Excavated	39	39	100.0%
Foundations Poured	39	39	100.0%
Foundations Backfilled	39	39	100.0%
Crane Pads Completed	39	39	100.0%
Tower Base Sections Erected	39	39	100.0%
Tower Mid Sections Erected	39	39	100.0%
Tower Top Sections Erected	39	39	100.0%
Nacelles Installed	39	39	100.0%
Rotors Installed	39	39	100.0%
Tower Wiring Complete	39	39	100.0%
Mechanically Complete	39	39	100.0%
Pre-Commissioned	17	39	100.0%
Commissioned	28	39	71.8%
4/0 Cable Trenched	180,864	251,642	100.0%
500 Cable Trenched	44,508	42,438	100.0%
1000 Cable Trenched	236,514	265,584	100.0%
1250 Cable Trenched	80,826	85,568	100.0%
Fiber Optic 12 Fiber SM	126,644	211,602	100.0%
Transformers Set	39	39	100.0%
(as of COB yesterday)			

