

# PLAINS

## ALL AMERICAN PIPELINE, L.P.

### Weekly Construction Progress Report


Case # **PU-10-630**  
 Project: **Bakken North Project**  
 Week Ending: 7/15/2012

Report # 8

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Jim Fleetwood	Plains Pipeline	307-472-9911	307-315-0574
Project Coordinator	Ron McCreery	Plains Pipeline	701-694-4414	406-765-8119
Contractor Spread	Mike Bondurant	Tomahawk	406-789-2380	406-789-7024
<b>Brief Description of Week's Activities</b>				
Right of Way (ROW) crew moved to Montana, footage not included in report.				
Environmental continued to check environmental control devices (ECD).				
No safety issues.				
628 welds x-rayed. 19 out of code and repaired. 2.5% rate.				
Installed 11 test lead stations.				
<b>Project Completion Spread</b>				
Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Clear & Grade lft.	151912	Montana	151912	36.20
ROW Finished lft.	161712	Montana	161712	38.60
Stringing lft.	162973	10136	173109	41.30
Welding / X Ray	1899	628	2527	n/a
Ditching	49316	18735	68051	16.2
Lowering In	41340	20280	61620	14.7
Backfill	32208	17600	49808	11.8
Clean-up		3600	3600	n/a
Coating (Welds)	1406	541	1947	n/a
<b>ECDs Installed</b>				
Silt Fence lft.	5511	2977	8488	n/a
Hay bales ea.	256	16	272	n/a
Mats ea.	489	156	645	n/a
Waddles ea.	38	0	38	n/a
Form changed to show footages instead of station numbers.				
<b>Project construction / reclamation activities</b>				
Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Roadway / Bores ea.	9	2	11	n/a
Erosion / Sediment	n/a	n/a		n/a
Topsoil	n/a	n/a		n/a
Restoration/Cleanup	n/a	n/a		n/a
Roadway Restoration	n/a	n/a		n/a
Fence / Gate	n/a	n/a		n/a
Fertilizing / Seeding	n/a	n/a		n/a
<b>Project Site Safety</b>				
Number of Plains/Onshore employees on-site (24), contractor employees (201).				
No equipment or environmental issues.				

Signature: Ron McCreery via e-mail R.M. 7-16-12

Date: 7/16/2012



# PLAINS

ALL AMERICAN  
PIPELINE, L.P.

## Weekly Construction Progress Report

Case # **PU-10-630**

Report # 8

Project: **Bakken North Project**

Week Ending: 7/15/2012

Dates of construction	Startup	Shutdown
	5/22/2012	

Temperature high and low for week.	High	Low
	98°	63°

Landowner / Public Concerns	Addressing Individual	Phone
Mr. Brad Olson	Ms. Cathy Owen (Environmental Inspector)	406-765-8125
Continue to check coulee and water daily.		

**Suspension of project activities (when, where, why, how long)**  
Ditching machine activities suspended due to vandalism. Contractor repairing equipment. Track-hoes used for ditching.

**Identify Cultural Resources not previously identified.**  
n/a

**Critical Habitat or Threatened or Endangered Species.**  
n/a


Cathodic Protection Installed	When	Where
Cathodic Protection test lead stations installed at eleven different locations on main line.		

Special Coordination	Who	When
North Dakota Public Service Commission scheduled to visit.		17-Jul-12

Pipeline in-service date	Date
n/a	



Ditch Line ready for lowering in.

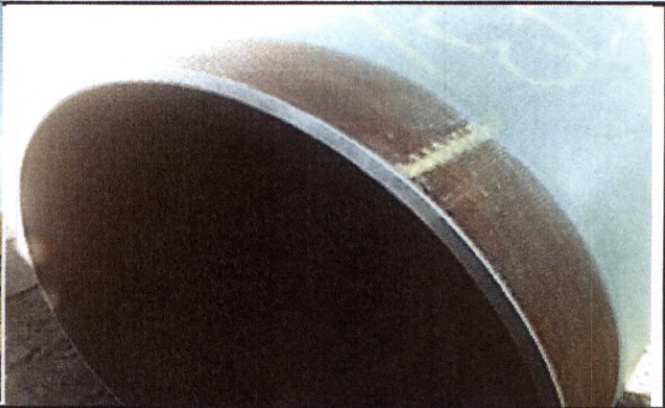


Bevel end ready for line-up and welding.



Pipe lowered in ditch.



Bending machine.

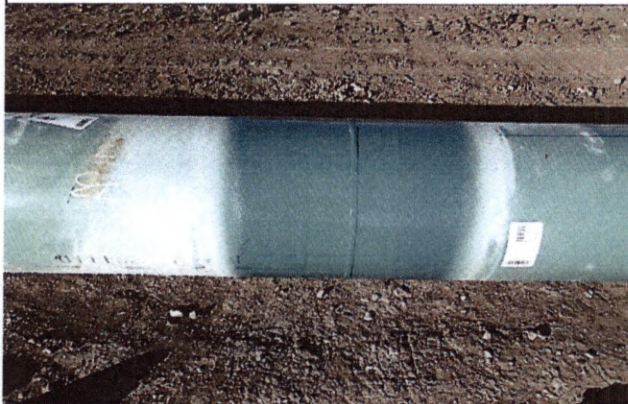

Coated tie-in weld.



Tie in point.

Report Number # 8

Date 7-15-2012
