



PLAINS ALL AMERICAN PIPELINE, L.P.

Weekly Construction Progress Report

Case # **PU-10-630**
 Project: **Bakken North Project**
 Week Ending: 7/29/2012

Report # 10

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Jim Fleetwood	Plains Pipeline	307-472-9911	307-315-0574
Project Coordinator	Ron McCreery	Plains Pipeline	701-694-4414	406-765-8119
Contractor Spread	Mike Bondurant	Tomahawk	406-789-2380	406-789-7024

Brief Description of Week's Activities

Right of Way (ROW) crew and mainline x-ray crew moved to Montana.
 Environmental continued to check environmental control devices (ECD).
 No safety issues.
 61 welds x-rayed by tie-in rig, 4 out of code and repaired. 6.56 % repair rate.
 Installed 7 test lead stations.
 Installed 5 aerial markers.
 Pipe gang and firing line moved to Montana.

Project Completion Spread

Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Clear & Grade lft.	151912	Montana	151912	36.26%
ROW Finished lft.	161712	Montana	161712	38.60%
Stringing lft.	201181	Montana	201181	48.03%
Welding / X Ray	2983	61	3044	n/a
Ditching	78510	35881	114391	27.31%
Lowering In	78731	30544	109275	26.09%
Backfill	68609	30075	98684	23.56%
Clean-up	6227	21854	28081	6.70%
Coating (Welds)	2359	538	2897	n/a

ECDs Installed

Silt Fence lft.	9269	Montana	9269	n/a
Hay bales ea.	320	Montana	320	n/a
Mats ea.	645	Montana	645	n/a
Waddles ea.	38	0	38	n/a

Form changed to show footages instead of station numbers, Total Project Footage **418901**

Project construction / reclamation activities

Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Roadway / Bores ea.	13	2	15	n/a
Erosion / Sediment	n/a	n/a		n/a
Topsoil	n/a	n/a		n/a
Restoration/Cleanup	6227	21854	28081	6.70%
Roadway Restoration	n/a	n/a		n/a
Fence / Gate	n/a	n/a		n/a
Fertilizing / Seeding	n/a	n/a		n/a

Project Site Safety

Number of Plains/Onshore employees on-site (25), contractor employees (210).
 Valve set installation started @ CR 64.
 No environmental issues. Adjusted cribbing to support pipe.

Signature:

Ron McCreery via e-mail *RM*

Date:

7/30/2012



PLAINS

ALL AMERICAN

PIPELINE, L.P.

Weekly Construction Progress Report

Case # PU-10-630
Project: Bakken North Project
Week Ending: 7/29/2012

Report # 10

Dates of construction	Startup	Shutdown
	5/22/2012	

Temperature high and low for week.	High	Low
	98°	68°

Landowner / Public Concerns	Addressing Individual	Phone
Mr. Brad Olson	Ms. Cathy Owen (Environmental Inspector)	406-765-8125
Continue to check coulee and water daily.		

Suspension of project activities (when, where, why, how long)
n/a

Identify Cultural Resources not previously identified.
n/a

Critical Habitat or Threatened or Endangered Species.
n/a


Cathodic Protection Installed	When	Where
Cathodic Protection test lead stations installed at 9 different locations on main line.		

Special Coordination	Who	When
----------------------	-----	------

Pipeline in-service date	Date
n/a	



Pipe to cross under.

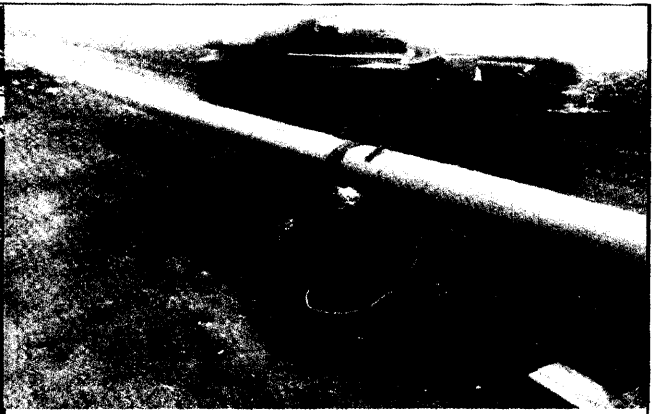


Firing line.



Tied-in pipe and sack breaker.



Pulled bore pipe.

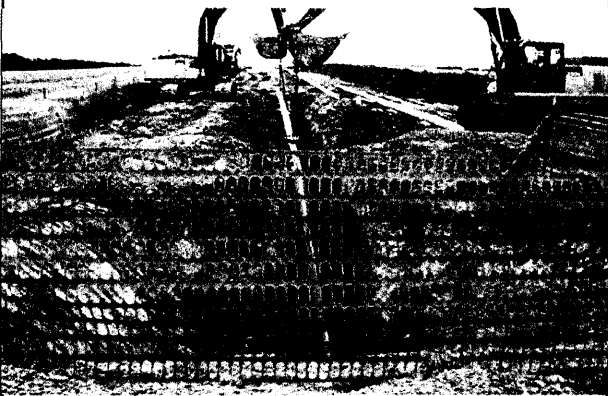

Lowering in pipe.



Tie-in to bore and lowered in pipe.

Report Number: # 10

Date: 7/29/2012
