

**PLAINS**  
ALL AMERICAN  
PIPELINE, L.P.

**Weekly Construction Progress Report**

Case # **PU-10-630**  
Project: **Bakken North Project**  
Week Ending: 8/5/2012

Report # 11

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Jim Fleetwood	Plains Pipeline	307-472-9911	307-315-0574
Project Coordinator	Ron McCreery	Plains Pipeline	701-694-4414	406-765-8119
Contractor Spread	Mike Bondurant	Tomahawk	406-789-2380	406-789-7024
<b>Brief Description of Week's Activities</b>				
Right of Way (ROW) crew and mainline x-ray crew moved to Montana.				
Environmental continued to check environmental control devices (ECD).				
No safety issues.				
50 welds x-rayed by tie-in rig, 2 out of code and repaired. 4 % repair rate.				
Installed 12 test lead stations.				
Installed 3 aerial markers.				
Reseeding has started on pasture land. No footage as of yet.				
<b>Project Completion Spread</b>				
Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Clear & Grade lft.	151912	Montana	151912	36.26%
ROW Finished lft.	161712	Montana	161712	38.60%
Stringing lft.	201181	Montana	201181	48.03%
Welding / X Ray	2983	50	3033	n/a
Ditching	114391	27869	142260	33.96%
Lowering In	109275	14502	123777	29.55%
Backfill	98684	21500	120184	28.69%
Clean-up	28081	8171	36252	8.65%
Coating (Welds)	2897	15	2912	n/a
<b>ECDs Installed</b>				
Silt Fence lft.	9269	Montana	9269	n/a
Hay bales ea.	320	Montana	320	n/a
Mats ea.	645	Montana	645	n/a
Waddles ea.	38	0	38	n/a
Form changed to show footages instead of station numbers, Total Project Footage				418901
<b>Project construction / reclamation activities</b>				
Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Roadway / Bores ea.	15	0	15	n/a
Erosion / Sediment	n/a	n/a		n/a
Topsoil	n/a	n/a		n/a
Restoration/Cleanup	28081	8171	36252	8.65%
Roadway Restoration	n/a	n/a		n/a
Fence / Gate	n/a	n/a		n/a
Fertilizing / Seeding	n/a			n/a
<b>Project Site Safety</b>				
Number of Plains/Onshore employees on-site (46), contractor employees (243).				
Adjusted cribbing to support pipe.				

Signature: Ron McCreery via e-mail *R.M. 8-6-12*

Date: 8/5/2012



**PLAINS**  
**ALL AMERICAN**  
**PIPELINE, L.P.**

**Weekly Construction Progress Report**

**Case #** PU-10-630

Report # 11

**Project:** Bakken North Project

**Week Ending:** 8/5/2012

Dates of construction	Startup	Shutdown
	5/22/2012	

Temperature high and low for week.	High	Low
	95°	65°

Landowner / Public Concerns	Addressing Individual	Phone
Mr. Brad Olson	Ms. Cathy Owen (Environmental Inspector)	406-765-8125
Continue to check coulee and water daily as necessary.		

**Suspension of project activities (when, where, why ,how long)**  
No activities on 8-3-4-5-2012 due to rain and wet conditions on right of way.

**Identify Cultural Resources not previously identified.**  
n/a

**Critical Habitat or Threatened or Endangered Species.**  
n/a

Cathodic Protection Installed	When	Where
Cathodic Protection test lead stations installed at 12 different locations on main line.		

Special Coordination	Who	When
----------------------	-----	------

Pipeline in-service date	Date
n/a	



Bore pipe tie-in



Prep for lowering in.




Pipe gang welding in at tie-in point



Prep for pipe gang welding



Pipe gang welding pipe

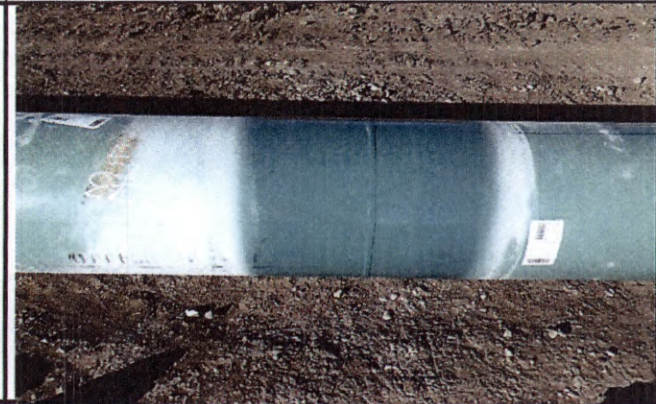

Coated pipe

Report Number # 11

Date 8/5/2012
