



PLAINS
ALL AMERICAN
PIPELINE, L.P.

Weekly Construction Progress Report

Case # **PU-10-630**

Project: **Bakken North Project**

Week Ending: 8/26/2012

Report # 14

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Jim Fleetwood	Plains Pipeline	307-472-9911	307-315-0574
Project Coordinator	Ron McCreery	Plains Pipeline	701-694-4414	406-765-8119
Contractor Spread	Mike Bondurant	Tomahawk	406-789-2380	406-789-7024

Brief Description of Week's Activities
 Right of Way (ROW) crew and mainline x-ray crew moved to Montana. Two ditching machines moved to MT.
 Environmental continued to check environmental control devices (ECD).
 Safety issues. Kids starting School, School buses on roads. Dusty conditions on ROW.
 74 welds x-rayed by tie-in rig, 4 out of code and repaired. 5.41 % repair rate.
 Installed 3 test lead stations.
 21 Line markers installed.
 Reseeding continuing on pasture land.

Project Completion Spread

Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Clear & Grade lft.	151912	Zero work in ND.	151912	100% Completed in ND.
ROW Finished lft.	161712	Zero work in ND.	161712	100% Completed in ND.
Stringing lft.	201181	Zero work in ND.	201181	100% Completed in ND.
Welding / X Ray	3033	74	3107	n/a
Ditching	150346	Completing final ditching at station	150346	35.89%
Lowering In	143344	Completing final lowering in at station	143344	34.22%
Backfill	146784	Completing final backfill at station	146784	35.04%
Clean-up	63853	5700	69553	16.60%
Coating (Welds)	2994	23	3017	n/a
ECDs Installed				
Silt Fence lft.	9269	Zero work in ND.	9269	100% Completed in ND.
Hay bales ea.	320	Zero work in ND.	320	100% Completed in ND.
Mats ea.	645	Zero work in ND.	645	100% Completed in ND.
Waddles ea.	38	Zero work in ND.	38	100% Completed in ND.
Form changed to show footages instead of station numbers, Total Project Footage				418901

Project construction / reclamation activities


Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Roadway / Bores ea.	16	2	18	n/a
Erosion / Sediment	n/a	.		n/a
Topsoil	n/a	n/a		n/a
Restoration/Cleanup	63853	5700	69553	16.60%
Roadway Restoration	n/a	n/a		n/a
Fence / Gate	n/a	n/a		n/a
Fertilizing / Seeding	18.6 acres	No figures		n/a

Project Site Safety
 Number of Plains/Onshore employees on-site (46), contractor employees (248).
 Due to holiday next report to be completed 9-4-2012

Signature: Ron McCreery via e-mail Date: 8/27/2012

71 **PU-10-630** Filed: 8/27/2012 Pages: 3
 Bakken North Project weekly progress report - week ending 8-26-2012

Plains Pipeline, L.P.



PLAINS
ALL AMERICAN
PIPELINE, L.P.

Weekly Construction Progress Report

Case # PU-10-630
Project: Bakken North Project
Week Ending: 8/26/2012

Report # 14

Dates of construction	Startup	Shutdown
	5/22/2012	

Temperature high and low for week.	High	Low
	93°	57°

Landowner / Public Concerns	Addressing Individual	Phone
Mr. Brad Olson	Ms. Cathy Owen (Environmental Inspector)	406-765-8125
Continue to check coulee and water daily as necessary.		

Suspension of project activities (when, where, why ,how long)
n/a

Identify Cultural Resources not previously identified.
n/a

Critical Habitat or Threatened or Endangered Species.
n/a

Cathodic Protection Installed	When	Where
Cathodic Protection test lead stations installed at 3 different locations on main line.		

Special Coordination	Who	When
----------------------	-----	------


Pipeline in-service date	Date
n/a	



Protective box



Sandblasting for coating

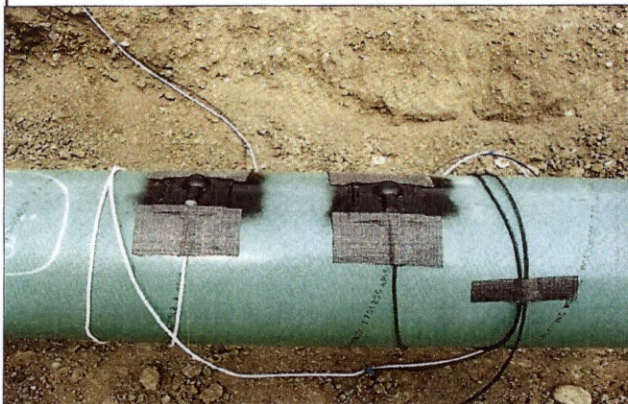

Test Leads



Foreign line



ROW after topsoil replacement/prior to seeding.



ROW clean up prior to topsoil replacement.

Report Number # 14

Date 8/26/2012
