

PLAINS ALL AMERICAN PIPELINE, L.P.

Weekly Construction Progress Report

Case # **PU-10-630**
 Project: **Bakken North Project**
 Week Ending: 10/14/2012

Report # 21

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Jim Fleetwood	Plains Pipeline	307-472-9911	307-315-0574
Project Coordinator	Ron McCreery	Plains Pipeline	701-694-4414	406-765-8119
Contractor Spread	Mike Bondurant	Tomahawk	406-789-2380	406-789-7024
Brief Description of Week's Activities				
Hydro test plan being prepared - will need to be reviewed.				
Sizing pig ran on 10-08-2012				
Environmental continued to check environmental control devices (ECD).				
Tomahawk contracted 3rd party to do seeding. No figures as yet.				
G3 no progress				
Contractor cutting back on equipment and personnel.				
Electrical contractor installing wiring to valve sites. Fencing crew working at valve sites.				
Project Completion Spread				
Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Clear & Grade lft.	151912	Zero work in ND.	151912	100% Completed in ND.
ROW Finished lft.	161712	Zero work in ND.	161712	100% Completed in ND.
Stringing lft.	201181	Zero work in ND.	201181	100% Completed in ND.
Welding / X Ray	3177	0	3177	n/a
Ditching	150346	0	150346	Completed
Lowering In	143344	0	143344	Completed
Backfill	146784	0	146784	Completed
Clean-up	141726	Work in progress, no figures	141726	33.83%
Coating (Welds)	3107	0	3107	n/a
ECDs Installed				
Silt Fence lft.	9832	0	9832	n/a
Hay bales ea.	353	0	353	n/a
Mats ea.	743	0	743	n/a
Waddles ea.	83	0	83	n/a
Curlex	26818	0	26818	
Project construction / reclamation activities				
Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Roadway / Bores ea.	17	0	17	n/a
Erosion / Sediment	n/a	0		n/a
Topsoil	n/a	n/a		n/a
Restoration/Cleanup	141726	Work in progress, no figures	141726	#DIV/0!
Roadway Restoration	n/a	0		n/a
Fence / Gate	n/a	n/a		n/a
Fertilizing / Seeding	18.6 acres	No figures		n/a
Project Site Safety				
Number of Plains/Onshore employees on-site (16), contractor employees (92).				


Signature:

Ron McCreery via e-mail

RM

Date:

10/15/2012



PLAINS
ALL AMERICAN
PIPELINE, L.P.

Weekly Construction Progress Report

Case # PU-10-630

Report # 21

Project: Bakken North Project

Week Ending: 10/14/2012

Dates of construction	Startup	Shutdown
	5/22/2012	

Temperature high and low for week.	High	Low
	54°	28°

Landowner / Public Concerns	Addressing Individual	Phone
Mr. Brad Olson	Ms. Cathy Owen (Environmental Inspector)	406-765-8125
Continue to check coulee and water daily as necessary.		
Eleven line markers installed.		

Suspension of project activities (when, where, why ,how long)

Identify Cultural Resources not previously identified.

n/a


Critical Habitat or Threatened or Endangered Species.

n/a


Cathodic Protection Installed	When	Where

Special Coordination	Who	When
Approval has been completed from PSC on minor reroute at Trenton station. Completion of work on route has started.		
Reroute work has been completed.		


Pipeline in-service date	Date
n/a	

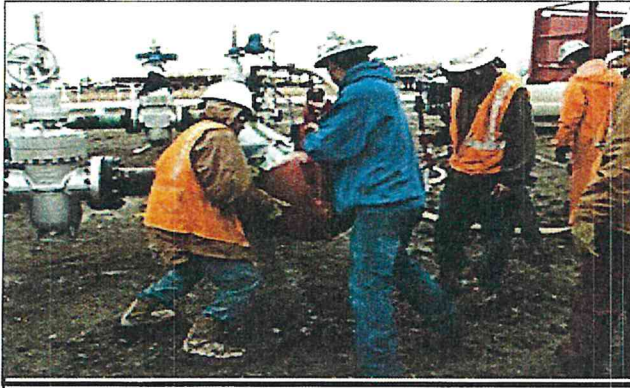

Loading sizing pig.

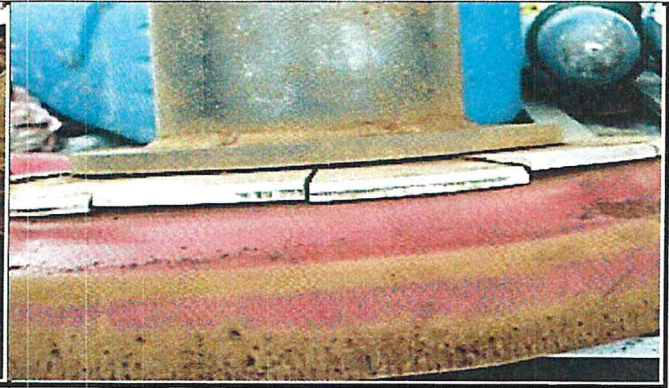

Sizing plate

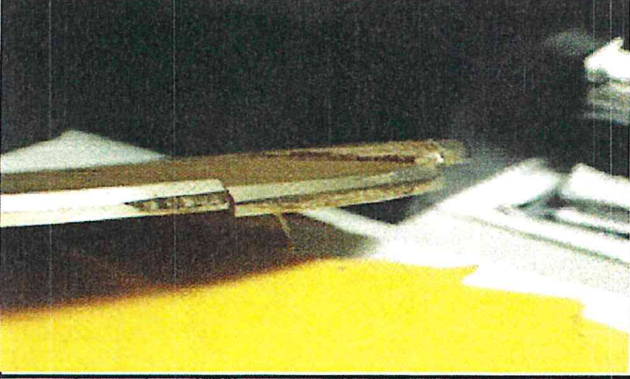

Sizing plate



Fencing at valve site



Valve site and fencing post.

Report Number # 21

Date 10/15/2012
