



PLAINS ALL AMERICAN PIPELINE, L.P.

Weekly Construction Progress Report

Case # **PU-10-630**
 Project: **Bakken North Project**
 Week Ending: 11/4/2012

Report # 24

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Jim Fleetwood	Plains Pipeline	307-472-9911	307-315-0574
Project Coordinator	Ron McCreery	Plains Pipeline	701-694-4414	406-765-8119
Contractor Spread	Mike Bondurant	Tomahawk	406-789-2380	406-789-7024
Brief Description of Week's Activities				
No date set for mainline hydro test.				
Environmental continued to check environmental control devices (ECD).				
Tomahawk contracted 3rd party to do seeding. No figures as yet.				
Contractor cutting back on equipment and personnel.				
Welding of bore pipe for G3 well site started - Completed				
Punch list started of small issues for land owners request.				
Successful Hydro test on G3 bore pipe.				
No additional work in North Dakota.				
Project Completion Spread				
Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Clear & Grade lft.	151912	Zero work in ND.	151912	100% Completed in ND.
ROW Finished lft.	161712	Zero work in ND.	161712	100% Completed in ND.
Stringing lft.	201181	Zero work in ND.	201181	100% Completed in ND.
Welding / X Ray	3177	0	3177	n/a
Ditching	150346	0	150346	Completed
Lowering In	143344	0	143344	Completed
Backfill	146784	0	146784	Completed
Clean-up	141726	Work in progress, no figures	141726	33.83%
Coating (Welds)	3107	0	3107	n/a
ECDs Installed				
Silt Fence lft.	9832	0	9832	n/a
Hay bales ea.	353	0	353	n/a
Mats ea.	743	0	743	n/a
Waddles ea.	83	0	83	n/a
Curlex	45678	0	45678	SQF
Project construction / reclamation activities				
Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Roadway / Bores ea.	21	0	21	n/a
Erosion / Sediment	n/a	0		n/a
Topsoil	n/a	n/a		n/a
Restoration/Cleanup	141726	Work in progress, no figures	141726	
Roadway Restoration	n/a	0		n/a
Fence / Gate	n/a	n/a		n/a
Fertilizing / Seeding	18.6 acres	No figures		n/a
Project Site Safety				
Number of Plains/Onshore employees on-site (14), contractor employees (80).				

Signature:

Ron McCreery via e-mail *RM*

Date:

11/5/2012

86 **PU-10-630** Filed: 11/5/2012 Pages: 3
 Bakken North Project weekly progress report - week
 ending 11-04-2012

Plains Pipeline, L.P.



PLAINS
ALL AMERICAN
PIPELINE, L.P.

Weekly Construction Progress Report

Case # PU-10-630

Report # 24

Project: Bakken North Project

Week Ending: 11/4/2012

Dates of construction	Startup	Shutdown
	5/22/2012	

Temperature high and low for week.	High	Low
	36°	23°

Landowner / Public Concerns	Addressing Individual	Phone
Mr. Brad Olson	Ms. Pam Bennett(Environmental Inspector)	406-765-8143
Continue to check coulee.		

Suspension of project activities (when, where, why ,how long)
n/a


Identify Cultural Resources not previously identified.
n/a

Critical Habitat or Threatened or Endangered Species.
n/a

Cathodic Protection Installed	When	Where
-------------------------------	------	-------

Special Coordination	Who	When
----------------------	-----	------

Pipeline in-service date	Date
n/a	

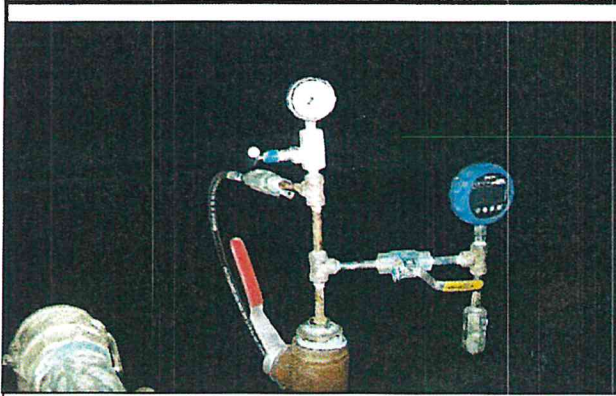




G 3 Well Pad Hydro Test



G 3 Well Pad Hydro Test



G 3 Well Pad Hydro Test



# 24		11/3/2012	G-3 pad # 7
------	--	-----------	-------------

Report Number
