

# PLAINS ALL AMERICAN PIPELINE, L.P.

## Weekly Construction Progress Report

Case # **PU-10-630**  
 Project: **Bakken North Project**  
 Week Ending: 1/20/13

Report # 33

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Jim Fleetwood	Plains Pipeline	307-472-9911	307-315-0574
Project Coordinator	Ron McCreery	Plains Pipeline	701-694-4414	406-765-8119
Chief Inspector	Jim Pennington	QCS	701-694-4415	406-765-8153
Contractor Spread	Mike Bondurant	Tomahawk	406-789-2380	406-789-7024

### Brief Description of Week's Activities

Dewatering and drying of pipeline from Trenton Station to MT state line completed.  
 Environmental continued to check ECDs all found to be intact and functioning properly.  
 Tomahawk seeding will not be done until next spring.  
 Contractor cutting back on equipment and personnel.  
 Punch list started of small issues for land owners request.  
 Ongoing cleanup at test site and discharge site.

### Project Completion Spread

Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Clear & Grade lft.	151912	Zero work in ND.	151912	100% Completed in ND.
ROW Finished lft.	161712	Zero work in ND.	161712	100% Completed in ND.
Stringing lft.	201181	Zero work in ND.	201181	100% Completed in ND.
Welding / X Ray	3177	0	3177	n/a
Ditching	150346	0	150346	Completed
Lowering In	143344	0	143344	Completed
Backfill	146784	0	146784	Completed
Clean-up	141726	Work in progress, no figures	141726	33.83%
Coating (Welds)	3123	0	3123	n/a
<b>ECDs Installed</b>				
Silt Fence lft.	9832	0	9832	n/a
Hay bales ea.	353	0	353	n/a
Mats ea.	743	0	743	n/a
Wattles ea.	89	0	89	n/a
Curlex	45678	0	45678	SQF

### Project construction / reclamation activities

Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Roadway / Bores ea.	21	0	21	n/a
Erosion / Sediment	n/a	0		n/a
Topsoil	n/a	n/a		n/a
Restoration/Cleanup	141726	Work in progress, no figures	141726	
Roadway Restoration	n/a	0		n/a
Fence / Gate	n/a	n/a		n/a
Fertilizing / Seeding	18.6 acres	No figures		n/a

### Project Site Safety

Number of Plains/Onshore employees on-site (8), contractor employees (15).

Signature:

*Ron McCreery* via e-mail

R.M.

Date:

1/20/13



**PLAINS**  
**ALL AMERICAN**  
**PIPELINE, L.P.**

**Weekly Construction Progress Report**

**Case #** PU-10-630

Report # 33

**Project:** Bakken North Project

**Week Ending:** 1/20/13

Dates of construction	Startup	Shutdown
	5/22/12	

Temperature high and low for week.	High	Low
	36°	-14°

Landowner / Public Concerns	Addressing Individual	Phone
n/a		

**Suspension of project activities (when, where, why ,how long)**

n/a

**Identify Cultural Resources not previously identified.**

n/a

**Critical Habitat or Threatened or Endangered Species.**

n/a

Cathodic Protection Installed	When	Where

Special Coordination	Who	When


Pipeline in-service date	Date
n/a	

**Plains All American Pipeline L.P.  
Daily Construction Report**



DATE: Week Ending 1/20/13  
Location: Grenora, ND  
AFE: 14933  
Project Name: **Bakken North Project**  
Chief Inspector: **Jim Pennington**

Page: 3  
General Contractor: Tomahawk  
Superintendent: Kyle Thomas  
Constr. Mgr./Cord. Ron McCreery  
Project Engineer: Jim Fleetwood

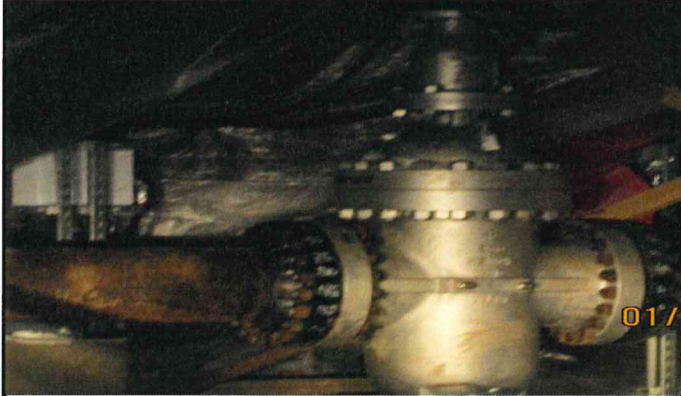

Monitoring of valves for temperature during Dewatering



Monitoring of each valve site during dewatering and drying



Retrieval of Drying PIGs



Retrieval of Dewatering PIGs
