



# PLAINS

ALL AMERICAN  
PIPELINE, L.P.

## Weekly Construction Progress Report

Case # **PU-10-630**  
**Project: Bakken North Project**  
 Week Ending: 2/3/13

Report # 35

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Jim Fleetwood	Plains Pipeline	307-472-9911	307-315-0574
Project Coordinator	Ron McCreery	Plains Pipeline	701-694-4414	406-765-8119
Chief Inspector	Jim Pennington	QCS	701-694-4415	406-765-8153
Contractor Spread	Mike Bondurant	Tomahawk	406-789-2380	406-789-7024

### Brief Description of Week's Activities

Check valves hydro tested and installed @ 52nd St and 67th Street valve sets.  
 Environmental continued to check ECDs all found to be intact and functioning properly.  
 Tomahawk seeding will not be done until next spring.  
 Contractor cutting back on equipment and personnel.  
 Punch list started of small issues for land owners request.  
 Aerial Marker 00 started.

### Project Completion Spread

Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Clear & Grade lft.	151912	0	151912	100% Completed in ND.
ROW Finished lft.	151912	0	151912	100% Completed in ND.
Stringing lft.	201181	0	201181	100% Completed in ND.
Welding / X Ray	3178	0	3178	100% Completed in ND.
Ditching	150346	0	150346	100% Completed in ND.
Lowering In	150346	0	150346	100% Completed in ND.
Backfill	150346	0	150346	100% Completed in ND.
Clean-up	151912	0	151912	100% Completed in ND.
Coating (Welds)	3178	0	3178	100% Completed in ND.

### ECDs Installed

Silt Fence lft.	9832	0	9832	n/a
Hay bales ea.	353	0	353	n/a
Mats ea.	743	0	743	n/a
Wattles ea.	89	0	89	n/a
Curlex	45678	0	45678	SQF

### Project construction / reclamation activities

Description	Previous Week Complete	This Week Complete	Total Complete	% Total Complete
Roadway / Bores ea.	21	0	21	n/a
Erosion / Sediment	n/a	0		n/a
Topsoil	n/a	n/a		n/a
Restoration/Cleanup	151912	0	151912	Not complete
Roadway Restoration	n/a	0		n/a
Fence / Gate	n/a	n/a		n/a
Fertilizing / Seeding	18.6 acres	0		n/a

### Project Site Safety

Number of Plains/Onshore employees on-site (6), contractor employees (8).

Signature:

Date:


*Ron McCreery* via e-mail

R.M.

2/3/13

97 **PU-10-630** Filed: 2/4/2013 Pages: 3  
**Bakken North Project weekly progress report - week ending 02-03-2013**

Plains Pipeline, L.P.



**PLAINS**  
**ALL AMERICAN**  
**PIPELINE, L.P.**

**Weekly Construction Progress Report**

**Case #** PU-10-630

Report # 35

**Project:** Bakken North Project

**Week Ending:** 2/3/13

Dates of construction	Startup	Shutdown
	5/22/12	

Temperature high and low for week.	High	Low
	22°	-29°

Landowner / Public Concerns	Addressing Individual	Phone
n/a		

**Suspension of project activities (when, where, why, how long)**  
 Project was halted due to weather conditions on 6Feb, 7Feb and 9Feb due to weather conditions. Work to resume 4Feb13.

**Identify Cultural Resources not previously identified.**  
 n/a

**Critical Habitat or Threatened or Endangered Species.**  
 n/a

Cathodic Protection Installed	When	Where

Special Coordination	Who	When


Pipeline in-service date	Date
n/a	

**Plains All American Pipeline L.P.  
Daily Construction Report**



DATE: Week Ending Sunday, February 3, 13  
 Location: Grenora, ND  
 AFE: 14933  
 Project Name: Bakken North Project  
 Chief Inspector: Jim Pennington

Page: 3  
 General Contractor: Tomahawk  
 Superintendent: Kyle Thomas  
 Constr. Mgr./Cord.: Ron McCreery  
 Project Engineer: Jim Fleetwood

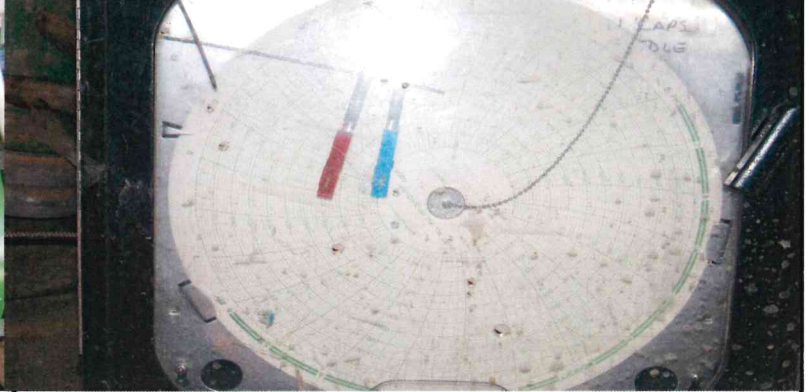

Check valve during HydroTesting

Chart recorder during hydro testing on check valves

