



**PROJECT DETAILS AND PROGRESS:**

**Contract 140094 – Site Preparation, Service Building, Foundations, and Underground Installations**

- Installed doors, door hardware, windows, repaired floor tile and cleaned up in the Service Building
- Installed fire protection piping and alarms in Service Building
- Installed grounding for access stairs
- Installed oily drain tank vent pipe and notched cover
- Installed rock in the area excavated for service water repair on east side of turbine
- Installed rock and graded area 5' outside of site security fence
- Graded top of basin and installed Class 5 aggregate for road around basin
- Rocked around septic tank on east and south side of Service Building
- Graded miscellaneous areas throughout site
- Repaired lighting conduit around gas yard
- Installed electrical lights, steel conduit, Gai-tronics, 1 ½" fiber conduit and wire pulling in Service Building

**Contract 140095 – Mechanical and Electrical Installation**

- Assembled and welded exhaust sections in laydown and on foundation and installed stack platforms
- Set top half of exhaust stack in place
- Assembled inlet air pieces: made adjustments to legs for elevation corrections
- Erected acoustic barrier panels
- Stripped and formed grout forms around various skids
- Formed grout forms around acoustic barrier base
- Installed lube oil piping
- Installed bleed heat piping
- Installed exhaust blower piping
- Installed fuel gas piping
- Pulled cable through PEECC, wastewater lift station, EMH-2, GSU, Pull Vault 2, and EMH-5
- Installed cable tray and steel conduit in electrical room of Service Building
- Installed GNAC braids
- Tested and energized control power to 480 volt and 4160 volt switchgear

**PROJECT OPEN ITEMS / CONCERNS:**

- None not already discussed
- Construction Equipment: 3900 crawler crane, 40-ton rubber tire crane, 2 fork lift (JLG Skytrak), 2 man lifts, 1 skid steer (New Holland C190)
- Visitors: Curtis Hanson (GE), Ray Beloin (GE)

Montana-Dakota Utilities Company  
R.M. Heskett Station Unit 3  
Project No. 11-0274-04




Top half of exhaust stack installation (looking NE)



Service Building window installation (looking SW)

Montana-Dakota Utilities Company  
R.M. Heskett Station Unit 3  
Project No. 11-0274-04

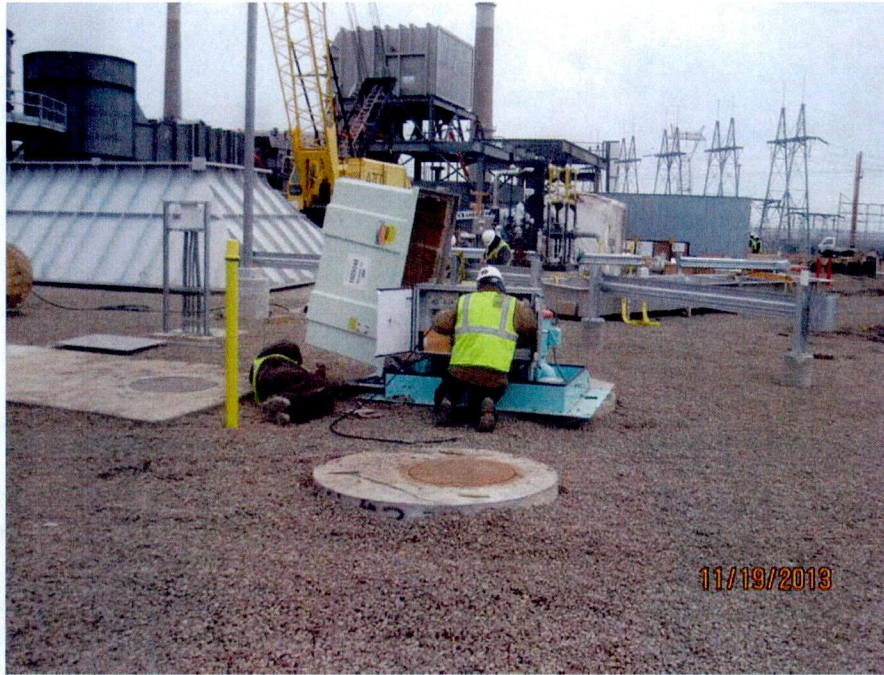

Waste water lift station cable installation (looking E)



Exhaust blower piping installation (looking S)
