

ONEOK Rockies Midstream Stateline NGL Pipeline

Weekly Construction Progress Report

Case #: PU-11-683

Project: Stateline to Riverview 10" NGL Pipeline

Week Ending: May 11, 2012

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Blayne Lyman	ONEOK	580 395-6309	580 761-3307
Construction Mgr	Tony Warner	ONEOK	N/A	580 741-0115
Contractor Spread 1	Torsten Leines	Alpha Oil & Gas	701 842-2855	612 916-8417
Contractor Spread 2	Scott Lawson	Frontier Services	406-670-1319	406-698-5047

Brief Description of Week's Activities


Contractors continued to clear & grade ROW and string pipe; welders have been tested for both spreads.

PROGRESS REPORT

Progress as of:	Week Ending	
	May 04	May 11
Mowing	9%	9%
Tot. Ft.	26677	26895
New Ft.		218
R.O.W.	0%	2%
Tot. Ft.	0	6100
New Ft.		6100
Pipe Strung	0%	0%
Tot. Ft.	0	1400
New Ft.		1400
Pipe Welded	0%	1%
Tot. Ft.	0	1600
New Ft.		1600
Coating	0%	0%
Tot. Ft.	0	0
New Ft.		0
Ditching	0%	0%
Tot. Ft.	0	0
New Ft.		0
Lowered	0%	0%
Tot. Ft.	0	0
New Ft.		0
Backfilled	0%	0%
Tot. Ft.	0	0
New Ft.		0
Cleanup	0%	0%
Tot. Ft.	0	0
New Ft.		0

Week Ending:
5/12/12

Footage:	289,958	Actual % Complete:	1%	Plan % Compl:	2%
Miles:	54.92	Spread:	Stateline NGL Pipeline	AFE:	255,111,6825.010000

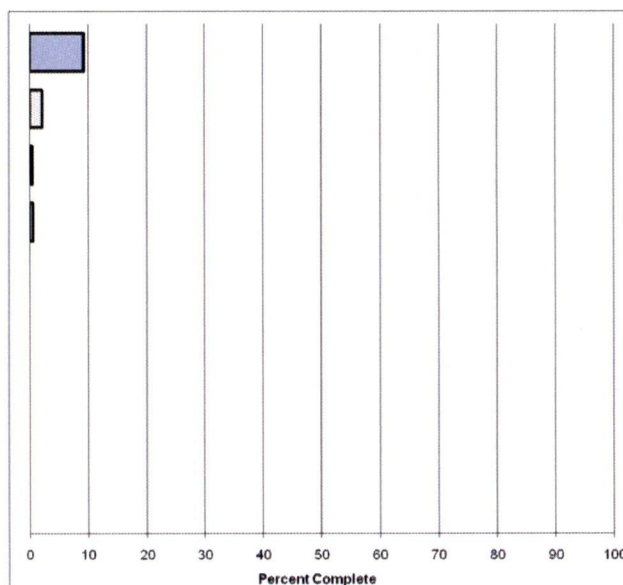

Contractor: Spread 1: Alpha Oil & Gas, Spread 2: Frontier Services

Rain Days: 2
Mud Days: 1
Snow Days: 0
Wind Out Days: 0

Completed through
week ending 5/4

Completed in
week ending 5/11

Project Site Safety

Contractors hold weekly safety meetings with all contract personnel and daily tailgate safety meetings with individual crews.

ONEOK Rockies Midstream Stateline NGL Pipeline

Comments

Signatory	Date
Blayne Lyman	5/17/2012
