

# ONEOK Rockies Midstream Stateline NGL Pipeline

## Weekly Construction Progress Report

Case #: PU-11-683

Project: Stateline to Riverview 10" NGL Pipeline

Week Ending: June 2, 2012

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Blayne Lyman	ONEOK	580 395-6309	580 761-3307
Construction Mgr	Tony Warner	ONEOK	N/A	580 741-0115
Contractor Spread 1	Torsten Leines	Alpha Oil & Gas	701 842-2855	612 916-8417
Contractor Spread 2	Scott Lawson	Frontier Services	406-670-1319	406-698-5047


### Brief Description of Week's Activities

Both Spreads clearing & grading ROW. Spread 1 is stringing pipe. Mainline construction continues on Spread 2.

### PROGRESS REPORT

Progress as of:	Week Ending	Week Ending
	May 26	Jun 02
<b>Mowing</b>	69%	82%
Tot. Ft.	198900	238500
New Ft.		39600
<b>R.O.W.</b>	54%	54%
Tot. Ft.	156995	156995
New Ft.		0
<b>Pipe Strung</b>	23%	34%
Tot. Ft.	67200	98700
New Ft.		31500
<b>Pipe Welded</b>	6%	13%
Tot. Ft.	17500	39100
New Ft.		21600
<b>Coating</b>	5%	11%
Tot. Ft.	15700	31800
New Ft.		16100
<b>Ditching</b>	5%	10%
Tot. Ft.	15300	30000
New Ft.		14700
<b>Lowered</b>	5%	10%
Tot. Ft.	15300	29300
New Ft.		14000
<b>Backfilled</b>	5%	9%
Tot. Ft.	15300	26200
New Ft.		10900
<b>Cleanup</b>	1%	1%
Tot. Ft.	1600	1600
New Ft.		0

Week Ending: 6/2/12			
Footage:	289,958	Actual % Complete:	18%
Miles:	54.92	Plan % Compl:	22%
Spread:	Stateline NGL Pipeline		AFE:
			255,111,6825.010000

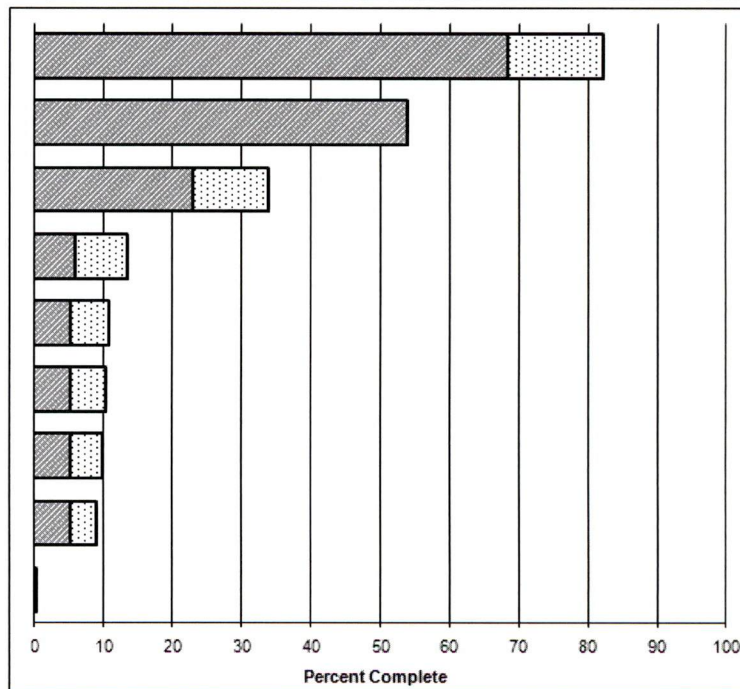

Contractor: Spread 1: Alpha Oil & Gas, Spread 2: Frontier Services

Rain Days: 3

Mud Days: 2

Snow Days: 0

Wind Out Days: 0

Holidays: 3

Completed through week ending 5/26

Completed in week ending 6/2

### Project Site Safety

First project safety conference call was held on May 31<sup>st</sup>, 2012.

# ONEOK Rockies Midstream Stateline NGL Pipeline

Comments

Signatory	Date
Blayne Lyman	6/7/2012
