

ONEOK Rockies Midstream Stateline NGL Pipeline

Weekly Construction Progress Report

Case #: PU-11-683
 Project: Stateline to Riverview 10" NGL Pipeline
 Week Ending: June 9, 2012

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Blayne Lyman	ONEOK	580 395-6309	580 761-3307
Construction Mgr	Tony Warner	ONEOK	N/A	580 741-0115
Contractor Spread 1	Torsten Leines	Alpha Oil & Gas	701 842-2855	612 916-8417
Contractor Spread 2	Scott Lawson	Frontier Services	406-670-1319	406-698-5047


Brief Description of Week's Activities

ROW work continues on Both Spreads. Spread 1 is stringing pipe. Mainline construction continues on Spread 2.

PROGRESS REPORT

Progress as of:	Week Ending	Week Ending
	Jun 02	Jun 09
Moving	82%	100%
Tot. Ft.	238500	289945
New Ft.		51445
R.O.W.	54%	67%
Tot. Ft.	156395	196100
New Ft.		39105
Pipe Strung	34%	48%
Tot. Ft.	41062	41069
New Ft.		7
U.T. Pipe	32%	49%
Tot. Ft.	98700	138500
New Ft.		39800
Pipe Welded	13%	20%
Tot. Ft.	39100	58300
New Ft.		19200
Coating	11%	18%
Tot. Ft.	31800	51000
New Ft.		19200
Ditching	10%	18%
Tot. Ft.	30000	51200
New Ft.		21200
Lowered	10%	16%
Tot. Ft.	29300	46800
New Ft.		17500
Backfilled	9%	16%
Tot. Ft.	26200	45100
New Ft.		18900
Cleanup	1%	6%
Tot. Ft.	1600	17700
New Ft.		16100

Footage:	290,704	Actual % Complete:	26%	Plan % Compl:	33%
Miles:	55.06	Spread:	Stateline NGL Pipeline	AFE:	255,111,6825.010000

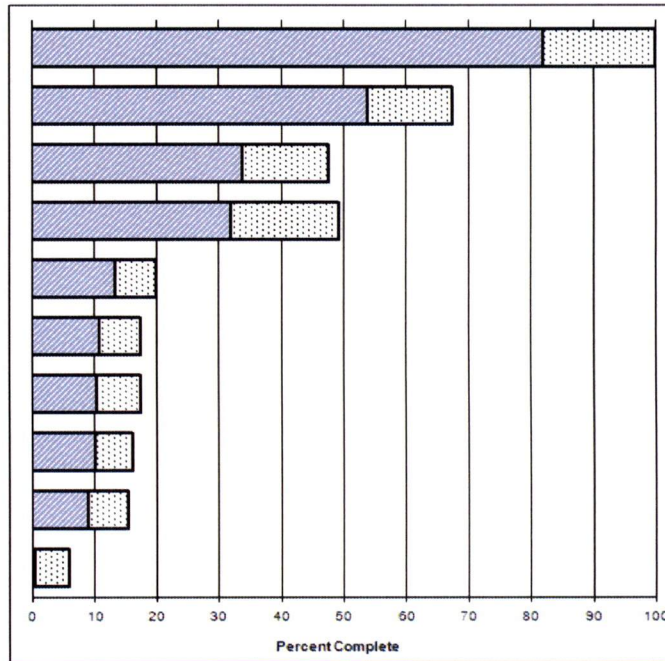

Completed through week ending 6/2

Completed in week ending 6/9

Contractor: Spread 1: Alpha Oil & Gas, Spread 2: Frontier Services
 Rain Days: 4
 Mud Days: 2
 Snow Days: 0
 Wind Out Days: 0
 Holidays: 3

Project Site Safety

Contractors are submitting safety data weekly which is compiled and discussed in weekly safety meetings.

ONEOK Rockies Midstream Stateline NGL Pipeline

Comments

Signatory	Date
Blayne Lyman	6/14/2012
