

ONEOK Rockies Midstream Stateline NGL Pipeline

Weekly Construction Progress Report

Case #: PU-11-683

Project: Stateline to Riverview 10" NGL Pipeline

Week Ending: June 30, 2012

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Blayne Lyman	ONEOK	580 395-6309	580 761-3307
Construction Mgr	Tony Warner	ONEOK	N/A	580 741-0115
Contractor Spread 1	Torsten Leines	Alpha Oil & Gas	701 842-2855	612 916-8417
Contractor Spread 2	Scott Lawson	Frontier Services	406-670-1319	406-698-5047


Brief Description of Week's Activities

Mainline construction is underway on both Spread 1 and Spread 2.

PROGRESS REPORT

Progress as of:	Week Ending	Week Ending
	Jun 23	Jun 30
Mowing	100%	100%
Tot. Ft.	290000	290000
New Ft.	0	0
R.O.W.	96%	96%
Tot. Ft.	278400	278400
New Ft.	0	0
Pipe Strung	85%	96%
Tot. Ft.	246800	278400
New Ft.	31600	31600
U.T. Pipe	81%	96%
Tot. Ft.	235200	278400
New Ft.	43200	43200
Pipe Welded	49%	69%
Tot. Ft.	143700	200100
New Ft.	56400	56400
Coating	40%	56%
Tot. Ft.	116300	161400
New Ft.	45100	45100
Ditching	29%	43%
Tot. Ft.	83700	125900
New Ft.	42200	42200
Lowered	29%	42%
Tot. Ft.	82900	122600
New Ft.	39700	39700
Backfilled	29%	40%
Tot. Ft.	83700	117300
New Ft.	33600	33600
Cleanup	18%	25%
Tot. Ft.	51300	72700
New Ft.	21400	21400

Footage:	290,704	Actual % Complete:	58%	Plan % Compl:	62%
Miles:	55.06	Spread:	Stateline NGL Pipeline	AFE:	255,111,6825.010000

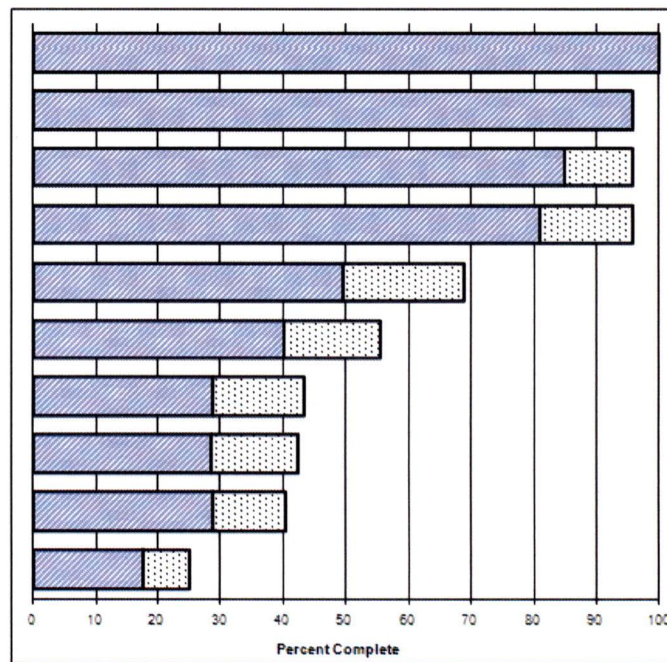

Contractor: Spread 1: Alpha Oil & Gas, Spread 2: Frontier Services
 Rain Days: 6
 Mud Days: 2
 Snow Days: 0
 Wind Out Days: 0
 Holidays: 3

Project Site Safety

The hot weather & the need for project personnel to keep hydrated were discussed in this week's safety call.

ONEOK Rockies Midstream Stateline NGL Pipeline

Comments

Signatory	Date
Blayne Lyman	7/5/2012
