

# ONEOK Rockies Midstream Stateline NGL Pipeline

## Weekly Construction Progress Report

Case #: PU-11-683  
 Project: Stateline to Riverview 10" NGL Pipeline  
 Week Ending: July 7, 2012

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Blayne Lyman	ONEOK	580 395-6309	580 761-3307
Construction Mgr	Tony Warner	ONEOK	N/A	580 741-0115
Contractor Spread 1	Torsten Leines	Alpha Oil & Gas	701 842-2855	612 916-8417
Contractor Spread 2	Scott Lawson	Frontier Services	406-670-1319	406-698-5047


**Brief Description of Week's Activities**  
 Mainline construction continues on both Spread 1 and Spread 2. Independence Day holiday.

**PROGRESS REPORT**

Progress as of:	Week Ending	Week Ending
	Jun 30	Jul 07
<b>Moving</b>	100%	100%
Tot. Ft.	290000	290000
New Ft.	0	0
<b>R.O.V.</b>	96%	96%
Tot. Ft.	278400	278400
New Ft.	0	0
<b>Pipe Strung</b>	96%	96%
Tot. Ft.	278400	278400
New Ft.	0	0
<b>U.T. Pipe</b>	96%	96%
Tot. Ft.	278400	278400
New Ft.	0	0
<b>Pipe Welded</b>	69%	70%
Tot. Ft.	200100	202600
New Ft.	2500	2500
<b>Coating</b>	56%	60%
Tot. Ft.	161400	175800
New Ft.	14400	14400
<b>Ditching</b>	43%	53%
Tot. Ft.	125900	152700
New Ft.	26800	26800
<b>Lowered</b>	42%	52%
Tot. Ft.	122600	152400
New Ft.	29800	29800
<b>Backfilled</b>	40%	50%
Tot. Ft.	117300	146000
New Ft.	28700	28700
<b>Cleanup</b>	25%	29%
Tot. Ft.	72700	83700
New Ft.	11000	11000

Week Ending: 7/7/12

Footage:	290,704	Actual % Complete:	63%	Plan % Compl:	77%
Miles:	55.06	Spread:	Stateline NGL Pipeline	AFE:	255,111,6825.010000

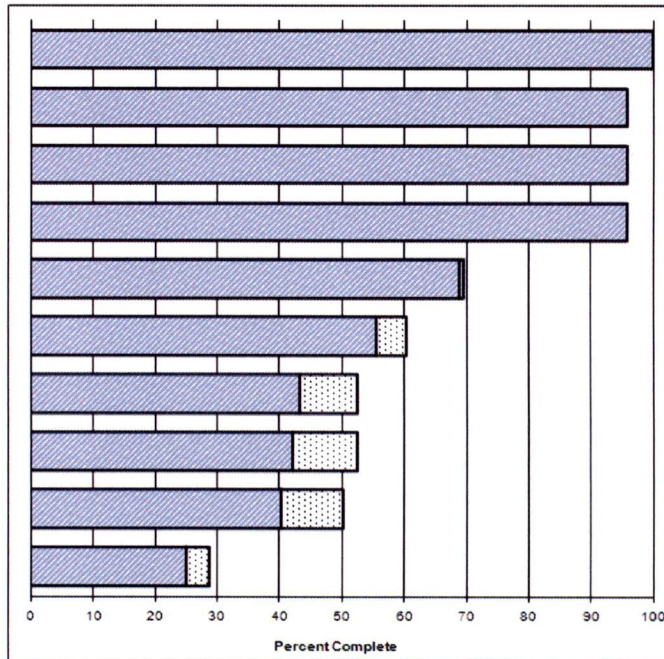

Completed through week ending 6/30
  Completed in week ending 7/7

Contractor: Spread 1: Alpha Oil & Gas, Spread 2: Frontier Services  
 Rain Days: 6  
 Mud Days: 2  
 Snow Days: 0  
 Wind Out Days: 0  
 Holidays: 5

**Project Site Safety**  
 Weekly project safety conference call was not held this week due to the Independence Day holiday.

# ONEOK Rockies Midstream Stateline NGL Pipeline

Comments

Signatory	Date
Blayne Lyman	7/12/2012
