

ONEOK Rockies Midstream Stateline NGL Pipeline

Weekly Construction Progress Report

Case #: PU-11-683
Project: Stateline to Riverview 10" NGL Pipeline
Week Ending: August 11, 2012

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Blayne Lyman	ONEOK	580 395-6309	580 761-3307
Construction Mgr	Tony Warner	ONEOK	N/A	580 741-0115
Contractor Spread 1	Torsten Leines	Alpha Oil & Gas	701 842-2855	612 916-8417
Contractor Spread 2	Scott Lawson	Frontier Services	406-670-1319	406-698-5047

Brief Description of Week's Activities


Directional drills and tie-ins continued on Spread 1. Spread 2 completed tie-in piping at Riverview.

PROGRESS REPORT

Progress as of:	Week Ending	Week Ending
	Aug 04	Aug 11
Mowing	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
R.O.W.	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
Pipe Strung	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
U.I. Pipe	100%	100%
Tot. Ft.	290164	290164
New Ft.	0	0
Pipe Welded	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
Coating	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
Ditching	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
Lowered	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
Backfilled	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
Cleanup	60%	71%
Tot. Ft.	175264	205364
New Ft.	0	30100
Hydrotest	50%	50%
Tot. Ft.	145864	145864
New Ft.	0	0

Rain Days: 8
Mud Days: 4
Snow Days: 0
Wind Out Days: 0
Holidays: 5

Week Ending: 8/11/12			
Footage:	290,910	Actual % Complete:	97%
Miles:	55.10	Spread:	Stateline NGL Pipeline
		AFE:	255,111,6825.010000
		Plan % Compl:	100%

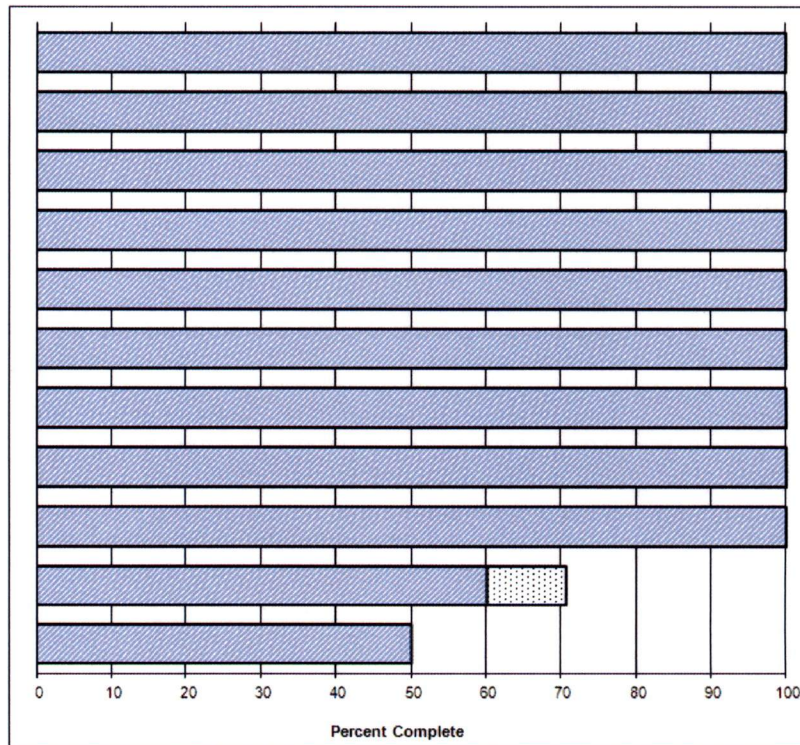

Contractor: Spread 1: Alpha Oil & Gas, Spread 2: Frontier Services

Completed through week ending 8/4	Completed in week ending 8/11
-----------------------------------	-------------------------------

Project Site Safety

Safety in securing loads for transport on and off the right-of-way was this week's safety topic.

ONEOK Rockies Midstream Stateline NGL Pipeline

Comments

Signatory	Date
Blayne Lyman	8/16/2012
