

# ONEOK Rockies Midstream Stateline NGL Pipeline

## Weekly Construction Progress Report

**Case #: PU-11-683**  
**Project: Stateline to Riverview 10" NGL Pipeline**  
**Week Ending: August 18, 2012**

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Blayne Lyman	ONEOK	580 395-6309	580 761-3307
Construction Mgr	Tony Warner	ONEOK	N/A	580 741-0115
Contractor Spread 1	Torsten Leines	Alpha Oil & Gas	701 842-2855	612 916-8417
Contractor Spread 2	Scott Lawson	Frontier Services	406-670-1319	406-698-5047

### Brief Description of Week's Activities


Directional drills and tie-ins continued on Spread 1 along with first hydrotest. Spread 2 completed line drying.

### PROGRESS REPORT

Progress as of:	Week Ending	Week Ending
	Aug 11	Aug 18
<b>Mowing</b>	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
<b>R.O.W.</b>	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
<b>Pipe Strung</b>	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
<b>U.T. Pipe</b>	100%	100%
Tot. Ft.	290164	290164
New Ft.	0	0
<b>Pipe Welded</b>	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
<b>Coating</b>	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
<b>Ditching</b>	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
<b>Lowered</b>	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
<b>Backfilled</b>	100%	100%
Tot. Ft.	290910	290910
New Ft.	0	0
<b>Cleanup</b>	71%	80%
Tot. Ft.	205364	232464
New Ft.	0	27100
<b>Hydrotest</b>	50%	68%
Tot. Ft.	145864	198895
New Ft.	0	53031

Rain Days: 8  
Mud Days: 4  
Snow Days: 0  
Wind Out Days: 0  
Holidays: 5

Week Ending: 8/18/12			
Footage:	290,910	Actual % Complete:	98%
Miles:	55.10	Spread:	Stateline NGL Pipeline
		AFE:	255,111,6825.010000

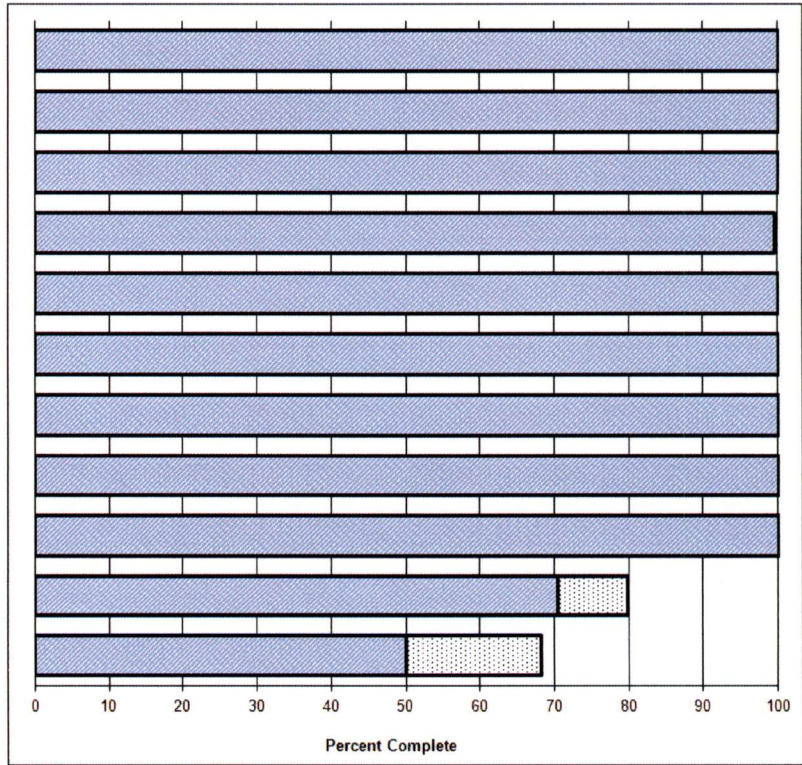

Contractor: Spread 1: Alpha Oil & Gas, Spread 2: Frontier Services

Completed through week ending 8/11
  Completed in week ending 8/18

### Project Site Safety

Safety in performing hydrotests was discussed in preparation for the first test on Spread 1.

# ONEOK Rockies Midstream Stateline NGL Pipeline

Comments

Signatory	Date
Blayne Lyman	8/23/2012
