

ONEOK Rockies Midstream Stateline NGL Pipeline

Weekly Construction Progress Report – Final Report

Case #: PU-11-683
Project: Stateline to Riverview 10" NGL Pipeline
Week Ending: September 22, 2012

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Blayne Lyman	ONEOK	580 395-6309	580 761-3307
Construction Mgr	Tony Warner	ONEOK	N/A	580 741-0115
Contractor Spread 1	Torsten Leines	Alpha Oil & Gas	701 842-2855	612 916-8417
Contractor Spread 2	Scott Lawson	Frontier Services	406-670-1319	406-698-5047

Brief Description of Week's Activities
 Construction is complete. Fence repair & restoration work continued. Site painting & fencing are scheduled.


PROGRESS REPORT

Progress as of:	Week Ending	
	Sep 15	Sep 22
Mowing	100%	100%
Tot. Ft.	290910	290910
New Ft.		0
R.O.W.	100%	100%
Tot. Ft.	290910	290910
New Ft.		0
Pipe Strung	100%	100%
Tot. Ft.	290910	290910
New Ft.		0
U.T. Pipe	100%	100%
Tot. Ft.	290910	290910
New Ft.		0
Pipe Welded	100%	100%
Tot. Ft.	290910	290910
New Ft.		0
Coating	100%	100%
Tot. Ft.	290910	290910
New Ft.		0
Ditching	100%	100%
Tot. Ft.	290910	290910
New Ft.		0
Lowered	100%	100%
Tot. Ft.	290910	290910
New Ft.		0
Backfilled	100%	100%
Tot. Ft.	290910	290910
New Ft.		0
Cleanup	100%	100%
Tot. Ft.	290910	290910
New Ft.		0
Hydrotest	100%	100%
Tot. Ft.	290910	290910
New Ft.		0

Rain Days: 8
 Mud Days: 4
 Snow Days: 0
 Wind Out Days: 0
 Holidays: 5

Week Ending: 9/22/12

Footage:	290,910	Actual % Complete:	100%	Plan % Compl:	100%
Miles:	55.10	Spread:	Stateline NGL Pipeline	AFE:	255,111,6825.010000

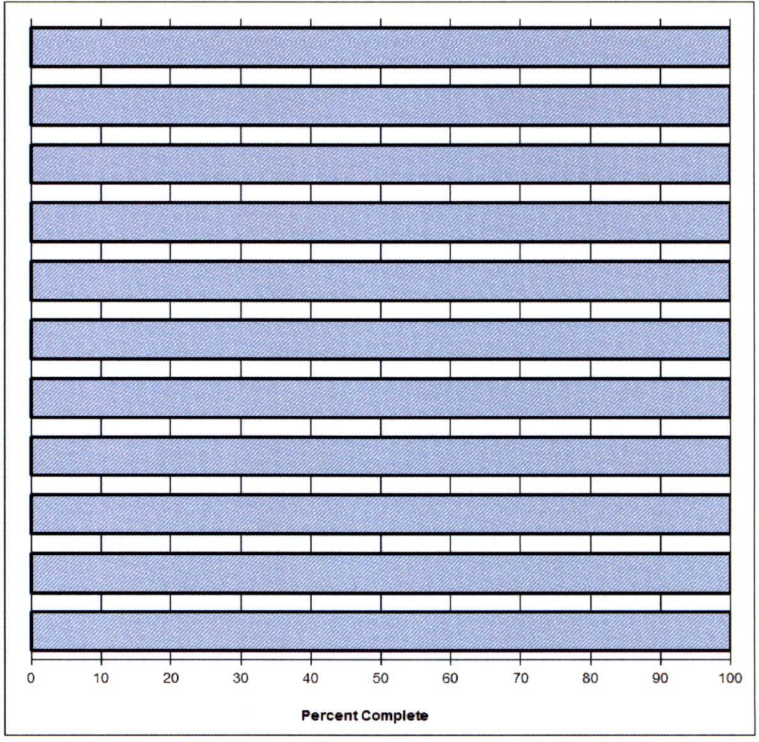

Contractor: Spread 1: Alpha Oil & Gas, Spread 2: Frontier Services

Completed through week ending 9/15	Completed in week ending 9/22
------------------------------------	-------------------------------

Project Site Safety
 Inspection continues to monitor project activities to ensure safety and quality expectations are met.

ONEOK Rockies Midstream Stateline NGL Pipeline

Comments

Signatory	Date
Blayne Lyman	9/27/2012
